

Tribhuvan University
Institute of Engineering, Pulchowk Campus
Department of Architecture and Urban Planning
M.Sc. Urban Planning 2025 to 2027



INTEGRATED URBAN DEVELOPMENT PLAN

Baglung Municipality 2026 to 2041

Planning Studio II

Submitted by Baglung Group

Advisor: Asst. Prof. Ajay Chandra Lal

August 2026 (Bhadra 2083 BS)

Data sources: NPHC 2011 and 2021, Baglung Municipality profile 2075 BS, municipal ward records, field surveys 2082 BS.

Document information

Table 0.1. Report metadata

Item	Detail
Report	Integrated Urban Development Plan (IUDP) of Baglung Municipality
Plan period	2026 to 2041 (fifteen years, three five-year phases)
Municipality	Baglung Municipality, Baglung District, Gandaki Province
Area	98.01 square kilometres
Wards	14
Population base	56,102 persons, Census 2021
Adopted projection	0.5 percent geometric growth per year
Prepared for	Department of Architecture, IOE Pulchowk Campus
Prepared by	Baglung Group, Planning Studio II
Advisor	Asst. Prof. Ajay Chandra Lal

Source: Baglung IUDP team.

Contents

Document information	2
Acronyms and abbreviations	17
Executive summary	18
The argument in one page	18
Key figures at a glance	18
Chapter synopses	19
1. Introduction	20
1.1 Purpose and scope	20
1.2 Legal and policy basis	21
1.3 Methodology	21
1.4 Data quality and honesty about gaps	23
2. Long term vision and goals	24
2.1 The vision	24
2.2 The goal and the objectives	24
2.3 Principles that bind the plan	24
2.4 From vision to sector plans	25
3. Municipal profile	25
3.1 Location and administration	25
3.2 Topography, climate and land	27
3.3 Demography	29
3.4 Economy and livelihoods	31
3.5 Infrastructure baseline	33
3.6 Social services baseline	35
3.7 Fiscal and institutional baseline	38
3.8 Environmental baseline and hazards	40
4. Analysis, projections and demand gaps	42
4.1 The four forces that shape the future	42
4.2 Population projection to 2041	42
4.3 Demand against DUDBC norms	43
Demand analysis and forecast	44
4.4 Land suitability	46
4.5 SWOT synthesis	47
4.6 Development concept	48
4.7 Ward level development potential and constraints	48

4.8 Baglung against national and regional norms.....	49
5. Thematic development plans.....	50
5. Physical Development Plan.....	50
5. Goal, objectives and strategy.....	50
5. Present condition and constraints	50
5. Problem analysis.....	52
5. Objective analysis.....	52
5. Alternative analysis	53
5. Plan and programmes	54
5. Logical framework	59
5. Assumptions and risk response	60
5. Implementation summary.....	61
5. Conclusion.....	61
5. Social Development Plan	62
5. Goal, objectives and strategy.....	62
5. Present condition and constraints	62
5. Problem analysis.....	63
5. Objective analysis.....	63
5. Alternative analysis	64
5. Plan and programmes	65
5. Logical framework	72
5. Assumptions and risk response	73
5. Implementation summary.....	75
5. Conclusion.....	75
5. Environmental Management Plan	76
5. Goal, objectives and strategy.....	76
5. Present condition and constraints	76
5. Problem analysis.....	77
5. Objective analysis.....	78
5. Alternative analysis	79
5. Plan and programmes	79
5. Logical framework	82
5. Assumptions and risk response	83
5. Implementation summary.....	84
5. Conclusion.....	84
5. Disaster Risk Reduction Plan	85

5. Goal, objectives and strategy	85
5. Present condition and constraints	85
5. Problem analysis.....	86
5. Objective analysis.....	86
5. Alternative analysis	87
5. Plan and programmes	88
5. Logical framework	89
5. Assumptions and risk response	90
5. Implementation summary	91
5. Conclusion.....	92
5. Tourism Development Plan.....	92
5. Goal, objectives and strategy	92
5. Present condition and constraints	92
5. Problem analysis.....	93
5. Objective analysis.....	94
5. Alternative analysis	95
5. Plan and programmes	95
5. Logical framework	104
5. Assumptions and risk response	106
5. Implementation summary	107
5. Conclusion.....	107
5. Economic Development Plan	108
5. Goal, objectives and strategy.....	108
5. Present condition and constraints	108
5. Problem analysis.....	109
5. Objective analysis.....	110
5. Alternative analysis	110
5. Plan and programmes	111
5. Logical framework	114
5. Assumptions and risk response	115
5. Implementation summary	117
5. Conclusion.....	117
5. Financial Development Plan.....	117
5. Goal, objectives and strategy.....	117
5. Present condition and constraints	118
5. Problem analysis.....	119

5. Objective analysis.....	120
5. Alternative analysis	120
5. Plan and programmes	121
5. Logical framework	122
5. Assumptions and risk response	124
5. Implementation summary	125
5. Conclusion.....	125
5. Institutional Development Plan	126
5. Goal, objectives and strategy	126
5. Present condition and constraints	126
5. Problem analysis.....	127
5. Objective analysis.....	127
5. Alternative analysis	128
5. Plan and programmes	129
5. Logical framework	130
5. Assumptions and risk response	131
5. Implementation summary	132
5. Conclusion.....	133
6. Multi Sector Investment Plan	133
6.1 The fifteen year programme	133
6.2 Funding sources.....	135
6.3 Phasing logic and the year one actions	135
7. Flagship projects.....	136
7. Kali Gandaki rafting corridor	136
7. Concept and site logic	136
7. Capital cost and revenue.....	137
7. Delivery and risks.....	137
7. Financial appraisal.....	138
7. Kali Gandaki gorge bungy	142
7. Concept and site logic	142
7. Capital cost and revenue.....	142
7. Delivery and risks.....	143
7. Financial appraisal.....	143
7. Panchakot cable car	147
7. Concept and site logic	147
7. Capital cost and revenue.....	147

7. Delivery and risks.....	148
7. Financial appraisal.....	148
8. Planning and building bylaws	152
8.1 Purpose and legal base	152
8.2 Zoning and density	152
8.3 Building rules	153
8.4 Enforcement and the building permit.....	153
8.5 Zoning standards by ward category.....	153
8.6 Heritage zone design guidelines.....	154
8.7 Tourism infrastructure standards.....	155
9. Implementation and monitoring	155
9.1 How the plan gets implemented	155
9.2 The annual scorecard.....	155
9.3 Roles.....	156
9.4 Data quality and the AI use note	157
9.5 Ward scorecard template	157
9.6 Data collection responsibility	157
10. Concluding remarks	158
11. References	159
Government and legal documents	159
Municipal and field sources.....	160
Sector and benchmark sources	160
Bibliography, works consulted beyond the cited references	160
12. Annexes	161
A.1 Ward road inventory from GIS analysis.....	161
A.2 DUDBC planning norms, condensed	161
A.3 Survey instruments used.....	162
A.4 Suitability model weights	163
A.5 Data quality matrix	163
A.6 Data and projection notes	164
Appendix B. Ward snapshots	164
Ward 1	164
Ward 2	165
Ward 3	165
Ward 4.....	165
Ward 5	166

Ward 6	166
Ward 7	167
Ward 8	167
Ward 9	167
Ward 10	168
Ward 11	168
Ward 12	168
Ward 13	169
Ward 14	169

List of Tables

Table 0.1. Report metadata	2
Table 0.2. Acronyms and abbreviations	17
Table 0.3. Baglung at a glance, 2021 base and 2036 outlook	18
Table 3.1. Ward level base data, Census 2021 and municipal profile	25
Table 3.2. Registered firms by sector, BCCI registry	32
Table 3.3. Ward wise occupation structure, EDP sheet	33
Table 3.4. Ward wise health facility inventory, SDP sheet	37
Table 3.5. Ward wise institutional capacity, IDP sheet	38
Table 4.1. Adopted population path, 2026 to 2041	42
Table 4.2. Physical infrastructure gaps against norms	43
Table 4.3. Social infrastructure gaps against norms	44
Table 4.4. Physical infrastructure demand analysis and forecast	45
Table 4.5. Social infrastructure demand analysis and forecast	45
Table 4.6. Economic infrastructure demand analysis and forecast	45
Table 4.7. Cross sector SWOT synthesis	47
Table 4.8. Cross sector opportunities and threats	47
Table 4.9. Ward level development potential and constraints	48
Table 4.10. Baglung vs national and regional benchmarks	49
Table 5.1. SWOT analysis, Physical Development Plan	50
Table 5.2. Community proposals register, Physical Development Plan	51
Table 5.3. Alternative options scored against five criteria, Physical Development Plan	53
Table 5.4. Road programme at unit rates	54
Table 5.5. Ward road priority classification	55

Table 5.6. Storm drain programme by section	55
Table 5.7. Water supply programme at unit rates	56
Table 5.8. Ward wise water demand at 120 lpcd, 2036 projection	57
Table 5.9. Sanitation and waste programme at unit rates	58
Table 5.10. Housing programme.....	58
Table 5.11. Logframe matrix (LFM), Physical Development Plan	59
Table 5.12. Risk register, Physical Development Plan	60
Table 5.13. Implementation summary, Physical Development Plan	61
Table 5.14. SWOT analysis, Social Development Plan	62
Table 5.15. Alternative options scored against five criteria, Social Development Plan	64
Table 5.16. Ward wise school consolidation plan	65
Table 5.17. Education programme.....	66
Table 5.18. Community proposals register, education and youth.....	66
Table 5.19. Ward wise health staffing and birthing centre gap	67
Table 5.20. Community proposals register, health.....	68
Table 5.21. Health programme.....	68
Table 5.22. Child protection programme	70
Table 5.23. Ageing, disability and GESI programme	70
Table 5.24. Community proposals register, GESI, sports and inclusion.....	71
Table 5.25. Logframe matrix (LFM), Social Development Plan	72
Table 5.26. Risk register, Social Development Plan	74
Table 5.27. Implementation summary, Social Development Plan	75
Table 5.28. SWOT analysis, Environmental Management Plan	76
Table 5.29. Community proposals register, environment.....	77
Table 5.30. Alternative options scored against five criteria, Environmental Management Plan	79
Table 5.31. Solid waste programme.....	79
Table 5.32. Ward wise waste generation and collection status.....	80
Table 5.33. Forest estate by type and ward.....	81
Table 5.34. Forest, water quality and climate programme.....	81
Table 5.35. Logframe matrix (LFM), Environmental Management Plan.....	82
Table 5.36. Risk register, Environmental Management Plan.....	83
Table 5.37. Implementation summary, Environmental Management Plan	84
Table 5.38. SWOT analysis, Disaster Risk Reduction Plan.....	85
Table 5.39. Alternative options scored against five criteria, Disaster Risk Reduction Plan.....	87
Table 5.40. Ward wise hazard exposure matrix	88
Table 5.41. Disaster risk reduction programme	88

Table 5.42. Logframe matrix (LFM), Disaster Risk Reduction Plan	89
Table 5.43. Risk register, Disaster Risk Reduction Plan	90
Table 5.44. Implementation summary, Disaster Risk Reduction Plan	91
Table 5.45. SWOT analysis, Tourism Development Plan	92
Table 5.46. Community proposals register, tourism and culture	93
Table 5.47. Alternative options scored against five criteria, Tourism Development Plan.....	95
Table 5.48. Visitor flow and revenue projection by product	102
Table 5.49. Heritage and cultural site inventory	102
Table 5.50. Tourism programme cost summary.....	103
Table 5.51. Logframe matrix (LFM), Tourism Development Plan.....	104
Table 5.52. Risk register, Tourism Development Plan.....	106
Table 5.53. Implementation summary, Tourism Development Plan	107
Table 5.54. SWOT analysis, Economic Development Plan.....	108
Table 5.55. Community proposals register, economic	109
Table 5.56. Alternative options scored against five criteria, Economic Development Plan.....	111
Table 5.57. Agro processing value chain by product	112
Table 5.58. Economic programme cost summary	113
Table 5.59. Logframe matrix (LFM), Economic Development Plan	114
Table 5.60. Risk register, Economic Development Plan	116
Table 5.61. Implementation summary, Economic Development Plan	117
Table 5.62. SWOT analysis, Financial Development Plan.....	118
Table 5.63. Alternative options scored against five criteria, Financial Development Plan	120
Table 5.64. Own source revenue path, 2026 to 2031	121
Table 5.65. Logframe matrix (LFM), Financial Development Plan	122
Table 5.66. Risk register, Financial Development Plan	124
Table 5.67. Implementation summary, Financial Development Plan.....	125
Table 5.68. SWOT analysis, Institutional Development Plan.....	126
Table 5.69. Alternative options scored against five criteria, Institutional Development Plan ...	128
Table 5.70. Ward wise staffing gap and e governance readiness	129
Table 5.71. Institutional programme	130
Table 5.72. Logframe matrix (LFM), Institutional Development Plan	130
Table 5.73. Risk register, Institutional Development Plan	131
Table 5.74. Implementation summary, Institutional Development Plan.....	132
Table 6.1. MSIP summary by sector, NPR crore	133
Table 6.2. Funding composition of the MSIP.....	135
Table 7.1. Rafting corridor capital cost.....	137

Table 7.2. Rafting corridor financing structure	138
Table 7.3. Rafting corridor staffing schedule	138
Table 7.4. Rafting corridor revenue basis	138
Table 7.5. Rafting corridor working capital	139
Table 7.6. Rafting corridor income statement, ten years.....	139
Table 7.7. Rafting corridor cash flow projection, ten years	139
Table 7.8. Rafting corridor loan amortisation	139
Table 7.9. Rafting corridor break-even.....	140
Table 7.10. Rafting corridor weighted average cost of capital.....	140
Table 7.11. Rafting corridor returns summary	140
Table 7.12. Rafting corridor net present value at 12 percent.....	141
Table 7.13. Rafting corridor sensitivity analysis	141
Table 7.14. Bungy capital cost.....	142
Table 7.15. Bungy financing structure	143
Table 7.16. Bungy staffing schedule.....	143
Table 7.17. Bungy revenue basis	143
Table 7.18. Bungy working capital	144
Table 7.19. Bungy income statement, ten years.....	144
Table 7.20. Bungy cash flow projection, ten years	144
Table 7.21. Bungy loan amortisation	145
Table 7.22. Bungy break-even.....	145
Table 7.23. Bungy weighted average cost of capital	145
Table 7.24. Bungy returns summary	146
Table 7.25. Bungy net present value at 12 percent.....	146
Table 7.26. Bungy sensitivity analysis.....	146
Table 7.27. Cable car capital cost.....	147
Table 7.28. Cable car financing structure	148
Table 7.29. Cable car staffing schedule	148
Table 7.30. Cable car revenue basis.....	149
Table 7.31. Cable car working capital.....	149
Table 7.32. Cable car income statement, ten years.....	149
Table 7.33. Cable car cash flow projection, ten years	149
Table 7.34. Cable car loan amortisation.....	150
Table 7.35. Cable car break-even.....	150
Table 7.36. Cable car weighted average cost of capital.....	151
Table 7.37. Cable car returns summary	151

Table 7.38. Cable car net present value at 12 percent.....	151
Table 7.39. Cable car sensitivity analysis	152
Table 8.1. Proposed zoning districts	152
Table 8.2. Detailed zoning standards by ward.....	153
Table 8.3. Heritage zone design standards.....	154
Table 8.4. Tourism infrastructure minimum standards	155
Table 9.1. The monitoring scorecard.....	155
Table 9.2. Who does what	156
Table 9.3. Ward scorecard template (illustrative, Ward 2 shown).....	157
Table 9.4. Data collection and reporting matrix.....	157
Table 12.1. Table A.1. Ward wise road length by surface type, GIS analysis	161
Table 12.2. Table A.2. Selected DUDBC planning norms used in this plan.....	162
Table 12.3. Table A.3. Survey instruments and their application.....	162
Table 12.4. Table A.4. Suitability factor weights.....	163
Table 12.5. Table A.5. Data quality by workbook sheet	163
Table 12.6. Table A.6. Data sources and projection methods	164
Table B.1. Ward 1 profile	164
Table B.2. Ward 2 profile	165
Table B.3. Ward 3 profile	165
Table B.4. Ward 4 profile	165
Table B.5. Ward 5 profile	166
Table B.6. Ward 6 profile	166
Table B.7. Ward 7 profile	167
Table B.8. Ward 8 profile	167
Table B.9. Ward 9 profile	167
Table B.10. Ward 10 profile	168
Table B.11. Ward 11 profile	168
Table B.12. Ward 12 profile	168
Table B.13. Ward 13 profile	169
Table B.14. Ward 14 profile	169

List of Figures

Figure 1.1. <i>Baglung bazaar plateau above the Kali Gandaki gorge, the urban core of the municipality. Photo: Wikimedia Commons, (c) Bksthapa, CC BY-SA 4.0, 2026.</i>	20
--	----

Figure 1.2. <i>Key informant interview in session, note taking on the discussion. Photo: Baglung Group field team, 2082 BS.</i>	22
Figure 1.3. <i>Baglung Municipality in the Dhaulagiri region.</i>	23
Figure 3.1. <i>Population by ward, 2021. The bazaar core carries the density.</i>	26
Figure 3.2. <i>Ward map of Baglung Municipality with ward boundaries and labels.</i>	27
Figure 3.3. <i>Topography of Baglung Municipality. The gorge cuts the eastern edge.</i>	27
Figure 3.4. <i>Slope aspect map. The buildable plateau and the steep hill wards stand apart.</i>	28
Figure 3.5. <i>Mean temperature surface for Baglung Municipality from WorldClim.</i>	28
Figure 3.6. <i>Land cover 2021. Forest dominates the hill wards, built up stays in the core.</i>	28
Figure 3.7. <i>Population and households, 2011 to 2021, with the projection path.</i>	29
Figure 3.8. <i>Age sex pyramid, 2021. The waist in the working ages shows male migration.</i>	30
Figure 3.9. <i>Dependency ratios, 2021 to 2036. Old age dependency nearly doubles.</i>	30
Figure 3.10. <i>Ward level population change 2011 to 2021. The core grew, the hills fell.</i>	31
Figure 3.11. <i>Occupation structure. Two economies coexist in one municipality.</i>	31
Figure 3.12. <i>Agricultural plantation areas by ward.</i>	32
Figure 3.13. <i>Livestock holdings by ward from the field survey.</i>	32
Figure 3.14. <i>Road network and hierarchy. The Mid-Hill and the Kali Gandaki corridor are the spines.</i>	34
Figure 3.15. <i>Electricity grid and transmission lines across the municipality.</i>	34
Figure 3.16. <i>Schools and health facilities with the service linkage. The core is dense, the hills are thin.</i>	35
Figure 3.17. <i>Hospital service coverage, one kilometre buffer.</i>	36
Figure 3.18. <i>School service coverage, buffer radius analysis.</i>	36
Figure 3.19. <i>Urban Health Promotion Centre in Ward 2, serving the core population. Photo: Baglung Group field team, 2082 BS.</i>	37
Figure 3.20. <i>Baglung Municipal Office staff, the institutional base for the TDF debt and ward allocations. Photo: Baglung Group field team, 2082 BS.</i>	39
Figure 3.21. <i>Ward offices and the administrative network of the municipality.</i>	39
Figure 3.22. <i>Modelled flood hazard. The river line and the bazaar runoff zones show highest exposure.</i>	40
Figure 3.23. <i>Modelled landslide susceptibility. The corridor and steep hill wards dominate.</i>	40
Figure 3.24. <i>Fault lines with risk buffers from the geological data of the region.</i>	41
Figure 3.25. <i>FY 2083/84 approved budget revenue composition. Federal grants dominate at 68 percent, with own source at 15.7 percent.</i>	41
Figure 4.1. <i>Projection scenarios. Even the high path stays below the 2011 population.</i>	43
Figure 4.2. <i>Service and demographic gaps against planning norms. Internet access, sex ratio and average household size show the largest gaps.</i>	44
Figure 4.3. <i>Land suitability for development from the multi criteria model.</i>	46

Figure 4.4. <i>Fault lines and risk buffers, the seismic constraint on new development.</i>	47
Figure 4.5. <i>Proposed development concept 2026 to 2041. The plan concentrates investment in the core and the corridor.</i>	48
Figure 5.1. <i>Problem analysis tree, Physical Development Plan. Baglung IUDP team, 2082 BS.</i>	52
Figure 5.2. <i>Objective analysis tree, Physical Development Plan. Baglung IUDP team, 2082 BS.</i>	53
Figure 5.3. <i>Alternative analysis heat grid, Physical Development Plan. Baglung IUDP team, 2082 BS.</i>	54
Figure 5.4. <i>Drainage and water resources model of the municipality.</i>	57
Figure 5.5. <i>Assumptions and risks response matrix, Physical Development Plan. Baglung IUDP team, 2082 BS.</i>	60
Figure 5.6. <i>Problem analysis tree, Social Development Plan. Baglung IUDP team, 2082 BS.</i>	63
Figure 5.7. <i>Objective analysis tree, Social Development Plan. Baglung IUDP team, 2082 BS.</i>	64
Figure 5.8. <i>Alternative analysis heat grid, Social Development Plan. Baglung IUDP team, 2082 BS.</i>	65
Figure 5.9. <i>Health post patient room with beds, the ward level service base. Photo: Baglung Group field team, 2082 BS.</i>	69
Figure 5.10. <i>Field team at the Dhaulagiri Ayurved Hospital, the facility whose staffing crisis the health programme addresses. Photo: Baglung Group field team, 2082 BS.</i>	69
Figure 5.11. <i>Field team with the District Police Office, the partner for road safety and crime data. Photo: Baglung Group field team, 2082 BS.</i>	72
Figure 5.12. <i>Assumptions and risks response matrix, Social Development Plan. Baglung IUDP team, 2082 BS.</i>	74
Figure 5.13. <i>Problem analysis tree, Environmental Management Plan. Baglung IUDP team, 2082 BS.</i>	78
Figure 5.14. <i>Objective analysis tree, Environmental Management Plan. Baglung IUDP team, 2082 BS.</i>	78
Figure 5.15. <i>Alternative analysis heat grid, Environmental Management Plan. Baglung IUDP team, 2082 BS.</i>	79
Figure 5.16. <i>Solid waste collection and transit route across the wards.</i>	80
Figure 5.17. <i>Assumptions and risks response matrix, Environmental Management Plan. Baglung IUDP team, 2082 BS.</i>	83
Figure 5.18. <i>Problem analysis tree, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.</i> ..	86
Figure 5.19. <i>Objective analysis tree, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.</i> .	87
Figure 5.20. <i>Alternative analysis heat grid, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.</i>	88
Figure 5.21. <i>Assumptions and risks response matrix, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.</i>	90
Figure 5.22. <i>Problem analysis tree, Tourism Development Plan. Baglung IUDP team, 2082 BS.</i>	94
Figure 5.23. <i>Objective analysis tree, Tourism Development Plan. Baglung IUDP team, 2082 BS.</i>	94

Figure 5.24. <i>Alternative analysis heat grid, Tourism Development Plan. Baglung IUDP team, 2082 BS.</i>	95
Figure 5.25. <i>Existing tourism visitor demand by site. Panchakot dominates with 5,000 to 7,000 visitors a day in season.</i>	96
Figure 5.26. <i>The Gandaki gorge and the bungy anchor site near Kushma, visible from the Baglung side. Photo: Wikimedia Commons, CC BY-SA 4.0, 2026.</i>	96
Figure 5.27. <i>Tourism trail route and the attractions it links.</i>	97
Figure 5.28. <i>Service and hospitality establishments across the wards.</i>	97
Figure 5.29. <i>Ward 2 campus area, the ridge access corridor for the proposed cable car alignment. Photo: Baglung Group field team, 2082 BS.</i>	99
Figure 5.30. <i>Kalika Bhagawati Temple in Ward 1, the heritage precinct anchor. Photo: Baglung Municipality, used with permission, 2026.</i>	100
Figure 5.31. <i>Two tier brick shrine with festive flags, a node of the proposed heritage circuit. Photo: Baglung Group field team, 2082 BS.</i>	100
Figure 5.32. <i>Focus group discussion with community members on the homestay and eco-tourism circuit. Photo: Baglung Group field team, 2082 BS.</i>	101
Figure 5.33. <i>Farm economy visit in Ward 6, the agro-tourism and orange belt. Photo: Baglung Group field team, 2082 BS.</i>	101
Figure 5.34. <i>Temple facade with brick ornaments and prayer flags, the craftsmanship the heritage zone guidelines of Chapter 8 protect. Photo: Baglung Group field team, 2082 BS.</i>	103
Figure 5.35. <i>Tourism programme capital by product. The cable car dominates at NPR 70 crore, with the bridge hub at NPR 40 crore.</i>	104
Figure 5.36. <i>Flagship project revenue projections at build-out. The municipal take is the royalty, not the gross revenue. Planning accuracy plus or minus 30 percent.</i>	105
Figure 5.37. <i>Assumptions and risks response matrix, Tourism Development Plan. Baglung IUDP team, 2082 BS.</i>	106
Figure 5.38. <i>Problem analysis tree, Economic Development Plan. Baglung IUDP team, 2082 BS.</i> ..	110
Figure 5.39. <i>Objective analysis tree, Economic Development Plan. Baglung IUDP team, 2082 BS.</i> ..	110
Figure 5.40. <i>Alternative analysis heat grid, Economic Development Plan. Baglung IUDP team, 2082 BS.</i>	111
Figure 5.41. <i>Livestock shed and farm house cattle, the buffalo line that feeds the proposed dairy cluster. Photo: Baglung Group field team, 2082 BS.</i>	112
Figure 5.42. <i>Farm machine, rice thresher, the mechanisation gap the processing clusters and MSME line address. Photo: Baglung Group field team, 2082 BS.</i>	113
Figure 5.43. <i>Fish pond with protective netting, the aquaculture line that produced 39,600 kilograms last year. Photo: Baglung Group field team, 2082 BS.</i>	114
Figure 5.44. <i>Assumptions and risks response matrix, Economic Development Plan. Baglung IUDP team, 2082 BS.</i>	116
Figure 5.45. <i>Year-on-year revenue change, FY 2082/83 to 2083/84. Federal grants fell 14.5 percent while own source rose 21.7 percent.</i>	119

Figure 5.46. <i>Problem analysis tree, Financial Development Plan. Baglung IUDP team, 2082 BS.</i>	119
Figure 5.47. <i>Objective analysis tree, Financial Development Plan. Baglung IUDP team, 2082 BS.</i>	120
Figure 5.48. <i>Alternative analysis heat grid, Financial Development Plan. Baglung IUDP team, 2082 BS.</i>	121
Figure 5.49. <i>Own-source revenue slope from FY 2083/84 to 2031 target. Tourism royalties are the new line, growing from zero to NPR 4 crore.</i>	122
Figure 5.50. <i>Municipal fiscal autonomy trajectory from 23.6 to 29.2 to the 40 percent target by 2031.</i>	123
Figure 5.51. <i>Assumptions and risks response matrix, Financial Development Plan. Baglung IUDP team, 2082 BS.</i>	124
Figure 5.52. <i>Problem analysis tree, Institutional Development Plan. Baglung IUDP team, 2082 BS.</i>	127
Figure 5.53. <i>Objective analysis tree, Institutional Development Plan. Baglung IUDP team, 2082 BS.</i>	128
Figure 5.54. <i>Alternative analysis heat grid, Institutional Development Plan. Baglung IUDP team, 2082 BS.</i>	129
Figure 5.55. <i>Assumptions and risks response matrix, Institutional Development Plan. Baglung IUDP team, 2082 BS.</i>	131
Figure 6.1. <i>MSIP 15-year total by sector. Physical infrastructure dominates at 53 percent, followed by tourism at 23 percent.</i>	134
Figure 6.2. <i>MSIP phasing by sector across three phases. Phase I is the action phase at NPR 431.3 crore.</i>	134
Figure 6.3. <i>MSIP funding composition. Federal and provincial transfers cover 55 percent, municipal own funds 25 percent, private and PPP 17 percent.</i>	135
Figure 7.1. <i>The Kali Gandaki gorge from the bazaar plateau, the river corridor for the rafting product. Photo: Wikimedia Commons, (c) Michal Salaban, CC BY-SA 2.5, 2026.</i>	136

Acronyms and abbreviations

Table 0.2. Acronyms and abbreviations

Acronym	Full form
ADB	Asian Development Bank
BCCI	Baglung Chamber of Commerce and Industry
CBS	Central Bureau of Statistics
DRRM	Disaster Risk Reduction and Management
DUDBC	Department of Urban Development and Building Construction
EDP	Economic Development Plan
EnDP	Environmental Development Plan
FDP	Financial Development Plan
GESI	Gender Equality and Social Inclusion
IDP	Institutional Development Plan
IUDP	Integrated Urban Development Plan
LGO	Local Government Operation Act 2074
MSIP	Multi Sector Investment Plan
NPHC	National Population and Housing Census
NPR	Nepali rupees
NSO	National Statistics Office
NUDS	National Urban Development Strategy
PDP	Physical Development Plan
PPP	Public private partnership
SDP	Social Development Plan
TDF	Town Development Fund
TPD	Tonnes per day

Source: Baglung IUDP team.

Executive summary

The argument in one page

Baglung sits at 1,020 metres above sea level on a plateau above the Kali Gandaki gorge, where the Mid-Hill Highway and the Kali Gandaki corridor cross. The municipality is the district headquarters of Baglung District and the trade and health town for the Dhaulagiri region. Between 2011 and 2021 the population fell from 57,823 to 56,102 while households rose from 15,182 to 15,924. The town is shrinking in people and growing in homes, ageing faster than the nation, and losing its young adults to foreign employment.

The plan responds with one core idea. Baglung should stop managing decline ward by ward and instead concentrate public investment where the growth already is, on the bazaar core, the highway corridor and the river. The bazaar wards hold 53 percent of the population on 16 percent of the land. The corridor wards 4, 13 and 14 hold the road access, the flat land and the future. Everything else in the plan hangs off that geography.

Three flagship projects carry the tourism economy. The Kali Gandaki rafting corridor from Balewa to Ramrekha turns the river into a revenue asset. A bungee jump on the gorge cliffs adds the adventure anchor that Kushma already proved across the river. A cable car to the Panchakot ridge, which already draws 5,000 to 7,000 visitors a day in season, connects that demand to the bazaar. Together the three projects are screened at about NPR 103 crore of capital cost, most of it private and PPP capital, with a combined build out municipal revenue of roughly NPR 1.5 to 2.0 crore a year, before the ridge trade and the park taxes.

The rest of the plan is quieter but equally important. Flood control for the bazaar, drinking water for the 11.3 percent of households still off the tap, a sewerage network where none exists, solid waste collection for the eight wards that have none, schools consolidated for a shrinking child cohort, geriatric care for a 60 plus share heading toward 20 percent, and a revenue reform that lifts internal revenue and revenue sharing autonomy from 29.2 percent of the budget toward 40 percent by 2031.

The total fifteen year investment programme is estimated at about NPR 1,040 crore at planning stage unit rates, of which municipal own funds cover about 25 percent, federal and provincial transfers about 55 percent, private and PPP capital about 17 percent and development partners about 3 percent. The phasing is honest. The first phase 2026 to 2031 does the flood control, the water and sewerage works, the ward road upgrades and the rafting and bungee investments. The second phase adds the cable car, the agro processing clusters and the heritage circuit. The third phase completes the district level facilities and the institutional upgrades.

Key figures at a glance

Table 0.3. Baglung at a glance, 2021 base and 2036 outlook

Indicator	2021	2036 outlook
Population	56,102	58,087 at adopted 0.5 percent growth
Households	15,924	about 16,600 to 17,100
Average household size	3.52	about 3.4
Sex ratio	86.9 males per 100 females	rising slowly
Literacy	83.5 percent	target 90 percent

Aged 60 plus	13.2 percent	about 20 percent
Female headed households	46.4 percent	persisting with ageing
Tap water coverage	88.7 percent	target 98 percent
Grid electricity	98.6 percent	100 percent
Schools carrying students	89 schools, 13,098 students	fewer students, consolidated schools
Internal revenue autonomy	29.2 percent	target 40 percent
Waste collected formally	6 of 14 wards	all 14 wards

Source: NPHC 2021, Baglung IUDP team analysis.

Chapter synopses

Chapter 1 states the purpose, the legal basis, the method and the data quality of the plan. Chapter 2 sets the long term vision, the goal and the six objectives that every budget line must serve. Chapter 3 profiles the municipality ward by ward, with the demographic, economic, infrastructure, social, fiscal and hazard baselines. Chapter 4 carries the analysis, the population projection, the demand gaps against the DUDBC norms, the land suitability model and the cross sector synthesis. Chapter 5 holds the eight thematic plans. Each plan follows one discipline, from goal and strategy through problem, objective and alternative analysis to the programme, the logical framework, the risk response and the phased cost. Chapter 6 assembles the Multi Sector Investment Plan with phasing and funding sources. Chapter 7 develops the three flagship projects to sub project level with full financial appraisal. Chapter 8 drafts the planning and building bylaws. Chapter 9 sets the monitoring scorecard, the review rhythm and the data responsibilities. Concluding remarks close the report, and the annexes carry the ward tables and the survey instruments.

Every figure and table carries a source line. Where the team could not verify a number, the text says so openly. The full ward tables and the survey instruments are in the annex.

1. Introduction

1.1 Purpose and scope



Figure 1.1. Baglung bazaar plateau above the Kali Gandaki gorge, the urban core of the municipality. Photo: Wikimedia Commons, (c) Bksthapa, CC BY-SA 4.0, 2026.

This document is the Integrated Urban Development Plan of Baglung Municipality for the period 2026 to 2041. An IUDP is the statutory long term plan of a local government in Nepal. It sets the vision, the sector strategies and the investment programme that guide the annual budget and the ward level projects. The Guidelines for Preparation of Integrated Urban Development Plan, prepared for DUDBC under ADB TA-9384, describe the IUDP as the comprehensive and integrated plan that binds the

physical, social, economic, environmental, financial and institutional sectors into one frame (DUDBC and ADB, 2019).

The scope covers all fourteen wards and the full 98.01 square kilometres of the municipality. The plan period is fifteen years, split into three five year phases that match the local government planning cycle. The first phase 2026 to 2031 is the action phase. The second and third phases carry the longer investments in tourism, the district facilities and the institutional upgrades.

Three audiences matter. The municipal assembly uses this plan to make budget decisions. The ward offices use it to align their own priorities with the corridor level investments. The private sector and the development partners use it to see where the municipality intends to spend, where it wants partners and what it will protect.

1.2 Legal and policy basis

- Constitution of Nepal, 2015. Schedule 8 lists local level planning among the exclusive powers of the municipality.
- Local Government Operation Act 2074 (2017). Section 43 requires the local government to prepare a long term plan and links the annual budget to it. Section 24 sets the GESI duty.
- National Urban Development Strategy 2017 (NUDS). It directs municipalities to prepare integrated plans and to manage urban growth with evidence.
- Fifteenth Plan of the National Planning Commission. It sets the national targets on literacy, inclusion and urban services.
- DUDBC Planning Norms and Standards 2013. This plan uses its norms for schools, health posts, parks, roads and water supply.
- Disaster Risk Reduction and Management Act 2074. It obliges the municipality to plan for hazards and to maintain response capacity.
- Environment Protection Act 2076 and the local building code regime. These govern the environmental assessment of the projects in Chapter 7.

Citation note. The norms cited throughout this plan follow DUDBC (2013). Where the team used an international norm, the source is named in the table itself.

1.3 Methodology

The plan was built in eight steps, each with a named output.

1. Stakeholder analysis. The team mapped the municipal officials, ward representatives, community leaders, business owners and farmers who hold the knowledge the plan needs.
2. Reconnaissance and field survey. All fourteen wards were visited in 2082 BS. Agricultural land, hazard sites, tourism points and infrastructure were photographed, measured and noted ward by ward.
3. Key informant interviews. Semi structured interviews were held with elected representatives, municipal section heads, the district police, hospital management, the Chamber of Commerce and community leaders.
4. Focus group discussions. Groups of women, farmers, traders and youth met in the bazaar wards and in the hills. Their minutes feed the social and economic chapters directly. The handwritten discussion notes were transcribed and are carried through the report as community proposals registers inside each sector plan, with a plan response for every proposal.

5. Secondary data assembly. Census 2011 and 2021 ward tables, the municipal profile 2075, the ward records, the budget red book and the Chamber registry were compiled into a single workbook (Baglung IUDP team, 2082 BS).
6. GIS analysis. DEM, slope, land cover, flood and landslide rasters and the road, building, health and school layers were analysed in QGIS. The maps in this report come from that database.
7. Sector analysis. For each sector the team ran trend analysis, norms based gap analysis and the problem, objective and alternative analysis chain, following the DUDBC IUDP guideline and the logical framework approach.
8. Plan preparation. Each thematic plan was drafted from its analysis chain with programmes at unit rates, a logical framework, a risk register and a phased cost, and the three flagship projects received a full financial appraisal.



Figure 1.2. Key informant interview in session, note taking on the discussion. Photo: Baglung Group field team, 2082 BS.

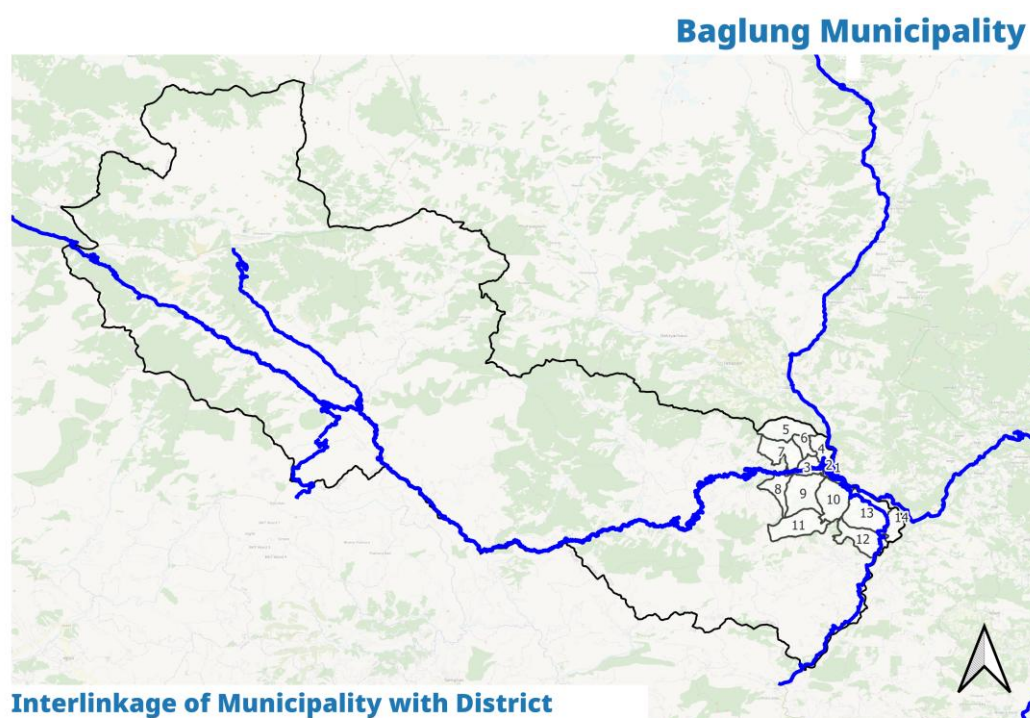


Figure 1.3. Baglung Municipality in the Dhaulagiri region.

The outputs of the method are this report and its working products, the municipal profile with the GIS database, the eight thematic plans with their logical frameworks, the Multi Sector Investment Plan, the three flagship project appraisals, the draft planning and building bylaws and the monitoring scorecard.

1.4 Data quality and honesty about gaps

The plan is only as good as its numbers, so the team has been deliberate about what it could and could not verify. Population, households, literacy, age structure and migration come from the censuses and are solid. Ward level service inventories, school tables and health post lists come from field survey and are good. Road kilometres per ward come from the GIS and are good for the surfaced network.

Some numbers are thinner. The tourism visitor counts are estimates given by key informants and site managers, not counters. The waste generation figure of 18 tonnes per day is an extrapolation from collection records and the municipal estimate. The financial figures are taken from the approved budget of FY 2083/84 and the audit trail of the year before. The team notes that the Detailed Project Reports for the flagship tourism projects and the full Investment Development Plan for the municipality are empty or incomplete, which means the costs and phasing in this plan are at a plus or minus 30 percent planning accuracy and will need detailed DPR work before commitment. Where a number is an estimate, the text says so.

Rule of the plan. Every gap table states a norm, a present condition and the difference. If the team could not verify a figure, the row says estimate and the source line says field survey 2082 BS.

2. Long term vision and goals

2.1 The vision

The vision was drafted with the municipal officials during the profile phase and tested in the focus groups. It is deliberately short, in Nepali first because that is the working language of the municipality, with the English reading beside it.

Vision (dighargakalin soch) “मध्यपहाडी व्यापारिक तथा पर्यटकीय शहर, सुन्दर, समृद्ध, सांस्कृतिक बागलुङ्ग नगर”

A mid hill commercial and touristic city, a beautiful, prosperous and cultural Baglung. By 2036 the municipality is realised as a flood resilient, well connected gateway city of the Dhaulagiri region, anchored in trade, health, education and tourism, where every ward from the dense Ward 2 bazaar to the highlands of Wards 9 and 11 shares a dignified quality of life.

The vision is grounded in three facts the evidence supports. First, the Mid-Hill Highway and the Kali Gandaki corridor already cross the municipality, so the gateway role is not an aspiration but a location. Second, Ward 2 alone holds 543 of the 1,219 registered firms, 44.5 percent, and serves as the trade hub for Myagdi, Parbat and Mustang (BCCI registry, 2082 BS). Third, the tourism assets already draw visitors, with Panchakot alone counting 5,000 to 7,000 visitors per day in season (field survey, 2082 BS).

2.2 The goal and the objectives

The goal translates the vision into one sentence the budget can serve.

Goal (mul lakshya). To build the foundation of a physically and economically advanced, socially inclusive, environmentally balanced and disaster and climate resilient municipality.

Six objectives carry the goal into action. Each objective is measured by the indicators in Chapter 9.

9. Achieve durable, all weather physical connectivity to every ward and permanently resolve the recurring flood hazard of Baglung Bazaar.
10. Diversify the local economy beyond retail trade through agro processing and heritage and adventure tourism.
11. Raise internal revenue and shared revenue autonomy from the current 29.2 percent toward long term fiscal self reliance.
12. Strengthen health, education and social inclusion services so that quality does not depend on which ward a resident lives in.
13. Complete the zero waste system and reverse net forest loss in the urbanising core.
14. Build in house institutional and technical capacity in GIS and urban planning so that flagship projects are municipally led and not externally dependent.

The objectives are deliberately few. A long list would dilute the budget the same way the tukra yojana parcels dilute the capital. These six are the tests the annual budget will be read against.

2.3 Principles that bind the plan

- Evidence first. Every recommendation carries a data line and a source. The plan does not propose what it cannot defend with a number.
- Spatial concentration. Investment follows the growth that exists, the bazaar core, the corridor wards and the river, instead of spreading thin across fourteen wards.

- GESI as a duty. Section 24 of the Local Government Operation Act 2074 makes gender equality and social inclusion a legal obligation. The plan reads every project through the lens of the 46.4 percent female headed households and the ageing wards.
- Climate and disaster proofing. Every physical project in Chapter 5 is screened against the flood and landslide rasters in Chapter 4.
- Fiscal honesty. The MSIP in Chapter 6 only commits what the municipality can fund or realistically mobilise from partners.

2.4 From vision to sector plans

Chapter 5 turns the six objectives into eight thematic plans. Each thematic plan states the present condition, the norm, the gap, the strategic priority, the programmes with unit rate costs and a logical framework. The logical framework follows the format used in the Siddharthanagar IUDP 2020 to 2035, with goal, objective, result, indicators, means of verification, assumptions, activities and cost (Siddharthanagar Municipality, 2020). The monitoring chapter then closes the loop with the scorecard.

3. Municipal profile

3.1 Location and administration

Baglung Municipality lies in the middle hills of Gandaki Province, on a plateau at about 1,020 metres above the Kali Gandaki gorge. The Mid-Hill Highway crosses it east to west and the Kali Gandaki corridor runs north to south, which makes the bazaar a natural stop between Pokhara, Mustang and the Dhaulagiri valleys (Baglung Municipality profile, 2075 BS). The municipality borders Parbat District and the Kali Gandaki to the east, Myagdi to the north, Kathekhola Rural Municipality to the west and Jaimini Municipality to the south.

Administratively the municipality runs fourteen wards. Ward 2 is the administrative and commercial core, holding the municipal office, the bazaar and the bus park. Wards 5 to 12 are the hill and agricultural wards. Wards 13 and 14 form the Balewa and Narayansthan area along the southern highway corridor.

Table 3.1. Ward level base data, Census 2021 and municipal profile

Ward	Households	Population	Male	Area (sq km)
1	1,361	4,746	2,275	1.39
2	2,216	7,318	3,486	0.72
3	2,782	9,829	4,569	4.48
4	1,313	4,892	2,275	4.49
5	538	2,005	963	8.79
6	667	2,489	1,158	2.95
7	871	3,092	1,425	7.87
8	664	2,292	1,036	5.49
9	930	3,323	1,500	11.92
10	848	3,077	1,430	10.87
11	442	1,587	730	11.14

12	1,144	3,933	1,804	9.86
13	1,336	4,547	2,059	13.69
14	812	2,972	1,370	4.35
Total	15,924	56,102	26,080	98.01

Source: Baglung IUDP DataSets workbook, PDP sheet and the municipal profile 2075 and NPHC 2021. Ward areas sum to the official 98.01 square kilometres.

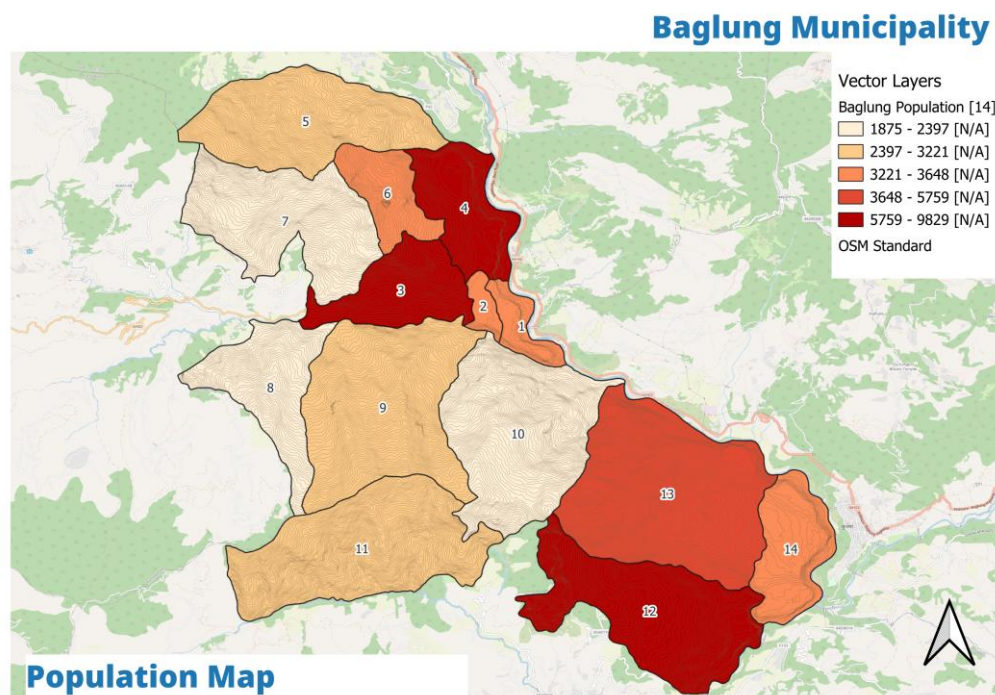


Figure 3.1. Population by ward, 2021. The bazaar core carries the density.

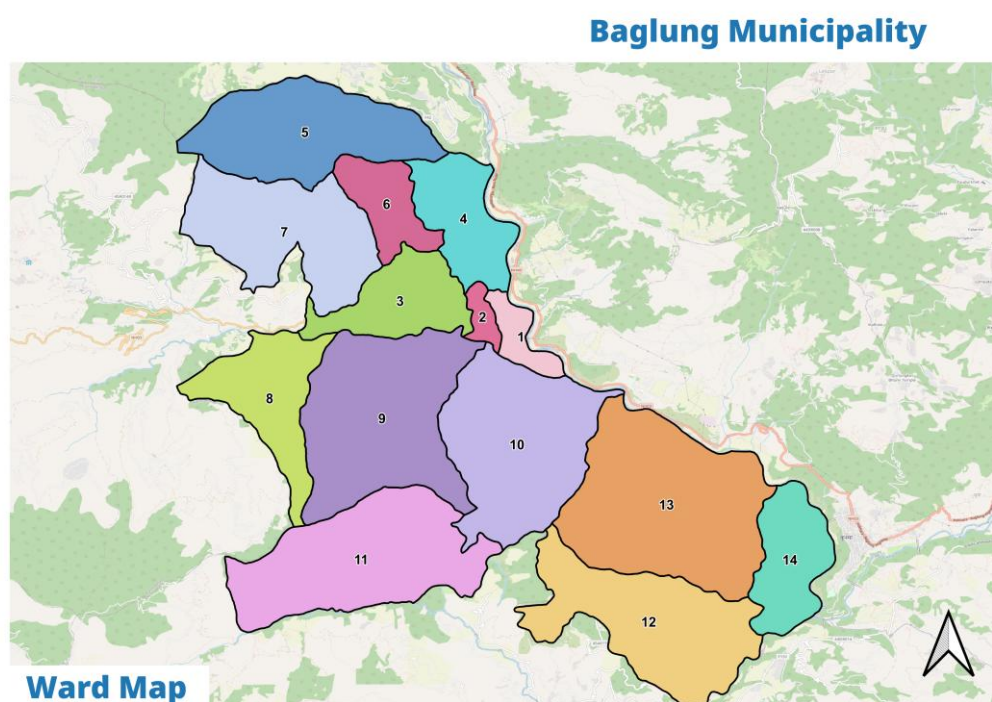


Figure 3.2. Ward map of Baglung Municipality with ward boundaries and labels.

3.2 Topography, climate and land

The municipality runs from about 640 metres at the Kali Gandaki riverbed to above 2,600 metres on the ridge tops. The DEM analysis in the team GIS shows that the buildable land concentrates on the plateau around the bazaar and on the gentler slopes of the corridor wards, while the hill wards climb steeply. The slope map in the GIS database was a key input to the land suitability model in Chapter 4.

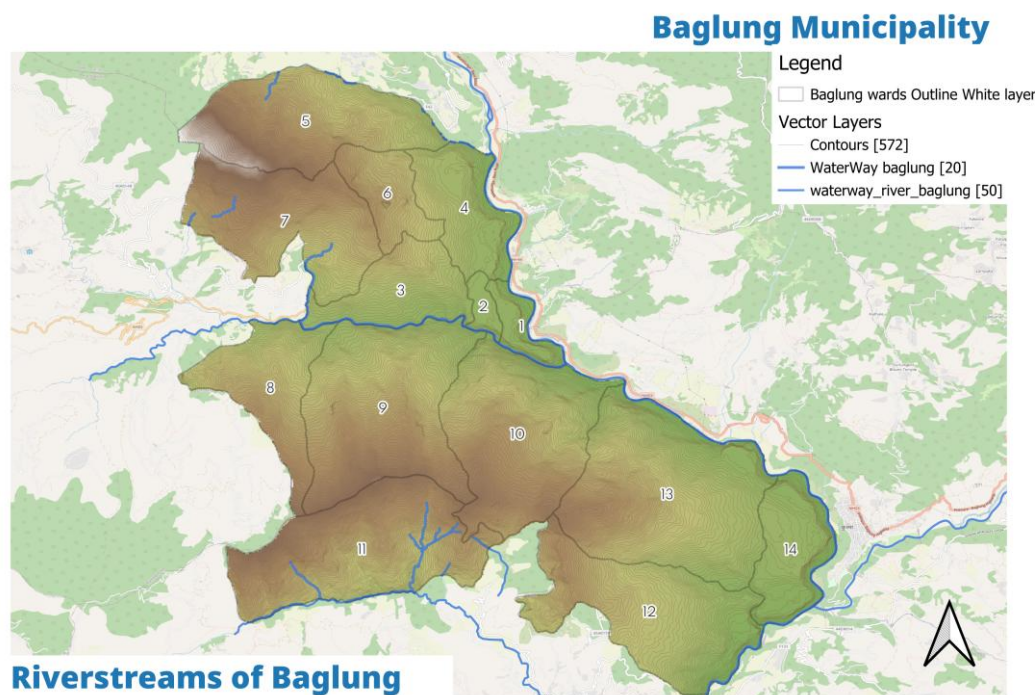


Figure 3.3. Topography of Baglung Municipality. The gorge cuts the eastern edge.

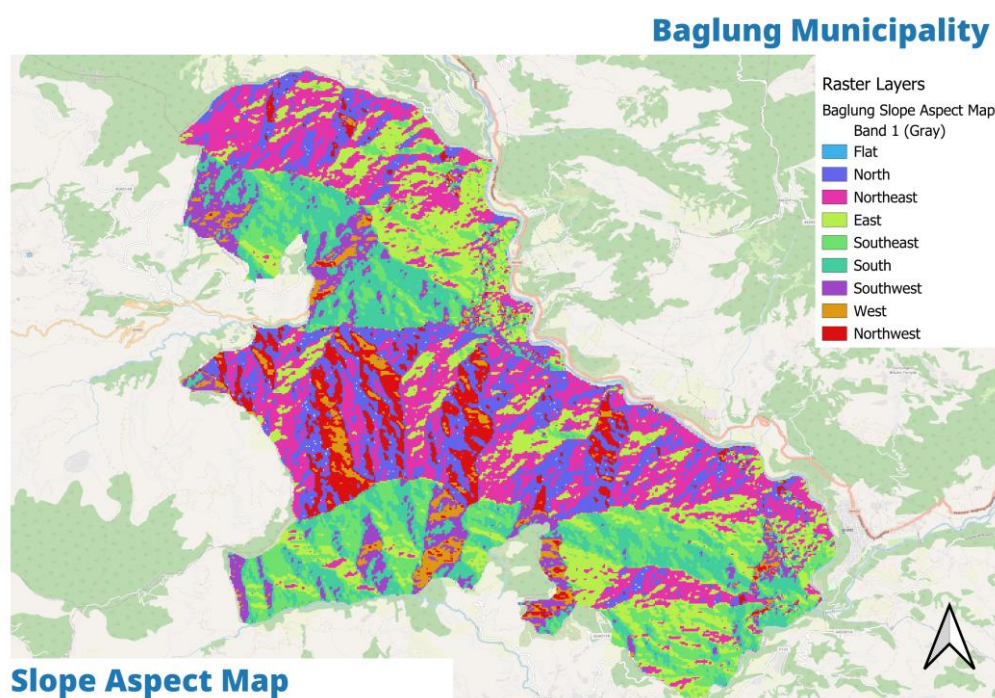


Figure 3.4. Slope aspect map. The buildable plateau and the steep hill wards stand apart.

The climate is the classic mid hill regime. Warm summers with the monsoon from June to September, dry winters with frost on the high wards, and the pre monsoon heat of March and April. The rainfall data from WorldClim in the GIS folder, downscaled for the municipality, shows the annual range between roughly 1,200 and 1,800 millimetres depending on elevation. The monsoon concentration is the reason the bazaar floods almost every year and the corridor wards slide in the rainy season.

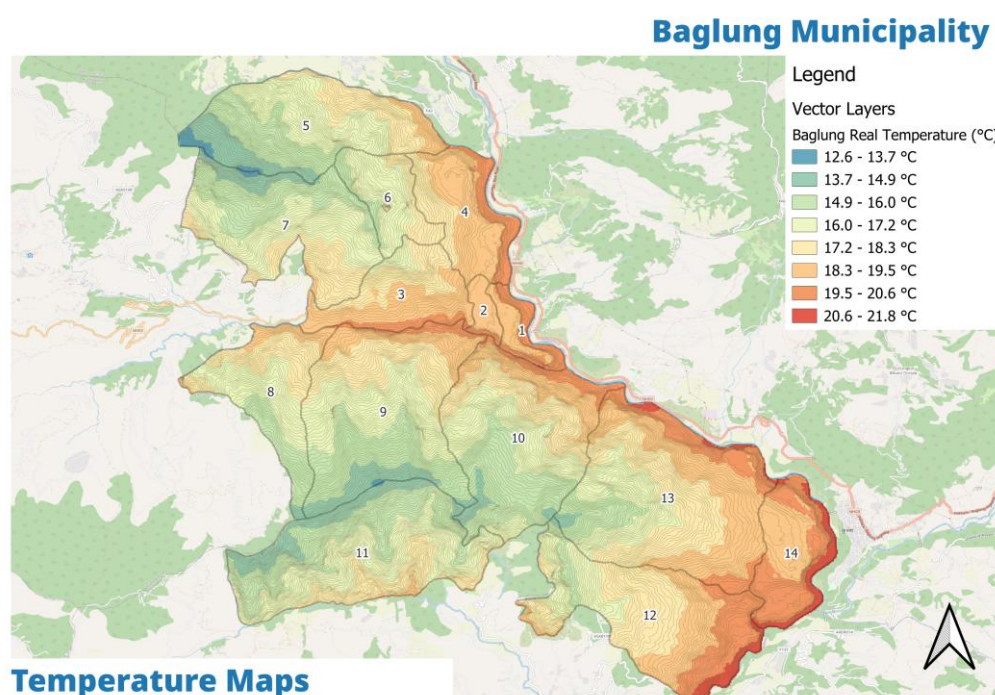


Figure 3.5. Mean temperature surface for Baglung Municipality from WorldClim.

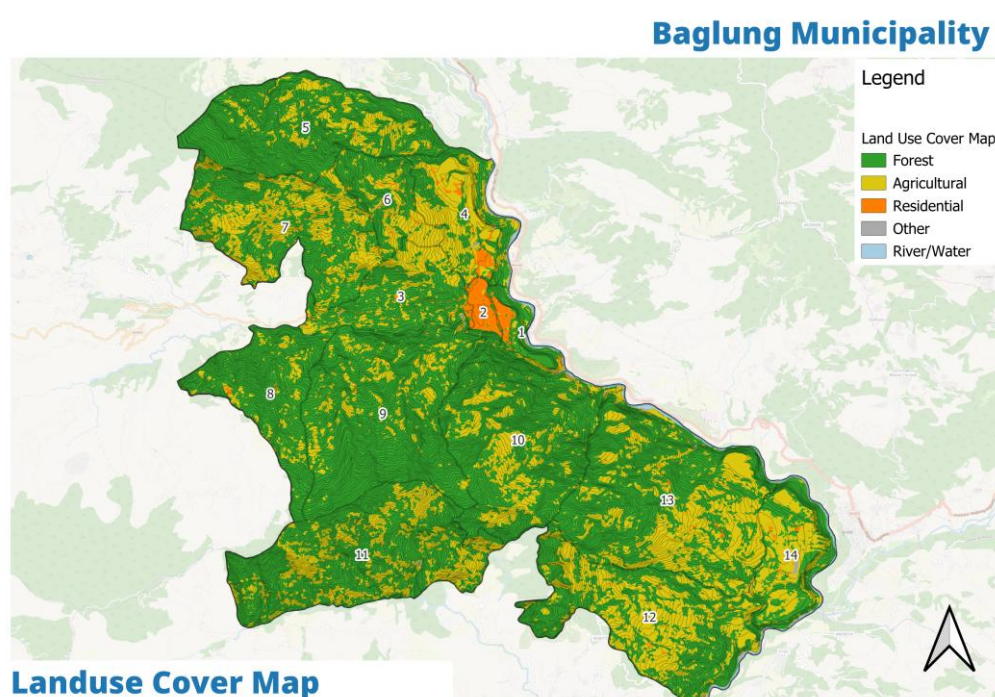


Figure 3.6. Land cover 2021. Forest dominates the hill wards, built up stays in the core.

Land cover tells the settlement story. The tree cover concentrates in the hill wards, the cropland wraps the settlements and the built up area stays in the core. The municipality reports 3,215 hectares of forest, of which 1,801.91 hectares are community forest across 43 user groups and 1,401.43 hectares are government managed (Baglung IUDP DataSets, EnDP sheet). The Malika community forest in Ward 5 alone covers 180 hectares and anchors the green belt on the western flank.

3.3 Demography

Between 2011 and 2021 the population of Baglung fell by 1,721 persons, a decline of 2.98 percent, while households rose by 742. Nepal as a whole grew at about 0.92 percent per year over the same decade (NSO, 2023). Baglung is one of the contracting municipalities, and the decline sits almost entirely in the hill wards while the bazaar wards hold steady.


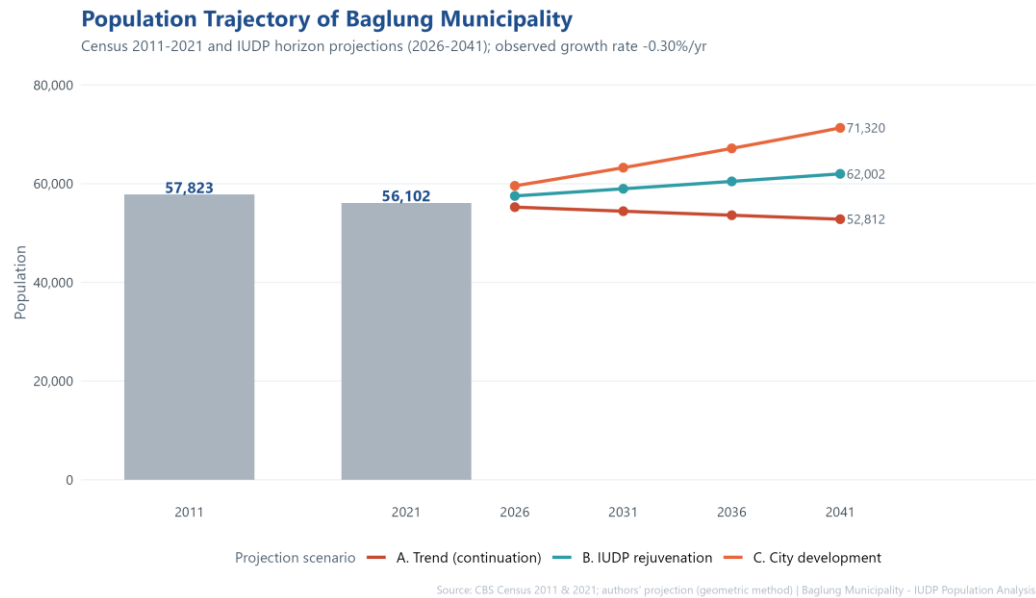


Figure 3.7. Population and households, 2011 to 2021, with the projection path.

The structure of the population carries the planning message. Women are 53.5 percent of residents and head 46.4 percent of households, both direct results of male labour migration. The sex ratio is 86.9 males per 100 females against the national 95.6. Children aged 0 to 14 are 24.4 percent, the working ages 15 to 59 are 62.4 percent and the 60 plus group is 13.2 percent, already above the national share of about 10.2 percent (NPHC 2021).

Age-Sex Pyramid of Baglung Municipality (2021)

Census 2021; narrow base and female-dominated adult ages reflect out-migration of young men

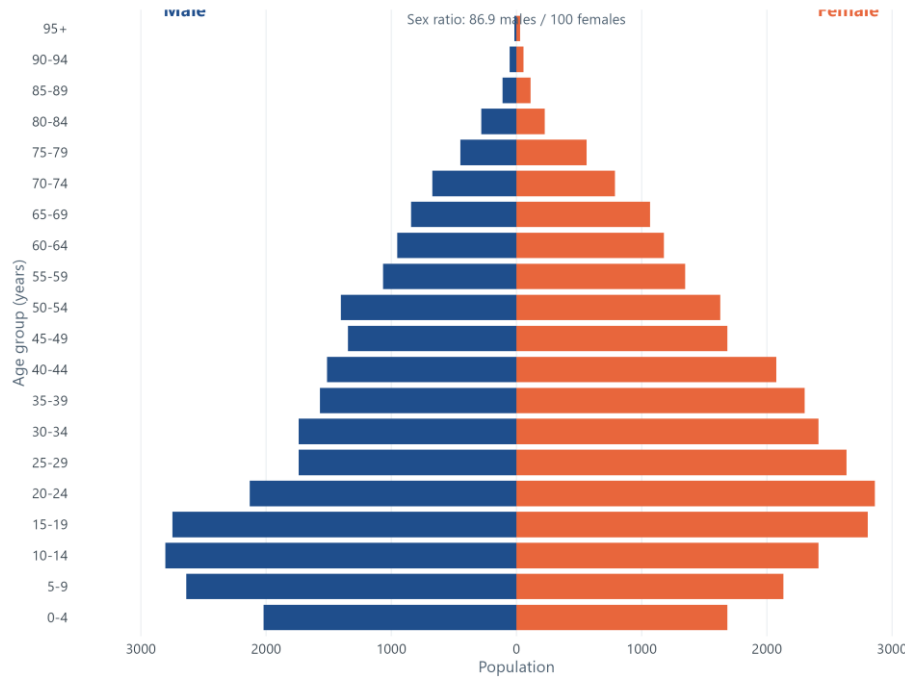


Source: CBS Census 2021 | Baglung Municipality - IUDP Population Analysis

Figure 3.8. Age sex pyramid, 2021. The waist in the working ages shows male migration.

Dependency Ratios through the IUDP Horizon (2021-2041)

Child (0-14), old-age (60+) and total dependency per 100 active persons (15-59)

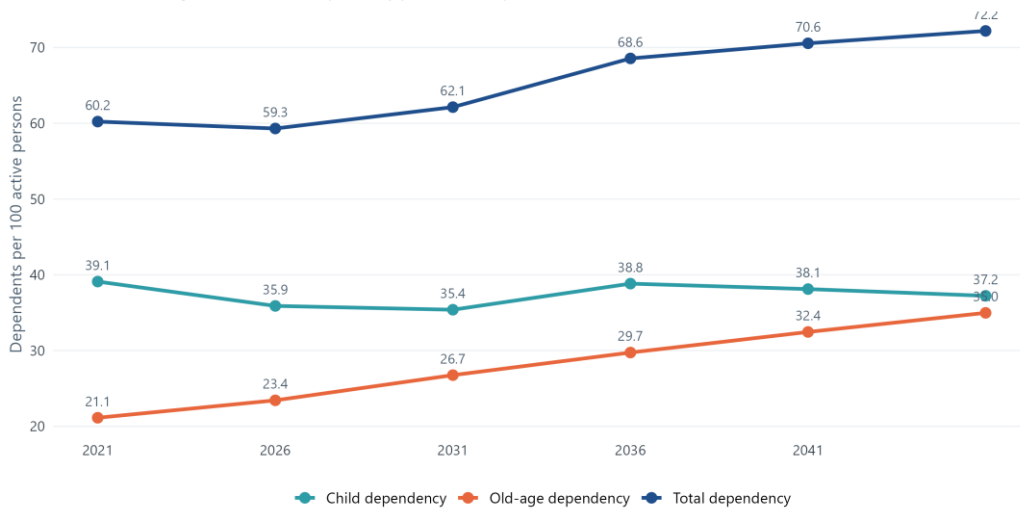

Source: Census 2021 & authors' cohort-component projection | Baglung Municipality - IUDP Population Analysis

Figure 3.9. Dependency ratios, 2021 to 2036. Old age dependency nearly doubles.

Households fragmented from 3.81 to 3.52 persons. That is the nuclearisation story, families splitting into smaller units even as total people fall. For service planning it matters a lot, because every new household needs its own connection, its own plot and its own roof, and the municipality must plan water, sanitation and housing for about 16,600 to 17,100 households by 2036 even with a flat population (SYNTHESIS, Baglung Output).

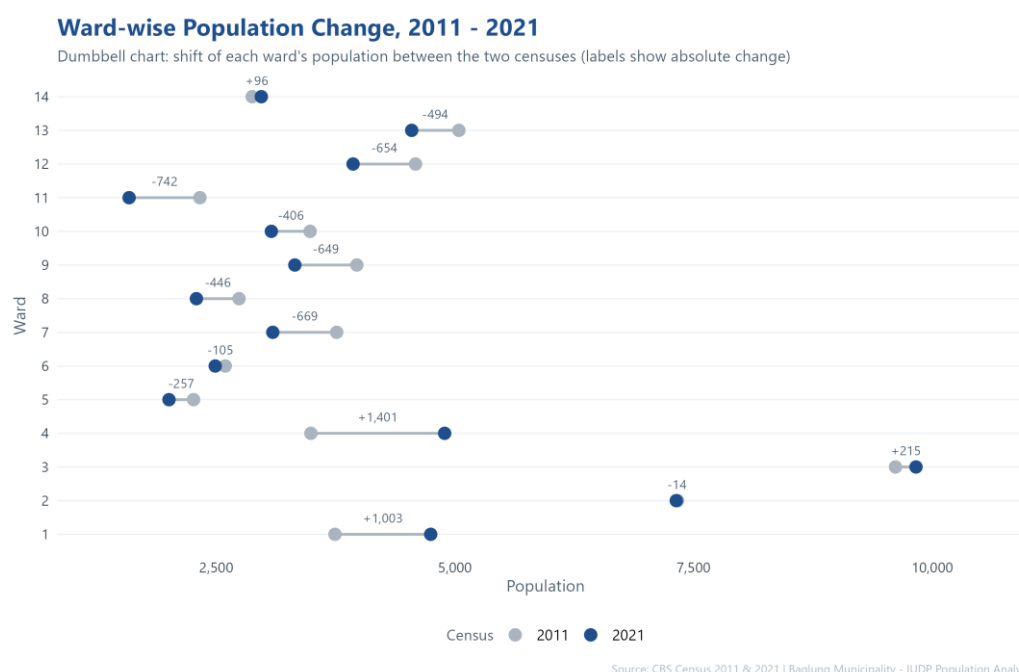


Figure 3.10. Ward level population change 2011 to 2021. The core grew, the hills fell.

3.4 Economy and livelihoods

The economy splits cleanly into two. The bazaar core trades, the hills farm. Half the workforce still works in agriculture, 48.7 percent at the 2021 census, while wholesale and retail trade carries 16.4 percent, construction 7.8 percent and education 5.0 percent. Industry, ICT and finance together hold only about 7 to 8 percent of employment (NPHC 2021).

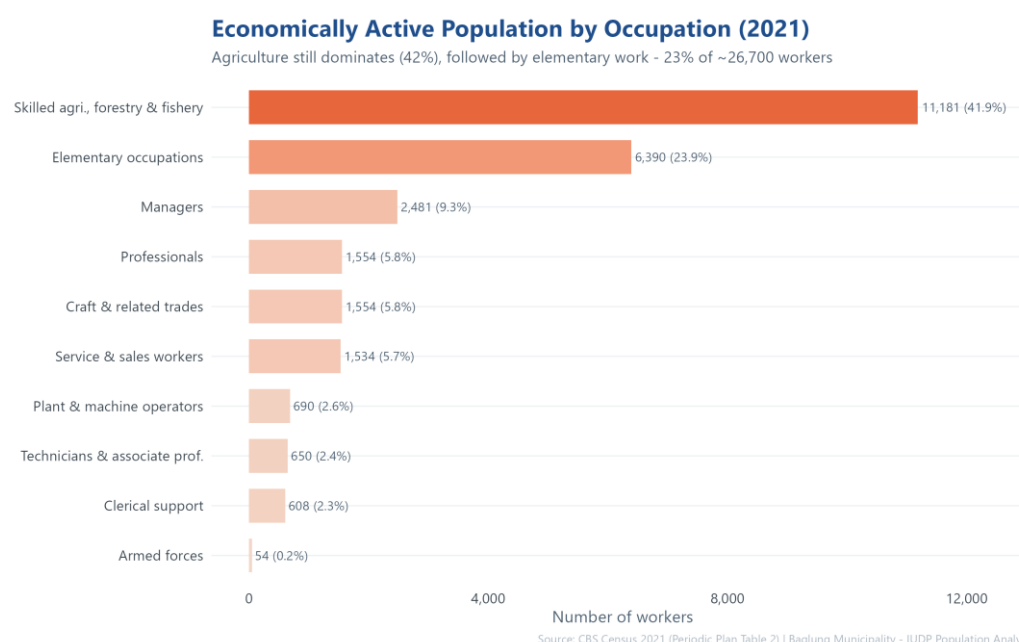


Figure 3.11. Occupation structure. Two economies coexist in one municipality.

The registered economy is concentrated. Of 1,219 registered firms in the Chamber registry, Ward 2 holds 543 or 44.5 percent, Wards 2 and 3 together hold 64.6 percent and the four bazaar wards hold 80.1 percent (BCCI registry, 2082 BS). Trade dominates with 574 firms, hospitality follows with 71, and manufacturing is thin at 20 firms.

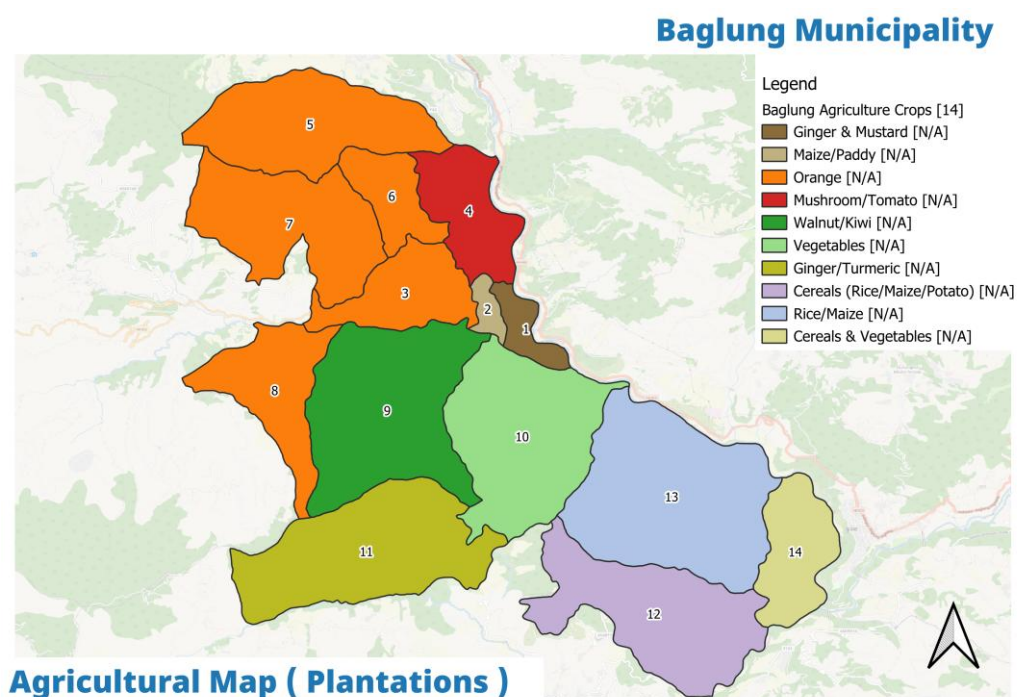


Figure 3.12. Agricultural plantation areas by ward.

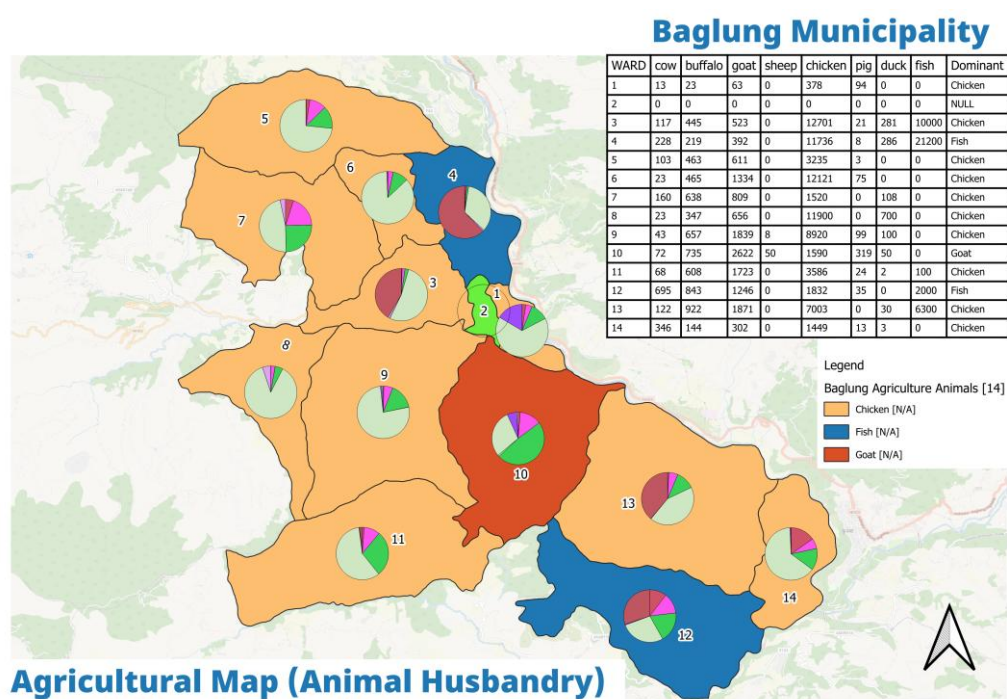


Figure 3.13. Livestock holdings by ward from the field survey.

Table 3.2. Registered firms by sector, BCCI registry

Sector	Number of firms	Share
Trade (wholesale and retail)	574	47.1 percent
Hospitality	71	5.8 percent

Construction	21	1.7 percent
Manufacturing	20	1.6 percent
Health	22	1.8 percent
Agriculture linked	15	1.2 percent
Education	7	0.6 percent
Others and services	489	40.1 percent
Total	1,219	100 percent

Source: BCCI lifetime and general member registry, 2082 BS, compiled in the Baglung IUDP DataSets.

Livestock follows the hills. The field count recorded 77,971 chickens, 13,991 goats, 6,509 buffaloes and 39,600 kilograms of fish production, concentrated in Wards 3, 4, 6, 8, 12 and 13. Ward 2 recorded zero holdings, which confirms the complete urbanisation of the core. The orange economy stands out in the agriculture rows, with Ward 6 alone reporting sales of about one crore rupees of oranges in the last year (EDP sheet, Baglung IUDP DataSets).

Table 3.3. Ward wise occupation structure, EDP sheet

Ward	Agriculture (% HH)	Service (% HH)	Business (% HH)	Foreign employment (% HH)
2	6	33	42	17
3	8	30	40	12
4	7	31	41	15
5	22	18	15	35
6	20	20	18	30
7	25	15	12	38
8	23	17	14	36
9	28	14	10	40
10	24	16	13	37
11	30	12	8	42
12	18	22	20	28
13	15	25	28	22
14	16	24	26	24

Source: EDP sheet, Baglung IUDP DataSets. Ward 1 not recorded in the occupation survey.

3.5 Infrastructure baseline

The road network totals about 322 kilometres at the municipal inventory, of which about 47.1 kilometres are blacktopped, roughly 13 percent. The OSM road analysis in the team GIS records about 487 kilometres of mapped roads of which about 30 kilometres are blacktopped, because the open data base includes trails and cart tracks the municipal inventory leaves out. About 62 percent of the maintained network remains earthen or seasonal. The GIS road analysis by ward is in the annex. Rights of way in the bazaar run 5 to 8 metres against the 10 to 30 metre standards of the Nepal Urban

Road Standard 2011, which is the single largest physical constraint in the core (Nepal Urban Road Standard, 2011).

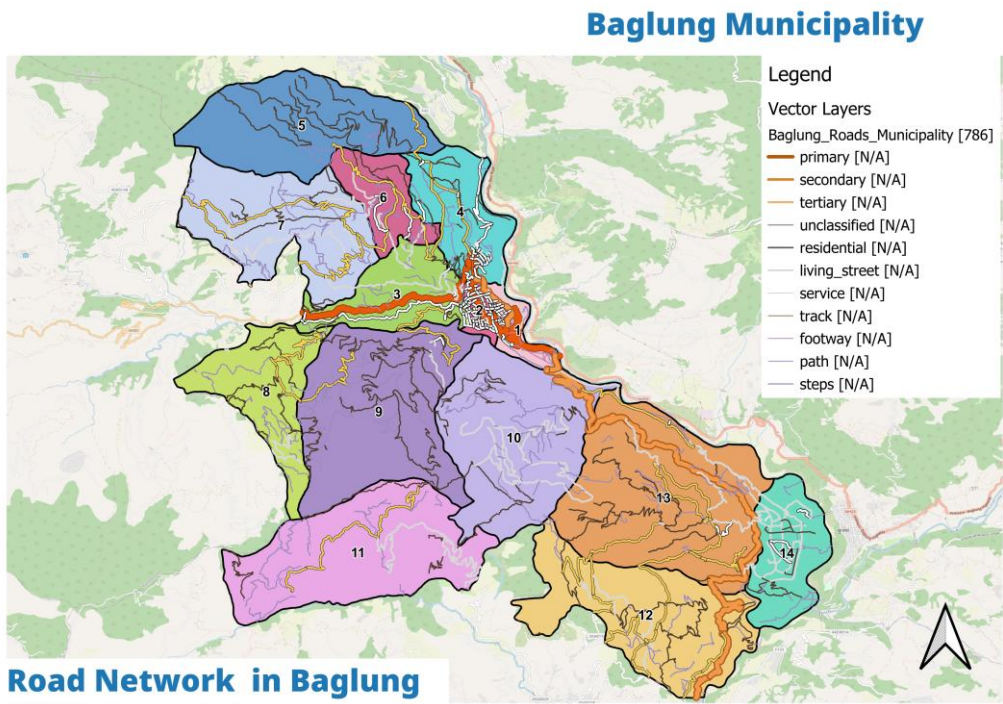


Figure 3.14. Road network and hierarchy. The Mid-Hill and the Kali Gandaki corridor are the spines.

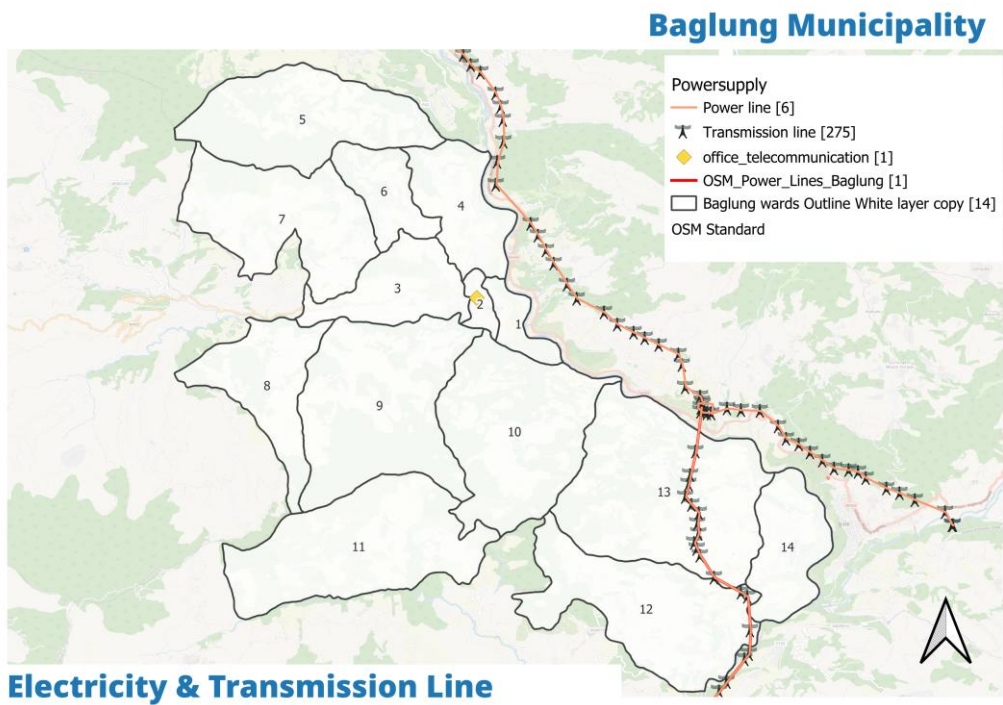


Figure 3.15. Electricity grid and transmission lines across the municipality.

Water supply reaches 88.7 percent of households with piped or tap water. The Kathekhola lift project pumps raw river water up a 250 metre vertical incline at 70 litres per second to serve more than 4,100 households in the bazaar, with reservoirs up to 700,000 litres (municipal records, 2082 BS). Treatment

is basic sedimentation and filtration. About 1,002 households in Ward 12 still draw on unimproved sources.

Sanitation is the weakest link. There is no public sewer network, no sewage treatment plant and no public toilet. Every building relies on septic tanks, and the storm drainage is incomplete, which is why the bazaar floods from hillside runoff each monsoon. Solid waste reaches about 18 tonnes per day, with the three bin system running in the core and eight wards still without formal collection (EnDP sheet, Baglung IUDP DataSets).

Electricity reaches 98.6 percent of households on the national grid with only 1.2 percent on solar backup. Telecommunication coverage is effectively complete. The 66/33 kV substation serves the bazaar load, and the FY 2083/84 budget already commits to smart street lighting and underground utilities in the core.

3.6 Social services baseline

The education inventory lists 89 schools carrying 13,098 students (SDP field survey, 2082 BS). The student teacher ratio averages 9.4 but ranges from 5.6 in Ward 11 to 19.6 in Ward 2 public schools, and the private schools concentrate in Wards 1 to 4 while the rural wards rely on public schools alone. Literacy stands at 83.5 percent against the national 76.3 percent, with the female rate at 77.0 percent, a 14 point gap that widens in the hill wards.

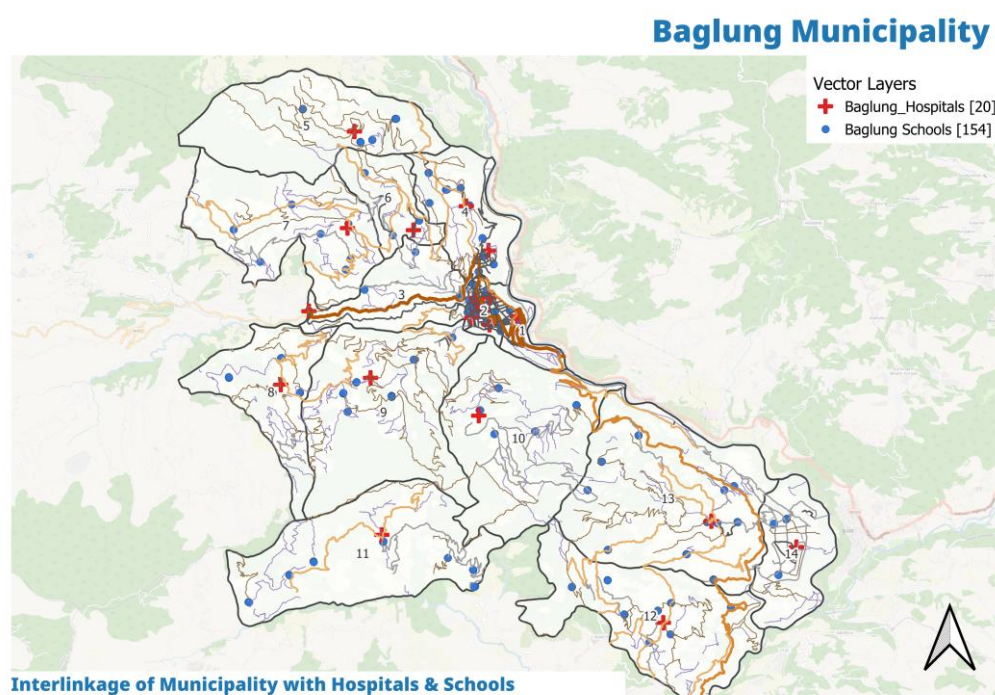


Figure 3.16. Schools and health facilities with the service linkage. The core is dense, the hills are thin.

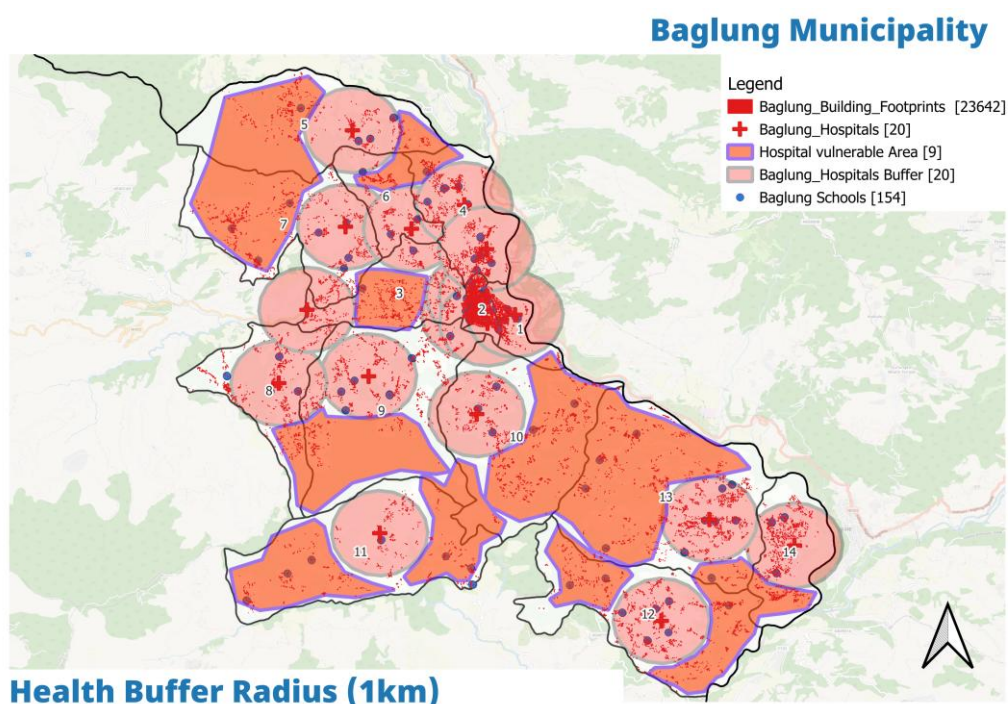


Figure 3.17. Hospital service coverage, one kilometre buffer.

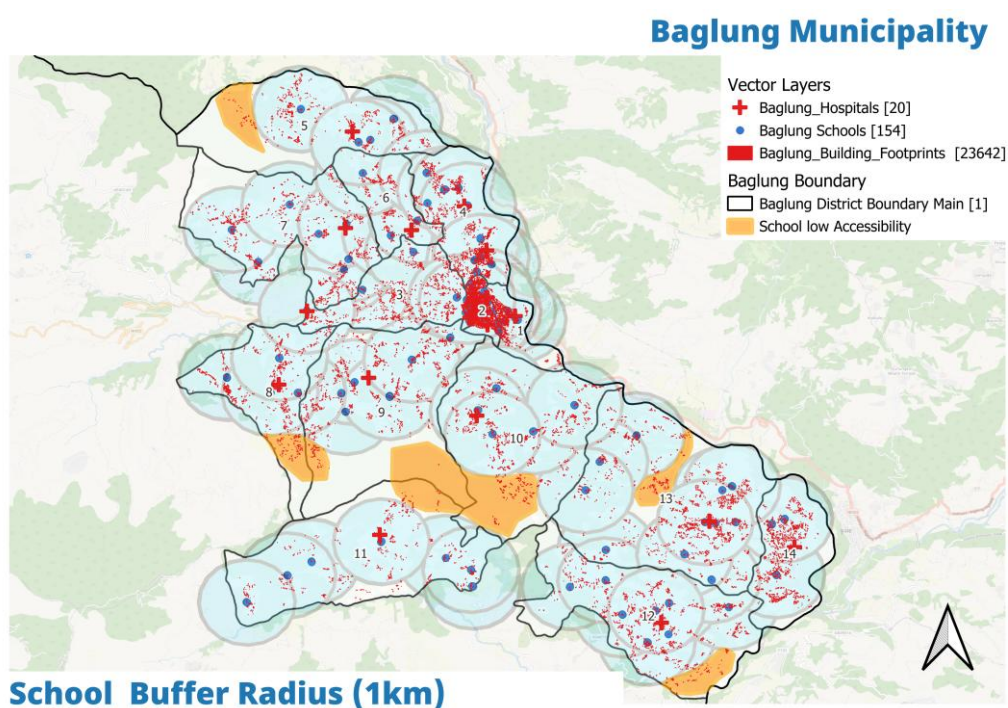


Figure 3.18. School service coverage, buffer radius analysis.

Health services anchor in the core. Dhaulagiri Provincial Hospital in Ward 2 carries 140 beds and serves 5,000 to 6,000 patients from five districts, with an approved trajectory toward 200 beds and a 300 bed medical college. The Dhaulagiri Ayurvedic Hospital adds 25 beds. Every ward has a health post, but only some have birthing centres, and dengue cases climbed from 85 in FY 79/80 to 1,120 in FY 81/82 (SDP sheet, Baglung IUDP DataSets).



Figure 3.19. Urban Health Promotion Centre in Ward 2, serving the core population. Photo: Baglung Group field team, 2082 BS.

The social protection register is the quiet crisis. Birth registration sits at about 62 percent, leaving roughly 284 births a year unregistered. The average age of marriage for girls is 18.3, below the legal age of 20 in every ward, and 19.9 percent of girls marry below 18, with Ward 8 at 28.8 percent (NPHC 2021). The registered disability count is 2.9 percent of the population, and the team field work suggests the real figure is higher.

Table 3.4. Ward wise health facility inventory, SDP sheet

Ward	Health post staff (M/F)	Birthing centre	Health centres	Facility type
1	Not recorded	No	1	Basic health service centre
2	1 / 3	No (provincial hospital in ward)	3	Clinic, urban health centre, provincial hospital
3	Not recorded	No	1	Basic health service centre
4	Not recorded	No	1	Health post
5	Not recorded	No	1	Health post
6	Not recorded	No	1	Health post
7	Not recorded	No	1	Health post
8	Not recorded	No	1	Health post
9	Not recorded	No	1	Health post
10	Not recorded	No	1	Health post
11	Not recorded	No	1	Health post
12	Not recorded	No	1	Health post

13	Not recorded	No	1	Health post
14	Not recorded	No	1	Health post

Source: SDP sheet, Baglung IUDP DataSets. Ward 2 is the only ward with multiple facilities and specialist access.

Table 3.5. Ward wise institutional capacity, IDP sheet

Ward	Admin staff	Vacancies	Ward committee (M/F)	User committees	e governance
1	Not recorded	Not recorded	Not recorded	Not recorded	Not recorded
2	5	0	3 / 2	16 to 18	Yes (high)
3	3	1	3 / 2	10	Partial
4	2	1	2 / 1	8	Partial
5	2	0	2 / 1	5	No
6	2	0	2 / 1	6	No
7	2	0	2 / 1	7	No
8	2	0	2 / 1	5	No
9	2	0	2 / 1	8	No
10	2	0	2 / 1	6	No
11	1	0	2 / 1	4	No
12	3	1	3 / 2	10	Partial
13	2	0	2 / 1	8	No
14	2	0	2 / 1	6	No

Source: IDP sheet, Baglung IUDP DataSets. Ward 2 has the strongest institutional base.

3.7 Fiscal and institutional baseline

The approved budget for FY 2083/84 is NPR 114.95 crore, down 12.2 percent from the year before. Internal revenue and bank balance contribute NPR 18.00 crore, revenue sharing NPR 15.55 crore, federal grants NPR 78.22 crore and provincial grants NPR 3.17 crore. The autonomy rate of 29.2 percent counts internal revenue and revenue sharing together, NPR 33.55 crore of the NPR 114.95 crore budget. Pure own source revenue, the NPR 18.00 crore line, is 15.7 percent of the budget, and both figures are used in this plan with the distinction stated wherever they appear (municipal budget red book, FY 2083/84).

The biggest single fiscal weight is the TDF debt on the Davgara Bus Park. NPR 3.50 crore is committed every year to service a 9 crore principal, and the park itself is not yet generating terminal revenue because bus routing is not enforced. The ward allocations of NPR 6.40 crore and the municipal infrastructure pool of NPR 4.00 crore are the capital that the plan proposes to pool into corridor projects.



Figure 3.20. Baglung Municipal Office staff, the institutional base for the TDF debt and ward allocations. Photo: Baglung Group field team, 2082 BS.

Institutionally the municipality has 72 local laws on the books, an unusually mature legal base, a sister city partnership with Windham Eco Global Village in Australia, and a LISA governance score that rose from 37.5 to 84 out of 100 in four years. The weaknesses are technical staff, with planning and GIS positions vacant, weak spatial databases and limited women in decision making (institutional review, 2082 BS).

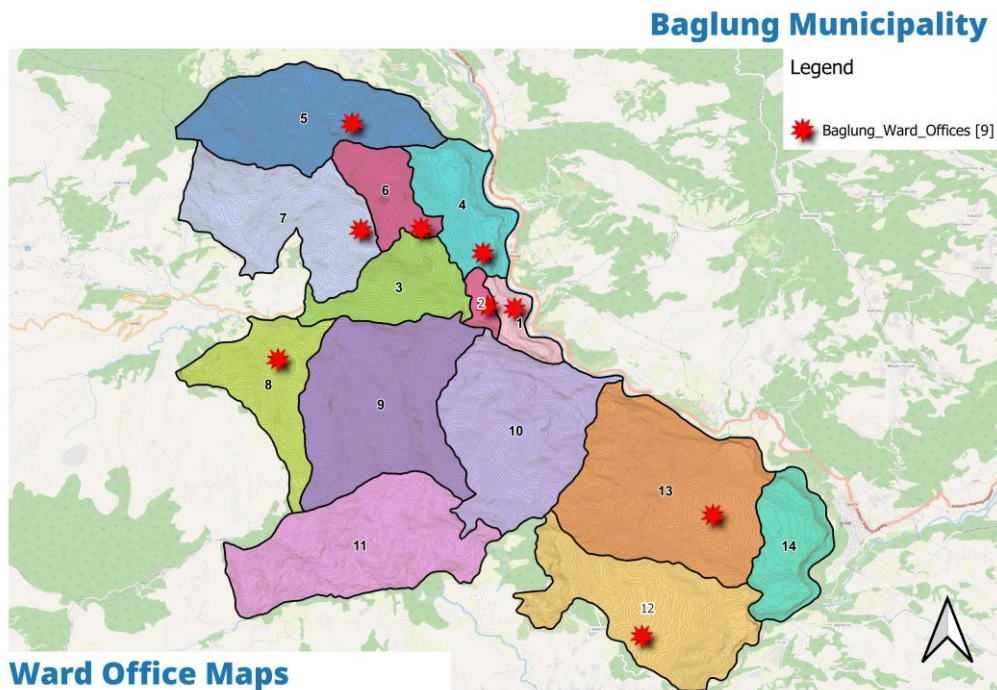


Figure 3.21. Ward offices and the administrative network of the municipality.

3.8 Environmental baseline and hazards

The forest estate of 3,215 hectares is the environmental anchor. The team GIS added the flood and landslide rasters from the DEM and rainfall analysis, which mark the Kali Gandaki corridor and the steep hill wards as the hazard belts. The ward disaster summary records two deaths in the Pangre Khola flash flood of Ward 5, annual monsoon landslides on the corridor in Ward 14, and Ward 12 as one of the most hazard prone wards of the municipality (EnDP sheet, Baglung IUDP DataSets).

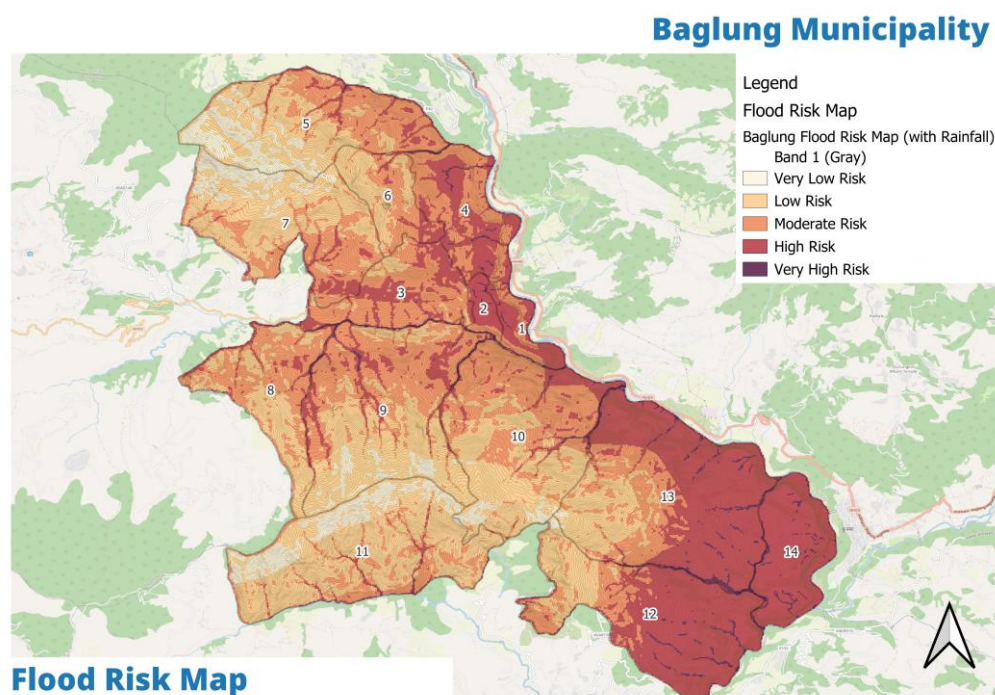


Figure 3.22. Modelled flood hazard. The river line and the bazaar runoff zones show highest exposure.

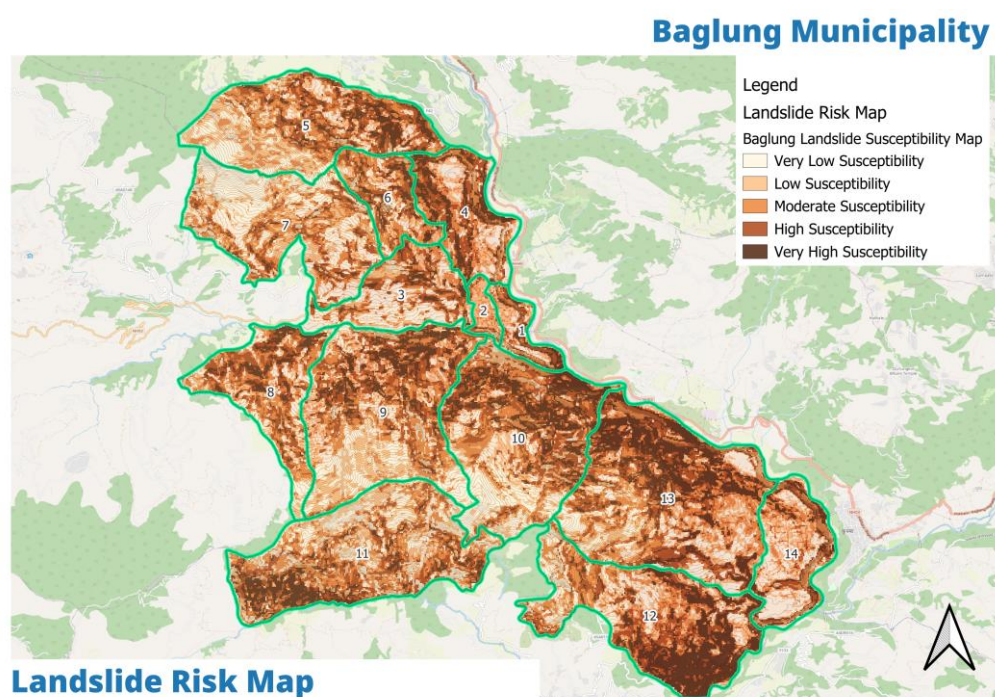


Figure 3.23. Modelled landslide susceptibility. The corridor and steep hill wards dominate.


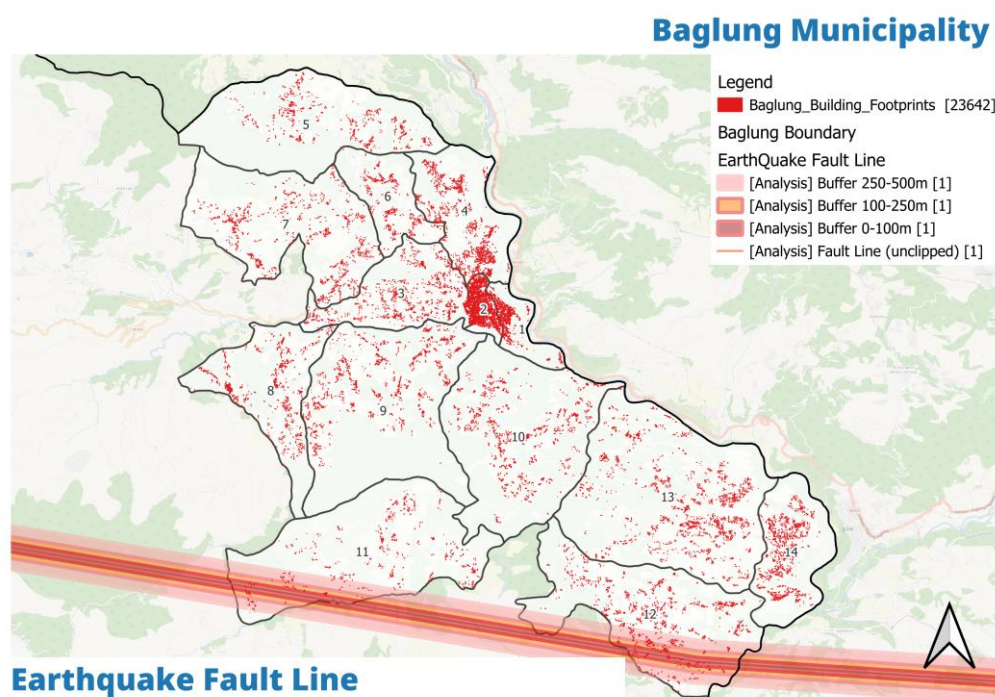


Figure 3.24. Fault lines with risk buffers from the geological data of the region.

FY 2083/84 Approved Budget Revenue Composition

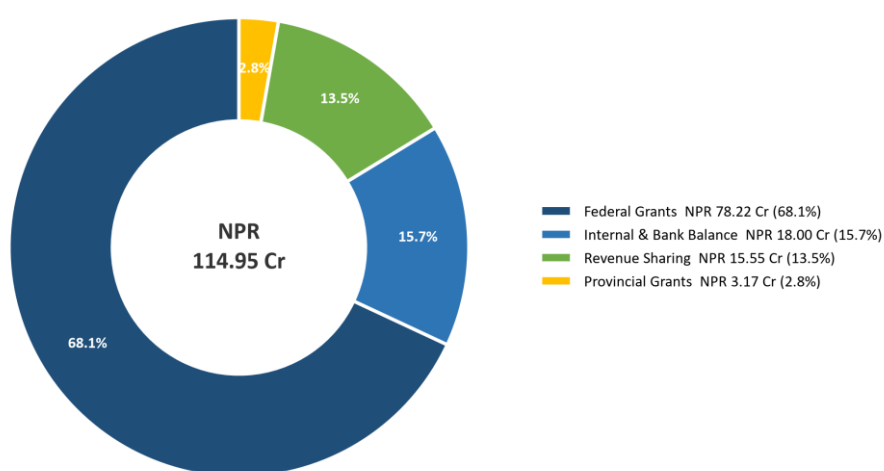

Source: Baglung Municipality red book FY 2083/84

Figure 3.25. FY 2083/84 approved budget revenue composition. Federal grants dominate at 68 percent, with own source at 15.7 percent.

Emergency capacity is thin for the hazard load. Two ambulances, one fire engine, two excavators and 150 to 200 trained search and rescue personnel exist, but only two evacuation centres are recorded and both are under equipped. The zero waste programme is the bright spot, with the three bin system in the core, an agreement with Samanata Abhiyan Nepal, and a signed incineration partnership with ALK

Eco for 1 to 3 tonnes per day of hazardous waste at a cost of NPR 6 to 12 million (municipal records, 2082 BS).

4. Analysis, projections and demand gaps

4.1 The four forces that shape the future

The demographic analysis in the companion Social Development Plan reduces the future to four forces, and this chapter adopts them as the frame for every sector plan (Baglung SDP, 2026).

15. Ageing. The 60 plus share rises from 13.2 percent toward 20 percent by 2036. Old age dependency doubles from 21 to about 32 elders per 100 workers. Wards 9 to 13 already pass 16 percent.
16. Youth drain. Of the residents absent abroad, 70.5 percent left for foreign employment and 80.7 percent are aged 15 to 34. The working age pool keeps leaking even as the 5 to 14 bulge replenishes it.
17. Fragmentation. Household size fell from 3.81 to 3.52. Housing demand climbs against a flat population, adding 700 to 1,100 dwelling units by 2036.
18. Core pull. The bazaar wards 1 to 4 and 14 hold 53 percent of the population on 16 percent of the land. Ward 4 grew 40.1 percent over the decade while Ward 11 lost 31.9 percent.

The four forces act together. The same out migration that ages the hills also feminises headship, fragments households and concentrates the core. No sector plan can treat them separately, which is why Chapter 5 carries the demographic handover into every thematic plan.

4.2 Population projection to 2041

The team projected the population with the three methods the IUDP guideline recommends, arithmetic growth, geometric growth and the cohort component model. The cohort model isolates the pure age structure effect with no mortality, no migration and births frozen at the 2021 rate, and it gives 63,496 by 2031. That is the natural increase ceiling. The observed 2011 to 2021 trend, by contrast, reflects heavy outmigration and gives minus 0.3 percent a year, which is the floor.

The adopted path sits between these bounds at plus 0.5 percent geometric growth from the 2026 base of 55,261. It assumes that outmigration eases as the tourism and agro processing jobs of Chapters 5.5 and 5.6 materialise, without assuming that it fully reverses. The low path at minus 0.3 percent gives about 53,600 by 2036, the medium at 0 percent holds 55,261, the high at plus 0.8 percent gives 59,844 and the adopted path gives 58,087 (Baglung Group, 2082 BS).


Table 4.1. Adopted population path, 2026 to 2041

Year	Population (adopted 0.5 percent)
2026 (base)	55,261
2031	56,656
2036	58,087
2041	59,556

Source: Baglung IUDP team projection, geometric growth on the 2021 census base.

Population Projection Scenarios for IUDP (2026-2041)

Geometric growth method; base population = 56,102 (Census 2021)

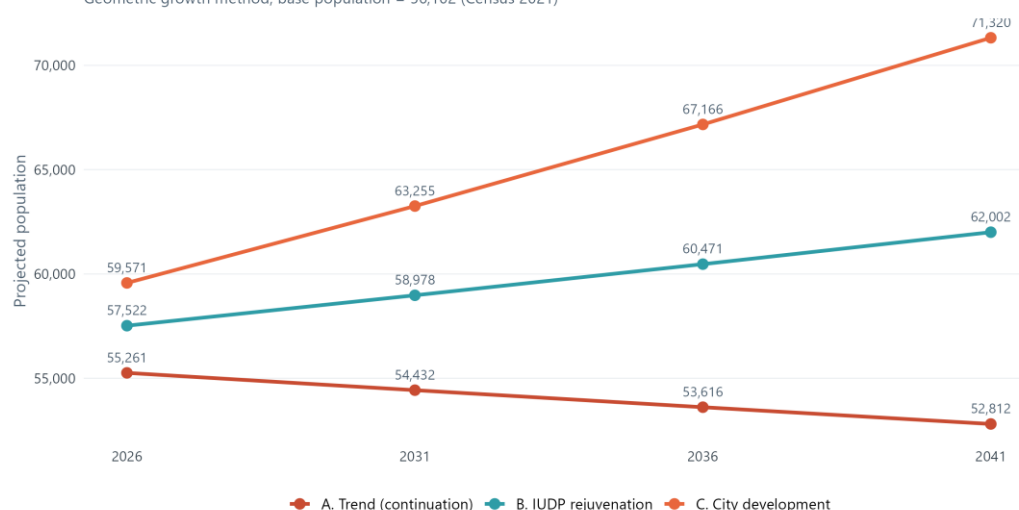

Source: Authors' projection for Baglung IUDP | Baglung Municipality - IUDP Population Analysis

Figure 4.1. Projection scenarios. Even the high path stays below the 2011 population.

The household count matters more than the population count for infrastructure sizing. At the adopted path and a household size easing to 3.45, the municipality passes about 16,800 households by 2036 and about 17,100 by 2041. Water, sanitation, solid waste and housing plans in Chapter 5 are all sized against this household line, not against the flat population line.

4.3 Demand against DUDBC norms

The gap analysis follows the DUDBC Planning Norms and Standards 2013. For each service the team compared the norm, the present condition and the gap at the 2031 and 2036 horizons. The norms table itself is reproduced in the annex. The headline results follow.

Table 4.2. Physical infrastructure gaps against norms


Service	Norm (DUDBC 2013)	Present	Gap
Road right of way	Arterial 30 m, collector 14 m, local 10 m	5 to 8 m in the core	Widening infeasible, manage through corridor planning
Road surface	90 percent of households within 1 km of motorable road	About 13 percent blacktop, 62 percent earthen	Priority blacktop of 60 km core and corridor roads
Water supply	80 to 100 litres per capita per day, metered connections	88.7 percent connected, unmeasured	Extend to 98 percent, add storage and metering
Sanitation	Public sewer with 200 mm trunk minimum	None, septic only	First phase sewer for the bazaar core
Storm drainage	Complete network	Partial, bazaar floods yearly	Trunk drains from hillside to river
Solid waste	Collection point within 200 m, 30 percent to landfill	6 of 14 wards served, 100 percent landfilled	Extend to 14 wards, compost and recycle 70 percent
Electricity	100 percent coverage	98.6 percent	Connect the residual 1.4 percent, solar backup

Source: DUDBC Planning Norms and Standards 2013 and municipal field survey 2082 BS.

Table 4.3. Social infrastructure gaps against norms

Service	Norm (DUDBC 2013)	Present	Gap
Primary school	1 per 3,000 at 0.4 to 0.8 km	89 schools, declining enrolment	Consolidate, right size to the 2036 child cohort
Health	PHCC 1 per 20,000, hospital 1 per 50,000	140 bed provincial hospital, 14 health posts	Staffing and specialties, not beds
Neighbourhood park	1 per 800 population, 0.4 ha	None in the dense wards	30 parks deficit in Wards 1 to 3
Local park	1 per 10,000, 1 ha	3 parks	3 more local parks
Community library	1 per 10,000	1 public library	5 more libraries
Old age home	1 per 20,000	2 ashrams	1 more, plus day care
Fire coverage	Station within 5 to 7 km radius	1 station in Ward 2	Second station for Wards 7 to 14

Source: DUDBC Planning Norms and Standards 2013 and the SDP facility survey 2082 BS.

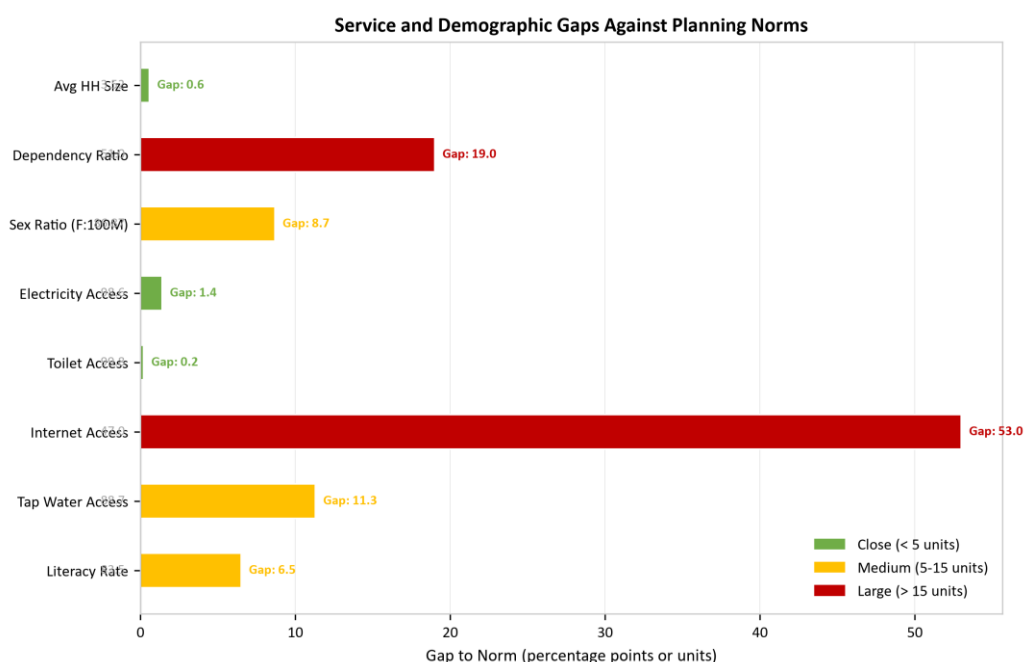

Source: Baglung IUDP team, norms from DUDBC (2013) and SDG targets. Present values from Census 2021 and field survey 2082 BS.

Figure 4.2. Service and demographic gaps against planning norms. Internet access, sex ratio and average household size show the largest gaps.

Demand analysis and forecast

The norm gaps convert into demand forecasts at the adopted population and household paths. The physical demand is sized on the 2031 and 2036 household counts, the social demand on the cohort and ageing projections of Chapter 4, and the economic demand on the programme targets of Chapter 5.6. These three tables are the quantitative bridge between the analysis of this chapter and the programmes of Chapter 5, and every programme quantity in the sector chapters traces back to a row here.

Table 4.4. Physical infrastructure demand analysis and forecast

Service	Norm or basis	Present	2031 forecast	2036 forecast	Gap to close
Water supply	120 lpcd at the adopted path	3.64 MLD delivered, 5 MLD capacity	6.8 MLD demand	6.9 MLD demand	1.9 MLD capacity plus treatment and metering
Road blacktop	90 percent households within 1 km motorable	47 km blacktopped, 13 percent	110 km	147 km	160 km by 2041
Core sewerage	Sewer with treatment for the core	None	25 km sewer, 2 MLD plant started	Core connected	Full core system
Storm drainage	Complete network	Partial, bazaar floods yearly	Trunk drains 12 km	Network complete	40 km total programme
Solid waste	70 percent diverted, collection 200 m	6 of 14 wards, 18.2 TPD landfilled	14 wards collected	70 percent diverted	8 wards plus processing
Electricity	100 percent coverage	98.6 percent	100 percent	100 percent	1.4 percent plus solar backup

Source: Baglung IUDP team forecast on the adopted population path, DUDBC norms 2013 and the sector programmes of Chapter 5.

Table 4.5. Social infrastructure demand analysis and forecast

Service	Norm or basis	Present	2031 forecast	2036 forecast	Gap to close
Primary school seats	1 school per 3,000, cohort sized	89 schools, 13,098 students	Cohort 7,406	Cohort about 7,000	Consolidate 12 schools, no new construction
Health staffing	PHCC norm staffing	45 staff at hospital vs 80 norm	8 specialty posts filled	200 bed expansion supported	35 staff plus specialties
Birthing centres	Delivery within ward	1 (hospital)	5 (4 new)	5 operating	4 centres
Old age homes	1 per 20,000	2 ashrams	3	3 plus day care	1 home plus 2 day care units
Neighbourhood parks	1 per 800 in dense wards	None in Wards 1 to 3	First 10 sites	30 park deficit met	30 parks in the core
Community libraries	1 per 10,000	1	3	6	5 libraries

Source: Baglung IUDP team forecast on NPHC 2021 cohorts and DUDBC norms 2013.

Table 4.6. Economic infrastructure demand analysis and forecast

Facility	Basis	Present	2031 forecast	2036 forecast	Gap to close
Agro processing clusters	Value chains of Chapter 5.6	None	2 clusters, Wards 13 and 14	3 clusters plus feed mill	3 sites, 33 crore programme
Cold storage	Fish and dairy	None	500 t capacity	1,000 t capacity	Full chain

	lines				
Logistics and parking	Ward 2 trade volume	Unregulated bazaar parking	Davgara terminal operating	Logistics hub complete	25 crore programme
Irrigation	Farm potential	25 percent of farmland	35 percent	45 percent	20 points via small schemes
Digital market platform	BCCI trade base	None	Wholesale catalogue live	Full platform	Build and operate

Source: Baglung IUDP team forecast on EDP sheet data, BCCI registry and the economic programme of Chapter 5.6.

4.4 Land suitability

The team GIS built a multi criteria suitability model from the DEM, slope, aspect, land cover, flood and landslide rasters, the fault buffers and the road access. The output classes run from not suitable to very highly suitable. The suitable classes concentrate on the plateau, the corridor wards and the gentler valley slopes, while the gorge edge, the steep hill wards and the flood plain fall into the least suitable classes.

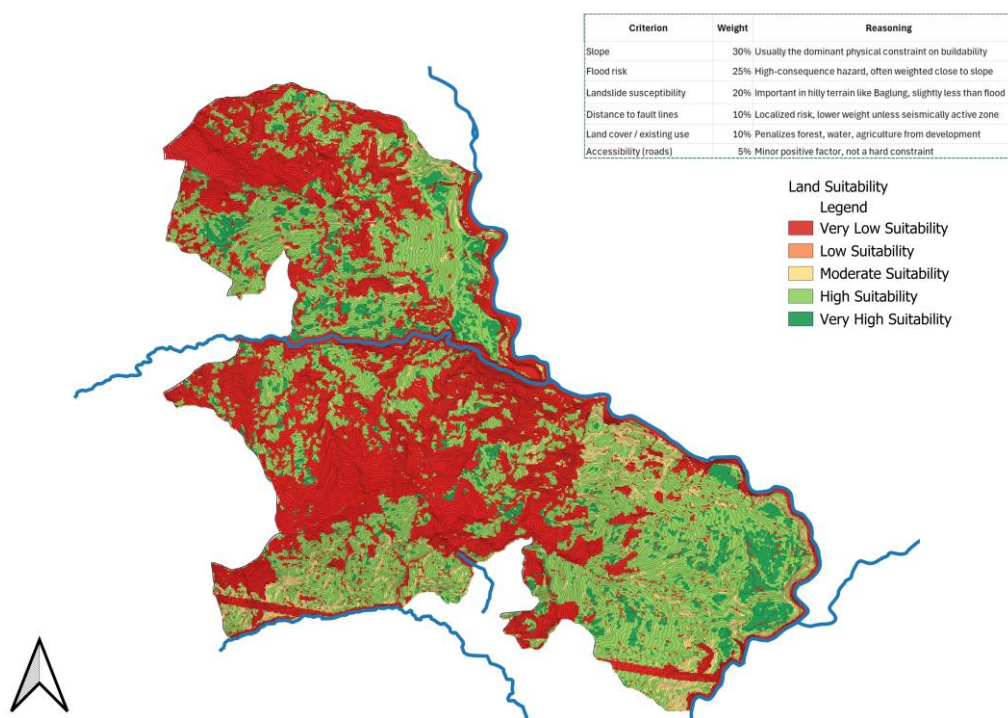


Figure 4.3. Land suitability for development from the multi criteria model.

The suitability map is the spatial spine of the plan. The development concept in Chapter 5.1 zones the municipality from this map, and the three flagship projects in Chapter 7 each pass a site level check against the same rasters. The fault line buffers in the GIS add the seismic constraint, and the full model documentation, the factor weights and the constraint masks are in the annex.

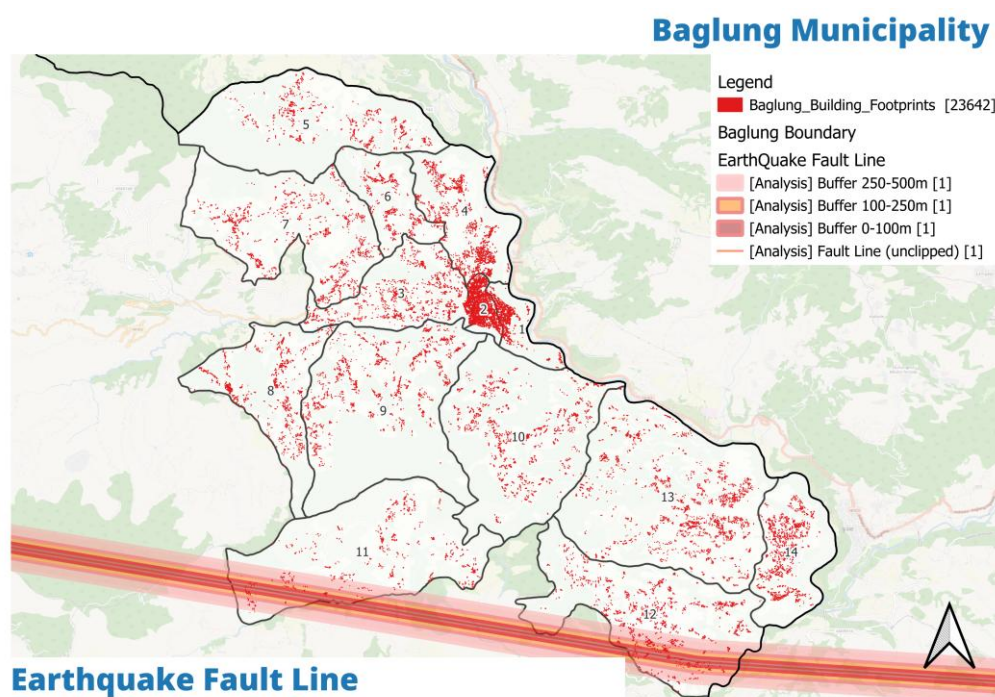


Figure 4.4. Fault lines and risk buffers, the seismic constraint on new development.

4.5 SWOT synthesis

Each sector chapter in the second presentation carried its own SWOT. This section condenses the cross sector picture because the plan level decisions must be read together.

Table 4.7. Cross sector SWOT synthesis

Strengths	Weaknesses
Gateway location on two highways, 2 hours from Pokhara	13 percent blacktop, 62 percent earthen roads
Trade hub with 1,219 registered firms, Ward 2 at 44.5 percent	Youth drain, 14.4 percent of residents absent abroad
Provincial hospital and 140 beds	No sewerage, no treatment plant, no public toilets
3,215 ha forest, zero waste programme, ALK Eco partnership	8 of 14 wards without formal waste collection
72 local laws, LISA score 84, sister city partnership	Planning and GIS staff vacancies, weak spatial database
Tourism demand at Panchakot and the temples	Fiscal dependence, 70.8 percent of budget external

Source: Baglung IUDP team synthesis of sector SWOTs, 2082 BS.

Table 4.8. Cross sector opportunities and threats

Opportunities	Threats
River and adventure tourism on the Kali Gandaki	Monsoon floods and corridor landslides each year
Agro processing and the orange economy	Climate intensified rainfall and drought
PPP capital for tourism and utilities	Federal grant contraction, budget fell 12.2 percent
GIS property tax and digital revenue	TDF debt service of NPR 3.50 crore a year

Paperless governance and e services	Political turnover breaking multi year plans
Cable car and heritage circuit demand	Competition from Pokhara and Kushma

Source: Baglung IUDP team synthesis of sector SWOTs, 2082 BS.

4.6 Development concept

The analysis converges on a simple spatial logic. Protect the core, grow the corridor, hold the hills. The development concept in this plan zones the municipality into the urban core of Wards 1 to 4, the growth corridor of Wards 13 and 14 along the highway, and the agricultural and forest belt of Wards 5 to 12.

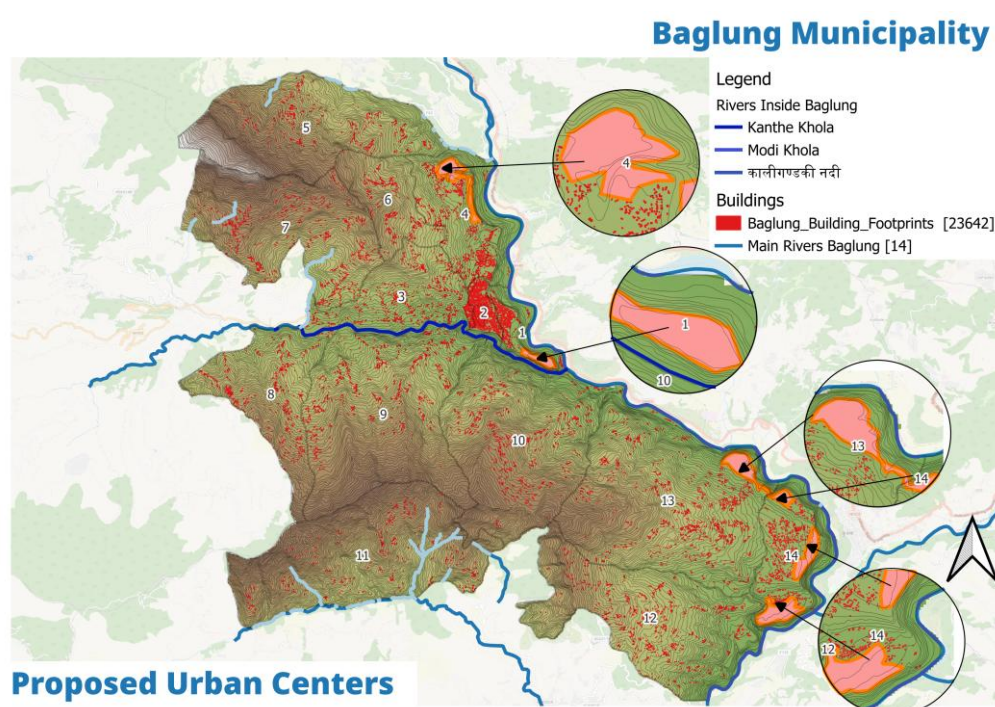


Figure 4.5. Proposed development concept 2026 to 2041. The plan concentrates investment in the core and the corridor.

The concept is the answer to the four forces. The core absorbs the fragmentation demand with infill and rental housing. The corridor absorbs the road and tourism investment where the land is suitable. The hills hold the forest, the farm and the ageing population with targeted services rather than scattered capital. Every programme in Chapter 5 can be located on this map.

4.7 Ward level development potential and constraints

Table 4.9. Ward level development potential and constraints

Ward	Population	Density (per sq km)	Key strength	Key weakness	Priority sector
1	4,746	3,414	Gorge frontage, river access	Flood zone, narrow ROW	DRR, tourism
2	7,318	10,164	Trade hub, 267 firms, hospital	Bazaar congestion, floods	Physical, economic

3	9,829	2,194	Largest population, fish production	Low density services	Social, physical
4	4,892	1,090	Highway corridor, cable car base	Limited facilities	Tourism, housing
5	2,005	228	180 ha Malika forest, pangolin	Flood hazard, remote	Environment, DRR
6	2,489	844	Orange economy, 1 crore crop	Limited road access	Economic, tourism
7	3,092	393	Agricultural potential	Ageing, youth drain	Social, economic
8	2,292	417	Livestock production	Child marriage 28.8%	Social
9	3,323	279	Spices and herbs	Ageing, remoteness	Social, economic
10	3,077	283	Baraha Lake, 11 homestays	Homestays only 4 operating	Tourism, social
11	1,587	143	Highest age dependency	Smallest ward, youth drain	Social
12	3,933	399	Hazard exposed, fish production	One of most hazard prone	DRR, economic
13	4,547	330	Highway, agro processing potential	Landslide corridor	Economic, physical
14	2,972	683	Corridor road, bazaar edge	Annual landslides	Physical, DRR

Source: Baglung IUDP team analysis, PDP, BCCI and EnDP sheets.

4.8 Baglung against national and regional norms

Table 4.10. Baglung vs national and regional benchmarks

Indicator	Baglung	National	Gandaki Province	Gap assessment
Population growth rate	minus 0.3% (2011 to 2021)	plus 0.92%	plus 0.5%	Severe decline, outmigration driven
Sex ratio	86.9 males per 100 females	95.6	91.2	Below province and national, male exodus
Literacy rate	83.5%	76.3%	78.5%	Above national, female gap 14 points
Household size	3.52	4.18	3.95	Fragmentation faster than national trend
Aged 60 plus	13.2%	10.2%	11.8%	Above national and province, ageing faster
Tap water coverage	88.7%	78.3%	82.5%	Above national but

				no treatment
Grid electricity	98.6%	96.8%	97.2%	Near universal, gap in remote wards
Road blacktopped	13%	35%	28%	Severe gap, below province average
Birth registration	62%	75%	70%	Below national, 284 unregistered per year
Female headed households	46.4%	32.5%	38.2%	Very high, migration driven
Own source revenue share	29.2%	40%	35%	Below national target, improving
School consolidation needed	89 schools, declining	National trend	Province trend	Over supplied estate for shrinking cohort

Source: Baglung IUDP team comparison, NPHC 2021, NSO 2023, DUDBC norms.

5. Thematic development plans

This chapter holds the eight thematic plans of the IUDP. Each plan follows one discipline, from goal and strategy through problem, objective and alternative analysis to the programme, the logical framework, the risk response and the phased cost. The plans are numbered 5.1 to 5.8 and are read with the demand forecasts of Chapter 4.

5. Physical Development Plan

5. Goal, objectives and strategy

The goal of the physical plan is a flood resilient, connected and serviced municipality. Its purpose in the first phase is concrete, a bazaar that does not flood and fourteen wards that are all on the motorable network. The strategy rests on three moves.

- Pool the NPR 6.40 crore ward allocations and the NPR 4.00 crore municipal pool into the two trunk works, the bazaar flood control and the Ward 9, 10 and 11 road extension, instead of splitting them into tukra parcels.
- Sequence the works so the drainage and the road corridor are built together, because opening the same trench twice is the classic waste of hill town budgets.
- Standardise the corridor as it is rebuilt, reserving the right of way lines the bylaws of Chapter 8 will protect.

Strategic priority. Flood proof the bazaar and connect the unserved wards, then standardise the corridor.

5. Present condition and constraints

The physical sector carries the heaviest gaps and the clearest geography. The bazaar core of Wards 1 to 4 runs on 5 to 8 metre rights of way against the 10 to 30 metre standards, the bazaar floods every monsoon from hillside runoff, and only 13 percent of the 322 kilometre road network is blacktopped (Nepal Urban Road Standard, 2011).

Table 5.1. SWOT analysis, Physical Development Plan

	Positive	Negative
Internal strengths	322 km road network with 13 percent blacktopped, 88.7 percent tap water coverage, 98.6 percent grid electricity, Mid-Hill Highway and Kali Gandaki corridor crossing the municipality, Ward 2 bazaar as the regional trade hub	5 to 8 metre rights of way against 10 to 30 metre standards, bazaar floods every monsoon from hillside runoff, no sewer network and no treatment plant, only 5 MLD system capacity against 6.9 MLD demand, 59 crashes with 44 fatalities in three years
Internal weaknesses	8 of 14 wards lack formal waste collection, no air or water quality monitoring stations, fragmented ward budgets split into tukra yojana parcels, planning and GIS positions sit vacant, 70.95 percent budget utilisation rate	Ward 9, 10 and 11 unserved by all weather road, 11.3 percent households off the tap, no public toilets, no dedicated water treatment plant, under execution of capital budget
External opportunities	Federal DRRM grants for flood control and corridor stabilisation, Town Development Fund debt facility for trunk works, Mid-Hill Highway upgrade programme, smart city budget for CCTV and underground utilities, PPP potential for bus park and water supply	Federal grants shrank 14.5 percent in FY 2083/84, contractor capacity limited in hill districts, climate change increasing monsoon intensity, land acquisition delays in the bazaar core
External threats	Kali Gandaki flood hazard with increasing monsoon intensity, corridor landslides in Ward 14 blocking the region lifeline road, Pangre Khola flash flood risk in Ward 5, Ward 12 recorded as one of the most hazard prone wards, seismic risk across the Mid-Hill belt	Federal fiscal transfers declining, TDF debt on Davgara bus park commits NPR 3.50 crore a year, population decline reducing the grant base, speculative land prices in the corridor

Source: Baglung IUDP team analysis from PDP, EnDP, municipal records and field survey, 2082 BS.

The plan also carries the proposals the community raised in the ward discussions of 2082 BS. The register below lists each proposal against the plan response and the section where it is addressed. Proposals the plan defers, such as the new Baglung to Myagdi road link, are recorded honestly as deferred with their reason, not silently dropped.

Table 5.2. Community proposals register, Physical Development Plan

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Include forest area in the land suitability map	Adopted, the multi criteria model already masks forest from the developable classes	Chapter 4.4 land suitability
Identify 3 to 4 named road projects and 1 to 2 road safety projects	Adopted, the ward priority matrix names the corridor and feeder works and the blackspot programme	Roads and transport, this chapter
Identify distant boring sources for drinking water	Adopted as part of the Kathekhola intake upgrade and reservoir siting study	Water supply, this chapter
Propose a road or suspension bridge	Deferred, outside municipal jurisdiction, referred to the provincial	Plan review 2031

toward the Myagdi side	road authority with the plan review	
Fix public bus station spots and publish a time schedule	Adopted, Davgara terminal routing and scheduling enforced as the logistics node	Roads and transport, this chapter
Analyse school proximity after mergers and ease transport access	Adopted, consolidation plan carries a transport guarantee and route check per merged school	Social Development Plan 5.2
Provide under road pipeline for drainage where roads are rebuilt	Adopted, trunk drains are trenched together with the corridor blacktop, one excavation	Storm drain programme, this chapter
Make core market road works inclusive with pedestrian sidewalks	Adopted, footpath and street lighting line covers 20 km of core sidewalks	Roads and transport, this chapter

Source: Baglung IUDP ward discussion notes, 2082 BS, transcribed in the working file assets ideas. Plan response by Baglung IUDP team.

5. Problem analysis

The problem chain runs from four causes to one core problem to four effects. The narrow rights of way, the missing trunk drains, the thin blacktop share and the water supply shortfall together explain why the bazaar core floods annually and fails to offer all weather mobility. The effects are the annual flood damage across Wards 1 to 4, the 74.6 percent crash fatality rate the district police recorded over three years, the 11.3 percent of households still off the piped network with no sewerage anywhere, and the business disruption the annual flooding costs the bazaar. The chain matters because it shows the flood control works and the road programme are one problem, not two.

PROBLEM ANALYSIS: THE PROBLEM TREE

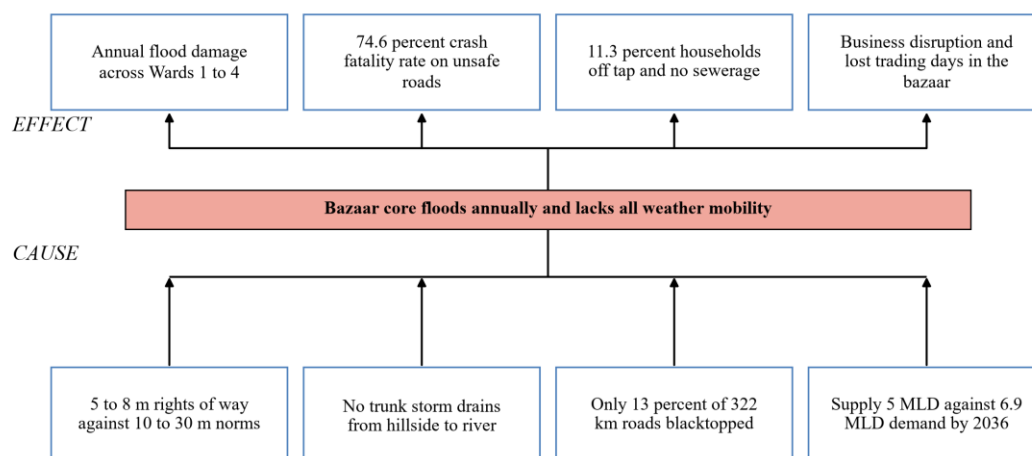


Figure 5.1. Problem analysis tree, Physical Development Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

Turning the chain positive gives the objective tree. The core objective, a flood free, connected and serviced urban core by 2031, is reached through four means that mirror the four causes, the 12 kilometres of trunk drains with 15 kilometres of hillside catch drains, the 60 kilometre blacktop with 40 kilometres of feeder upgrades, the Kathekhola treatment upgrade with three new reservoirs, and the 25 kilometre core sewer with its treatment plant. The ends are the four measurable states, zero flood

damage to the core, every ward on an all weather road, 98 percent tap coverage with metering, and a core sewerage plant treating two million litres a day.

OBJECTIVE ANALYSIS

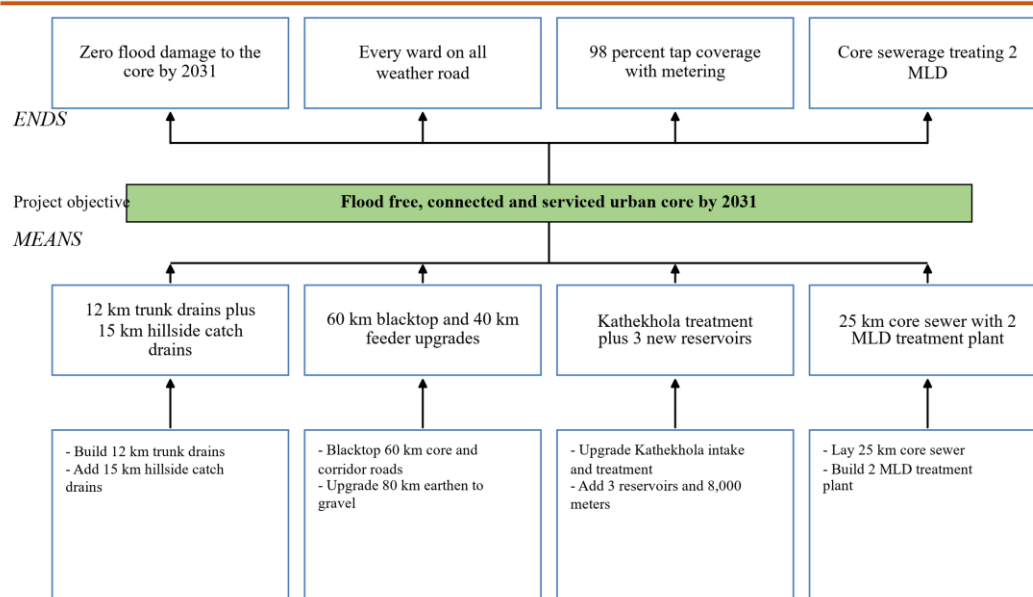


Figure 5.2. Objective analysis tree, Physical Development Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Three delivery options were scored against five criteria. Continuing the ward by ward tukra parcels scores low on every efficiency criterion because it fragments the same money the corridor needs. A full conventional sewer across all 98 square kilometres fails the cost test for a hill town of this density. The pooled corridor programme is the balanced choice, and it is the one this plan adopts.

Table 5.3. Alternative options scored against five criteria, Physical Development Plan

Criterion	A. Ward by ward tukra parcels	B. Pooled corridor programme	C. Full conventional sewer
Cost efficiency	Low	Medium	Low
Chance of success	Low	High	Medium
Speed of delivery	Medium	Medium	Low
GESI impact	Low	High	Medium
Environmental risk	Medium	Medium	Low
Total score (1 to 3 per criterion)	7	12	7

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Ward by ward tukra parcels	Low	Low	Medium	Low	Medium	7
Pooled corridor programme	Medium	High	Medium	High	Medium	12
Full conventional sewer town wide	Low	Medium	Low	Medium	Low	7

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.3. Alternative analysis heat grid, Physical Development Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

5. Roads and transport

The road programme has three tiers. First, the trunk works, the bazaar flood control with its drainage and the corridor road standardisation. Second, the ward road upgrades, blacktop for the 60 kilometres that carry the daily traffic and the school and market routes. Third, the maintenance regime, small pothole repair machinery already budgeted for FY 2083/84 and an annual resealing line.

Table 5.4. Road programme at unit rates

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Blacktop of core and corridor roads	60 km	1.5 crore per km	90.00
Gravel to blacktop of feeder links	40 km	1.2 crore per km	48.00
Earthen to gravel upgrade	80 km	0.45 crore per km	36.00
Bazaar trunk storm drains with flood walls	12 km	2.5 crore per km	30.00
Hillside catch drains and check dams	15 km	0.8 crore per km	12.00
Footpaths and street lighting, core	20 km	0.6 crore per km	12.00
Davgara bus park terminal works and routing	lump sum	lump sum	8.00
Maintenance machinery and annual resealing	5 years	lump sum	10.00
Total road and drainage			246.00

Source: Baglung IUDP team unit rate estimates, DoR district road rates and municipal rate schedule FY 2083/84. Planning stage accuracy plus or minus 30 percent.

The road safety record demands the traffic engineering line. The district police recorded 59 crashes, 44 fatalities and 119 injuries over three years, a 74.6 percent fatality rate per crash. The plan therefore

adds blackspot treatment, speed tables at school fronts and the CCTV traffic management already in the smart city budget.

Table 5.5. Ward road priority classification

Ward	Existing surface (km)	Blacktop (km)	Priority tier	First phase action
1	8.5	4.2	Tier 1	Blacktop remaining, flood drainage
2	12.3	8.1	Tier 1	ROW standardisation, footpaths
3	25.6	5.8	Tier 1	Core road blacktop, storm drains
4	18.2	4.5	Tier 1	Corridor road blacktop
5	15.4	0.8	Tier 3	Gravel upgrade, hill catch drains
6	12.8	1.2	Tier 2	Gravel to blacktop feeder links
7	22.1	1.5	Tier 3	Earthen to gravel, check dams
8	18.7	1.0	Tier 3	Gravel upgrade, flood protection
9	28.5	2.1	Tier 3	Earthen to gravel, slope stabilisation
10	25.3	1.8	Tier 3	Gravel upgrade, access to lake
11	20.1	0.9	Tier 3	Earthen to gravel, hill trails
12	24.6	2.5	Tier 2	Blacktop main access, drains
13	45.2	6.8	Tier 2	Corridor blacktop, landslide works
14	45.1	7.9	Tier 2	Corridor blacktop, landslide bio engineering

Source: Baglung IUDP team GIS road audit and municipal inventory. Tier 1 is bazaar core, Tier 2 is corridor, Tier 3 is hill wards.

Table 5.6. Storm drain programme by section

Section	Length (km)	Type	NPR crore	Priority
Bazaar trunk drains with flood walls	12	Concrete lined, 600 mm to 900 mm	30.00	Immediate
Hillside catch drains and check dams	15	Stone pitched, 400 mm to 600 mm	12.00	Phase 1
Corridor road side	8	Concrete, 300 mm	6.40	Phase 2

drains				
Ward 14 landslide diversion drains	3	Heavy duty, debris resistant	4.50	Phase 1
Ward 5 Pangre Khola bank drains	2	Stone pitched, 500 mm	3.20	Phase 1
Total	40		56.10	

Source: Baglung IUDP team estimates on the municipal drainage survey and GIS flood rasters.

5. Water supply

The service is strong on coverage and weak on treatment and storage. The norm is 80 to 100 litres per capita per day with metered connections and storage at 25 percent of treatment capacity (DUDBC, 2013). The municipality serves about 6.9 million litres a day at 120 lpcd of demand for the 2036 household line, against the current system capacity of roughly 5 million litres a day with no dedicated treatment plant.

Table 5.7. Water supply programme at unit rates

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Extension of gravity schemes to unserved wards	1,200 connections	0.25 lakh per connection	3.00
Kathekhola intake upgrade and treatment units	1 system	lump sum	12.00
Reservoir and distribution expansion	3 new reservoirs	4 crore each	12.00
Metering of bazaar connections	8,000 meters	0.04 lakh each	3.20
Ward 12 and 9 unimproved source replacement	1,100 connections	0.30 lakh per connection	3.30
Rainwater harvesting in public buildings	40 buildings	15 lakh each	6.00
Total water			39.50

Source: Baglung IUDP team unit rate estimates, DWSS norms and municipal records. Planning stage accuracy plus or minus 30 percent.

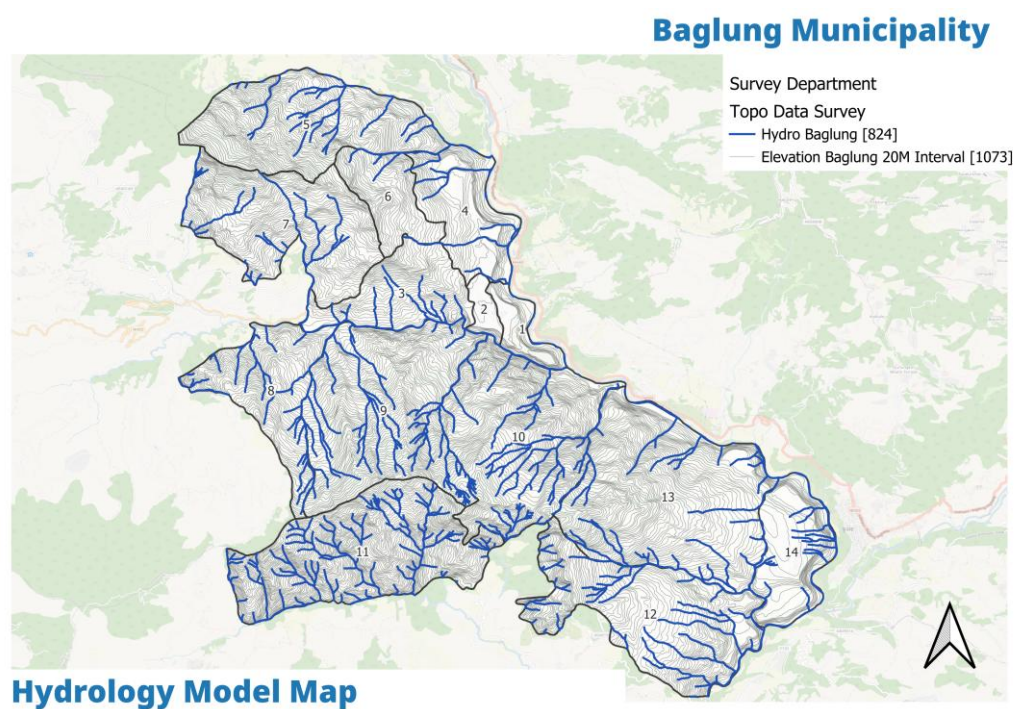


Figure 5.4. Drainage and water resources model of the municipality.

Table 5.8. Ward wise water demand at 120 lpcd, 2036 projection

Ward	Households 2036	Population 2036	Demand (MLD)	Current supply (MLD)	Gap (MLD)
1	1,410	4,860	0.58	0.35	0.23
2	2,300	7,550	0.91	0.70	0.21
3	2,880	10,100	1.21	0.85	0.36
4	1,360	5,020	0.60	0.40	0.20
5	560	2,060	0.25	0.10	0.15
6	690	2,560	0.31	0.12	0.19
7	900	3,180	0.38	0.15	0.23
8	690	2,350	0.28	0.10	0.18
9	960	3,410	0.41	0.12	0.29
10	880	3,160	0.38	0.10	0.28
11	460	1,630	0.20	0.05	0.15
12	1,180	4,040	0.48	0.25	0.23
13	1,380	4,670	0.56	0.30	0.26
14	840	3,050	0.37	0.15	0.22
Total	16,490	57,640	6.92	3.64	3.28

Source: Baglung IUDP team projection at 120 lpcd DUDBC norm, household size 3.5, 2036 adopted path. Ward supply figures are field estimates, the system capacity headroom is about 5 MLD against the 3.64 MLD delivered. Ward projections are independent estimates and sum slightly below the municipal adopted path of 58,087, about 16,600 households.

5. Sanitation, drainage and solid waste

The municipality has no sewer network, no treatment plant and no public toilets. The first phase therefore builds a core sewer with a decentralised treatment plant, because a full conventional sewer for the whole 98 square kilometres is neither affordable nor appropriate for a hill town. The DUDBC norm of 0.2 to 0.75 hectare per MLD for treatment guides the plant sizing.

Table 5.9. Sanitation and waste programme at unit rates

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Core sewer network, Wards 1 to 4	25 km	0.8 crore per km	20.00
Decentralised treatment plant	2 MLD	6 crore per MLD	12.00
Public toilets at bus park, bazaar, temples	12 units	30 lakh each	3.60
Community septic and soakage programme	3,000 households	0.15 lakh each	4.50
Solid waste vehicles and containers	4 compactors plus bins	lump sum	8.00
Transfer station at Odarchaur	1 site	lump sum	3.00
Sanitary landfill with recycling platform	1 ha	lump sum	8.00
ALK Eco incinerator, 1 to 3 tonnes per day	1 unit	lump sum	1.20
Total sanitation and waste			60.30

Source: Baglung IUDP team unit rate estimates and the municipal waste programme records, 2082 BS.

5. Housing

Housing demand rises from fragmentation, not growth. The demographic analysis adds 700 to 1,100 dwelling units by 2036, and the plan sites them in the core and the corridor where the land suitability map is favourable. The core absorbs infill and rental housing, the corridor absorbs the family plots. The plan proposes density zoning for Wards 1 to 4 with plot rationalisation, and a municipal land bank in the corridor to prevent speculative prices.

Table 5.10. Housing programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Infill and rental housing in the core	500 units	25 lakh per unit	125.00
Affordable plots near campuses	300 units	18 lakh per unit	54.00
Density zoning and plot rationalisation	planning work	lump sum	1.50
Municipal land bank in the corridor	10 ha	lump sum	25.00

Total housing			205.50
---------------	--	--	--------

Source: Baglung IUDP team estimates, DUDBC housing norms and municipal land records. Private sector share is significant.

5. Electricity and telecommunications

The grid reaches 98.6 percent of households. The remaining 1.4 percent and the backup duty fall to solar, and the FY 2083/84 budget already commits to smart street lighting and underground utilities in the core. The plan keeps this line and adds solar for public buildings, which serves the zero waste incinerator and the future cable car station.

5. Logical framework

Table 5.11. Logframe matrix (LFM), Physical Development Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Flood resilient, connected and serviced municipality		Zero flood damage events in the core, all wards motorable by 2031	Municipal annual report and scorecard	R1: Federal grants shrink further (Medium probability, High impact)
Project Purpose Bazaar flood free and every ward connected by 2031	•	Bazaar flood free each monsoon from 2030, 60 km blacktopped	Municipal annual report, GIS road audit, ward service records	R2: Contractor capacity limited in hill district (Medium probability, Medium impact)
Expected Outputs (Results) - Trunk drainage and flood walls complete - Corridor and ward roads upgraded - Water, sewer and waste at norm	•	12 km drains, 60 km blacktop, 98 percent tap coverage	Municipal annual report, GIS road audit, ward service records	R3: Land acquisition delays in the core (High probability, Medium impact)
Activities - Build 12 km trunk drains - Blacktop 60 km core and corridor roads - Lay 25 km core sewer		Works completed per approved annual programme	Project completion reports	R4: Monsoon intensity exceeds design storm (Medium probability, High impact)
Inputs NPR 226.0 crore phase one 2026 to 2031 of NPR 551.3 crore over three phases, municipal, federal and TDF sources		Budget utilisation above 85 percent	Budget red book and financial reports	R5: Ward committees resist pooling (Medium probability, Medium impact)

Source: Baglung IUDP team, 2082 BS.

5. Assumptions and risk response

The logical framework carries six planning assumptions. Each is scored on the probability of failure and the expected impact, and the matrix assigns the response, from ignore through monitor and mitigate to a mitigation with a contingency plan. No assumption of this sector falls in the killer cell, but two sit in the red band and are managed with named contingencies.

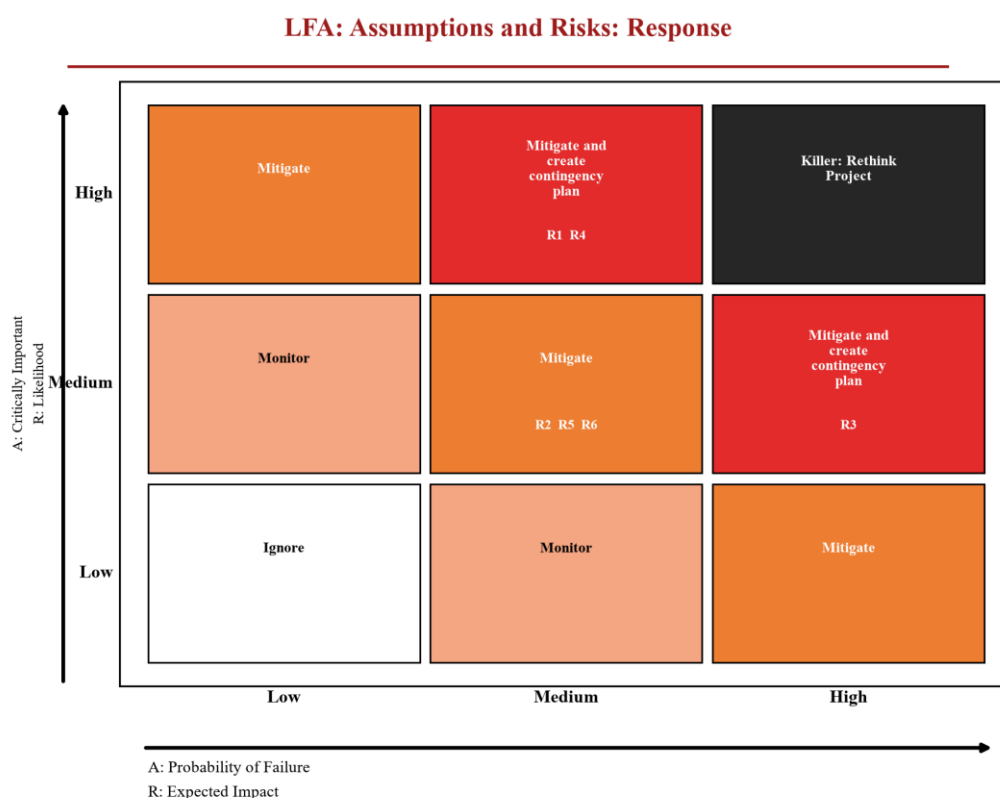


Figure 5.5. Assumptions and risks response matrix, Physical Development Plan. Baglung IUDP team, 2082 BS.

Table 5.12. Risk register, Physical Development Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Federal grants shrink further	Medium	High	Mitigate and create contingency plan	Phase the trunk works so each year is fundable alone, reserve the TDF window, finance section
R2	Contractor capacity limited in the hill district	Medium	Medium	Mitigate	Pre qualify in advance, package works at corridor scale, municipal works section
R3	Land acquisition delays in the core	High	Medium	Mitigate and create contingency plan	Start negotiation a year ahead of construction, use the land bank for staging, planning section

R4	Monsoon intensity exceeds the design storm	Medium	High	Mitigate and create contingency plan	Design drains to a 20 year return period, keep the DRRM contingency line, DRRM committee
R5	Ward committees resist pooling	Medium	Medium	Mitigate	Sign the pooling agreement before the budget call, publish ward benefits annually, executive office
R6	Cost escalation beyond plus 30 percent	Medium	Medium	Mitigate	Annual unit rate revision, multi year contracts with escalation clauses, finance section

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.13. Implementation summary, Physical Development Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Bazaar flood control, trunk drains, core and corridor blacktop, water treatment and metering, core sewer start	226.0
Phase 2	2031 to 2036	Ward 9, 10 and 11 road completion, corridor standardisation, sewer extension, corridor housing	180.0
Phase 3	2036 to 2041	Residual feeder upgrades, maintenance consolidation, second fire station siting works	145.3
Total			551.3

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent.

5. Conclusion

The physical plan is the trust builder of the whole IUDP. If the bazaar stops flooding and the unserved wards get their road in the first phase, the municipality will have earned the credibility to attempt the tourism wager of the second phase. The programme is priced at NPR 551.3 crore over fifteen years, front loaded into a first phase of NPR 226.0 crore, and every line traces to a norm gap measured in Chapter 4.

5. Social Development Plan

5. Goal, objectives and strategy

The goal of the social plan is social services of equal quality across all wards. Its purpose in the first phase is a hospital with its specialists at post, a school estate matched to the children who actually exist, and a protection system that registers every birth and defends every girl. The strategy rests on three moves.

- Right size before building. The child cohort is falling 26 percent by 2031, so the plan consolidates and reuses before it constructs.
- Buy staff before beds. Beds are adequate, the missing specialties are not, so the money goes to eight salary lines that change what the hospital can treat.
- Tie women's training to the tourism and homestay value chain so that skills convert into monetised, year round income rather than certificates.

Strategic priority. Close the specialist staffing gap at Dhaulagiri Hospital and link women's skill training directly to the tourism and homestay value chain so that training converts into monetised, year round income.

5. Present condition and constraints

Baglung is one municipality with three social geographies, the dense core, the peri urban band and the ageing hills. The population is declining with ageing, so the services must right size, not grow. The institutional gaps, registration, inclusion and geriatric care, are larger than the physical ones.

Table 5.14. SWOT analysis, Social Development Plan

	Positive	Negative
Internal strengths	Dhaulagiri Provincial Hospital with 140 beds, 89 schools carrying 13,098 students, 83.5 percent literacy rate, 12 health facilities across the municipality, strong community institutions with 43 registered forest user groups	Hospital staffing critically short on specialists, birth registration at only 62 percent, child marriage at 19.9 percent below age 18, disability register undercounts at 2.9 percent, Ward 8 child marriage at 28.8 percent
Internal weaknesses	Three distinct social geographies with unequal service quality, child cohort declining 26 percent from 9,986 to 7,406 by 2031, school estate built for the old cohort, 48 suicides over three years, 42.8 percent crime rise	No geriatric care infrastructure in ageing wards, Ayurvedic hospital staffing crisis, no telemedicine network, no mental health hotline, girls dropping out after child marriage
External opportunities	Federal health and education grants at norm, 15th Plan target of 90 percent literacy, telemedicine technology now affordable, women skill training linked to tourism and homestay value chain, school consolidation freeing classrooms for preschools	Population decline reducing the student base, youth emigration hollowing the working age cohort, dengue climbing from 85 to 1,120 cases in two years, climate change increasing vector borne disease risk
External threats	Child marriage entrenched in rural wards despite legal age of 20, widow share of 11 to 13 percent in rural wards with limited social security, crime concentrated in Wards 1, 2, 3, 4 and 9, drug use rising among youth, remittance dependency creating	Federal health budget uncertain, specialist recruitment competing with Kathmandu and Pokhara, community resistance to school consolidation, ageing population increasing the care burden

	speculative consumption	
--	-------------------------	--

Source: Baglung IUDP team analysis from SDP, NPHC 2021, field survey and demographic analysis, 2082 BS.

5. Problem analysis

The problem chain starts from four causes, the vacant specialty posts, a school estate sized for a cohort that has shrunk 26 percent, birth registration stalled at 62 percent, and the absence of any geriatric care in the wards that are already past 16 percent elderly. Together they produce the core problem, social services of uneven quality across the three geographies. The effects are visible in the record, dengue climbing from 85 to 1,120 cases in two years, 284 births unregistered every year, 19.9 percent of girls married below 18, and 48 suicides in three years.

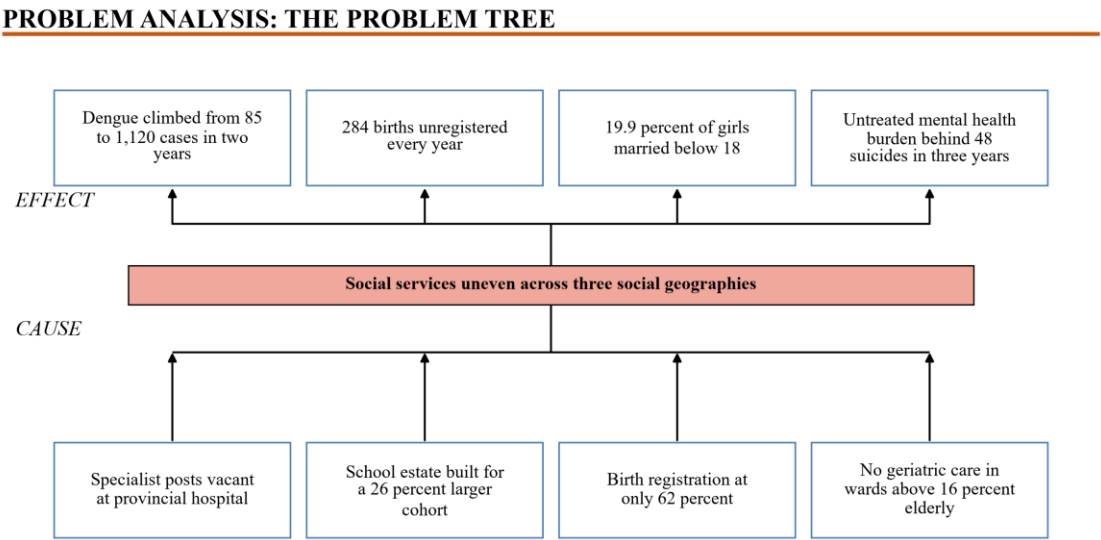


Figure 5.6. Problem analysis tree, Social Development Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree inverts the chain. The core objective, equal quality health, education and protection in every ward, is pursued through four means, filling the eight specialty posts and four birthing centres, consolidating twelve schools and converting their classrooms, running mobile registration with marriage age enforcement committees, and building the third old age home with five home care networks. The ends are measurable, dengue below 300 cases a year, birth registration at 100 percent, and elders and disabled residents served in place.

OBJECTIVE ANALYSIS

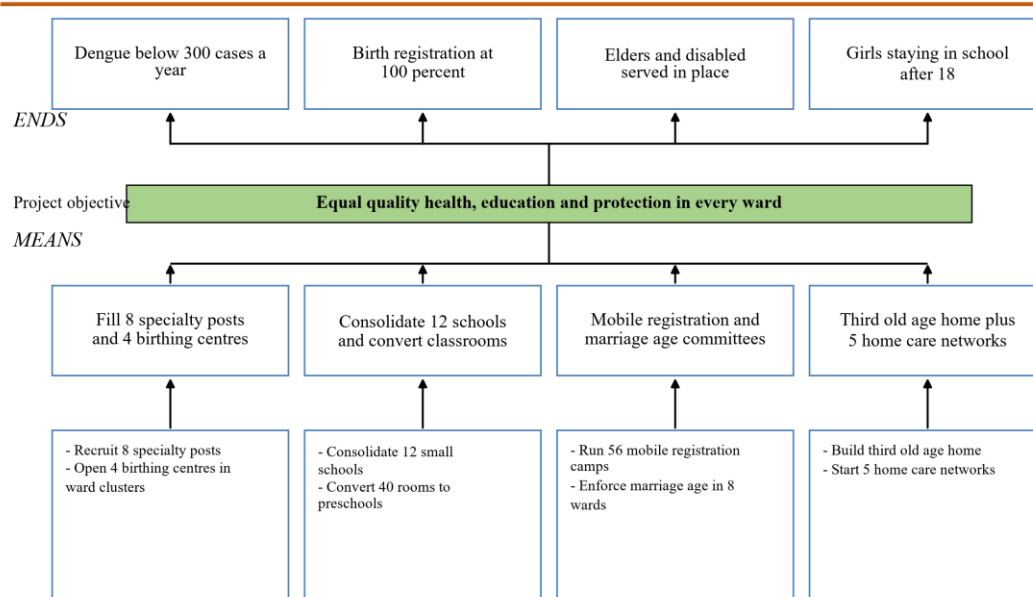


Figure 5.7. Objective analysis tree, Social Development Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Three strategies were scored. Building new facilities in every ward fails the cost test against a shrinking cohort. Referring everything to the provincial hospital fails the access test for the hills. Right sizing and staffing the existing estate wins on cost, success probability and inclusion, and it is the strategy adopted.

Table 5.15. Alternative options scored against five criteria, Social Development Plan

Criterion	A. New facilities in every ward	B. Right size and staff the estate	C. Refer all to the hospital
Cost efficiency	Low	High	Medium
Chance of success	Medium	High	Low
Speed of delivery	Low	Medium	High
GESI impact	Medium	High	Low
Environmental risk	Medium	High	Low
Total score (1 to 3 per criterion)	8	14	8

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Build new facilities in every ward	Low	Medium	Low	Medium	Medium	8
Right size and staff the existing estate	High	High	Medium	High	High	14
Refer all cases to the provincial hospital	Medium	Low	High	Low	Low	8

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.8. Alternative analysis heat grid, Social Development Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

5. Education

The child cohort aged 5 to 14 falls from 9,986 in 2021 to about 7,406 by 2031, a drop of 26 percent. The school estate of 89 schools was built for the old cohort. The plan therefore consolidates the small rural schools under 300 students, converts surplus classrooms into preschools and community learning rooms, and targets the female and rural adult literacy gap that keeps the municipal rate at 83.5 percent against the 15th Plan target of 90 percent.

Table 5.16. Ward wise school consolidation plan

Ward	Schools	Students	Student:teacher	Below 300 students	Action
1	5	520	12.5	1	Merge 1, convert to preschool
2	10	3,250	19.6	0	Retain, right size classes
3	9	2,480	14.2	1	Merge 1, STEM lab
4	6	1,090	11.1	1	Merge 2, convert to community learning
5	5	310	8.4	2	Merge to 1, transport support
6	5	440	9.7	0	Retain, add preschool
7	6	620	10.4	1	Merge 1, adult literacy hub
8	5	480	11.2	0	Retain, add digital lab
9	8	780	11.3	1	Merge 1, keep secondary
10	6	660	11.2	1	Retain, add library

11	5	230	6.0	2	Merge to 1, transport support
12	7	820	12.0	0	Retain, STEM lab
13	7	990	14.8	1	Merge 1, add skills lab
14	5	428	11.9	1	Retain, digital lab
Total	89	13,098		12	12 schools consolidated

Source: SDP field survey 2082 BS. 12 schools below 300 students eligible for consolidation.

Table 5.17. Education programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
School consolidation and transport support	12 schools merged	0.8 crore each	9.60
Classroom conversion, preschools and libraries	40 rooms	15 lakh each	6.00
Adult literacy and digital classes	60 batches	2 lakh each	1.20
STEM and skills labs in secondary schools	6 schools	40 lakh each	2.40
Total education			19.20

Source: Baglung IUDP team estimates on the SDP school inventory, 2082 BS.

The ward discussions added a strong skills and learning voice, and the plan carries it. The community proposals register below lists each education and youth proposal with the plan response. The adventure instructor line is the standout, certification in bungy operations, rafting guiding and cable car maintenance feeds the tourism flagship jobs directly, and it is funded within the skills lines of the economic chapter.

Table 5.18. Community proposals register, education and youth

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Community library and e library provision	Adopted, classroom conversions include libraries, e library in the digital classes line	Education programme, this chapter
Adult literacy with mindset upliftment	Adopted, 60 adult literacy batches reframed to include mindset and civic content	Education programme, this chapter
Sessions on social taboos, sex education and mental health in schools	Adopted, folded into the school health and counselling programme	Health and child protection, this chapter
Online portal for problem filing with consultation and counselling	Adopted, portal scoped under the paperless governance budget with the municipal IT focal person	Institutional Development Plan 5.8
Youth skills in CAD, web design,	Adopted, course list adopted in the	Economic Development Plan 5.6

public speaking, leadership, graphic design	skills training line	
Instructor skills for bungy, rafting and cable car	Adopted, certification tied to the flagship concessions with placement	Tourism Development Plan 5.5 and Economic 5.6
Newspapers including online English papers for current affairs	Adopted at modest cost through school and library subscriptions	Education programme, this chapter
Weekly mental health counselling for youth, suicide and drug response	Adopted as the mental health hotline and counsellor line, weekly ward sessions	Sports, culture and security, this chapter
Health checkup and short isolation for returnees from abroad	Adopted as a referral protocol with the provincial hospital	Health, this chapter
Jobs for disabled youths in library, reception and ticket counters	Adopted, reserved placement quota in municipal facilities and tourism desks	Ageing, disability and GESI, this chapter

Source: Baglung IUDP ward discussion notes, 2082 BS. Plan response by Baglung IUDP team.

5. Health

Beds are adequate, staff are not. The plan supports the Dhaulagiri Provincial Hospital expansion from 140 to 200 beds and the long term 300 bed medical college, but the immediate money goes to the missing specialties, dermatology, psychiatry, ENT and pathology, and to the staffing crisis at the Ayurvedic hospital. Dengue control is a programme of its own after the climb from 85 to 1,120 cases in two years.

Table 5.19. Ward wise health staffing and birthing centre gap

Ward	Facility	Staff present	Staff norm	Gap	Birthing centre
1	Basic health centre	2	5	3	No
2	Provincial hospital + 2 clinics	45	80	35	Yes (hospital)
3	Basic health centre	2	5	3	No
4	Health post	2	4	2	No
5	Health post	2	4	2	No
6	Health post	2	4	2	No
7	Health post	2	4	2	No
8	Health post	2	4	2	No
9	Health post	2	4	2	No
10	Health post	2	4	2	No
11	Health post	1	3	2	No
12	Health post	2	4	2	No
13	Health post	2	4	2	No
14	Health post	2	4	2	No

Source: SDP sheet, Baglung IUDP DataSets. Only Ward 2 has specialist and birthing access.

The health discussions were the most specific of the whole field round, and the plan adopts their logic. The register below shows each health proposal against the plan response. The staffing incentive proposal is the most consequential, it changes the specialist retention question from a salary race the municipality cannot win into a posting package it can.

Table 5.20. Community proposals register, health

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Staff ratio survey per facility and posting incentives for hard stations	Adopted, incentive package designed on the ward staffing gap table with remote ward weighting	Health programme, this chapter
Awareness programmes for vector borne diseases	Adopted within the dengue and vector control programme	Health programme, this chapter
HIV and AIDS awareness programme	Adopted within the health awareness calendar with the hospital	Health programme, this chapter
Birthing centres by ward cluster, Wards 12, 13, 14, Wards 9, 10, 11 and Wards 5, 6, 7	Adopted, the four new birthing centres are sited on exactly these clusters	Health programme, this chapter
Telemedicine for remote wards	Adopted, 14 ward telemedicine posts in the health programme	Health programme, this chapter
Skin condition awareness	Adopted within the health awareness calendar with the dermatology post	Health programme, this chapter

Source: Baglung IUDP ward discussion notes, 2082 BS. Plan response by Baglung IUDP team.

Table 5.21. Health programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Specialist staffing at provincial hospital	8 posts, 5 years	0.5 crore per year	2.50
Birthing centres in wards without them	4 wards	1.0 crore each	4.00
Dengue and vector control programme	5 years	0.6 crore per year	3.00
Telemedicine and referral network	14 ward posts	0.2 crore each	2.80
Geriatric beds and day care at hospital	20 beds plus unit	lump sum	3.00
Total health			15.30

Source: Baglung IUDP team estimates and the SDP health survey, 2082 BS.



Figure 5.9. Health post patient room with beds, the ward level service base. Photo: Baglung Group field team, 2082 BS.



Figure 5.10. Field team at the Dhaulagiri Ayurved Hospital, the facility whose staffing crisis the health programme addresses. Photo: Baglung Group field team, 2082 BS.

5. Child protection and registration

Birth registration sits at about 62 percent, leaving 284 births a year unregistered. Girls marry below the legal age of 20 in every ward, with 19.9 percent married below 18 and Ward 8 at 28.8 percent. The plan treats both as institutional programmes with targets. Mobile registration camps, school and hospital doorstep registration, marriage age enforcement committees in the high prevalence wards and re enrolment guarantees for girls.

Table 5.22. Child protection programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Mobile birth registration camps	56 camps	0.5 lakh each	0.28
Doorstep registration in hospitals and schools	14 ward systems	0.2 crore each	2.80
Child marriage enforcement and awareness	8 wards, 5 years	0.3 crore each	2.40
Re enrolment and economic alternatives for girls	600 girls	0.2 lakh each	1.20
Total child protection			6.68

Source: Baglung IUDP team estimates on NPHC 2021 ward data.

5. Ageing, disability and inclusion

The 60 plus share crosses 20 percent by 2036 and Wards 9 to 13 are already above 16 percent. The plan adds the third old age home the norm requires, plus day care and home care networks in the ageing wards. The disability register at 2.9 percent undercounts, so the plan funds a ward level enumeration and accessible footpaths at the public buildings. The 46.4 percent female headed households get childcare, safety and home enterprise support, and the widow share of 11 to 13 percent in the rural wards gets social security outreach.

Table 5.23. Ageing, disability and GESI programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Old age home and day care centre	1 plus 2 units	3.0 crore each	9.00
Home care networks in Wards 9 to 13	5 ward networks	0.6 crore each	3.00
Disability enumeration and ID drive	14 wards	0.15 crore each	2.10
Accessible footpaths and ramps	12 km	0.3 crore per km	3.60
Childcare centres near markets	6 centres	0.5 crore each	3.00
Women's enterprise and market linkage	5 years	1.0 crore per year	5.00
Total ageing, disability and GESI			25.70

Source: Baglung IUDP team estimates, LGO 2074 Section 24 duty and SDP field work.

The women, men and elderly discussions produced the register below. Two entries deserve emphasis. The skills continuation gap, training that exists but does not match market demand, is answered by tying every course to the placement system of the economic chapter. And the elderly programme is not only care, the skill sharing workshops where seniors teach traditional cooking, woodworking and local history treat the municipality's elders as an asset, not a caseload.

Table 5.24. Community proposals register, GESI, sports and inclusion

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Match skill courses to market demand so training continues into work	Adopted, placement guaranteed training seats in the economic chapter	Economic Development Plan 5.6
Training on reuse of recyclable materials	Adopted within the eco club and awareness programme of the waste system	Environmental Management Plan 5.3
Violence awareness and an online complaint window for women	Adopted, complaint window scoped with the paperless governance portal	Institutional Development Plan 5.8
Leadership and political knowledge training for women in decision making	Adopted within the GESI desk programme with the 50 percent participation target	Institutional Development Plan 5.8
Rehabilitation and upliftment schemes for abused and exploited women	Adopted within the women's enterprise and market linkage line with referral to the hospital	Ageing, disability and GESI, this chapter
Reduce child marriage and educate female children	Adopted, enforcement committees plus re enrolment guarantees	Child protection, this chapter
Attitude change programmes for men and boys from school level, end caste discrimination from the ward level	Adopted within the school health and counselling programme and ward GESI duties	Child protection and GESI, this chapter
Mayor's Cup for women, not only men	Adopted, women's tournament added to the annual sports calendar	Sports, culture and security, this chapter
Improve existing playgrounds with parking, changing rooms and toilets	Adopted within the covered hall and ground improvement line	Sports, culture and security, this chapter
E sports tournaments within and between municipalities	Adopted as a low cost annual event in the sports calendar	Sports, culture and security, this chapter
Covered halls with futsal on a private model, ramps and disabled friendly courts	Adopted, hall siting includes accessibility standard and PPP operation	Sports, culture and security, this chapter
Elderly programmes, yoga, morning exercise, chess and memory games	Adopted within the day care and home care networks	Ageing, disability and GESI, this chapter
Skill sharing workshops where seniors teach cooking, woodworking and history	Adopted within the day care programme with school linkage	Ageing, disability and GESI, this chapter
Youth volunteering in bhajan kirtan and cultural transfer	Adopted within the cultural programme calendar	Sports, culture and security, this chapter
Identify pocket areas for open space in dense wards and repair inclusive park amenities	Adopted, pocket park sites screened on the GIS in the core wards	Physical Development Plan 5.1

Source: Baglung IUDP ward discussion notes, 2082 BS. Plan response by Baglung IUDP team.

5. Sports, culture and security

Twelve of fourteen wards lack covered halls and the Mayor's Cup and Kalika Cup already draw crowds. The plan adds covered halls in Ward 2 and the Balewa cluster, and preserves the Bangechaur ground. The security line responds to the 42.8 percent crime rise and the 48 suicides over three years with ward patrols in the high crime wards 1, 2, 3, 4 and 9, a mental health hotline and an anti drug taskforce, all at modest cost.



Figure 5.11. Field team with the District Police Office, the partner for road safety and crime data. Photo: Baglung Group field team, 2082 BS.

5. Logical framework

Table 5.25. Logframe matrix (LFM), Social Development Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Social services of equal quality across all wards		Dengue below 300, literacy 90 percent, registration 100 percent by 2031	Municipal annual report and scorecard	R1: Specialist recruitment fails against Kathmandu salaries (High probability, Medium impact)
Project Purpose Health staffed, schools right sized, children and elders protected by 2031		8 specialty posts filled, 77 schools, no marriage below 18 above 5 percent	SDP annual dashboard, ward records, hospital and school reports	R2: Communities resist school consolidation (Medium probability, Medium impact)

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Expected Outputs (Results) - 8 specialty posts and 4 birthing centres filled - School estate consolidated to 77 schools - Registration at 100 percent and care networks running	●	4 birthing centres open, transport support running, 3 old age homes	SDP annual dashboard, ward records, hospital and school reports	R3: Federal health and education grants cut (Medium probability, High impact)
Activities - Recruit and retain specialists - Merge 12 small schools - Run mobile registration camps			Project completion reports	R4: Registration drive stalls on paperwork (Low probability, Medium impact)
Inputs NPR 32.0 crore phase one 2026 to 2031 of NPR 66.9 crore over three phases, federal and municipal sources		Programme utilisation above 85 percent	Budget red book and financial reports	R5: Enforcement of marriage age backlashes (Medium probability, Medium impact)

Source: Baglung IUDP team, 2082 BS.

5. Assumptions and risk response

Six assumptions carry the social plan. The heaviest is specialist recruitment, scored high probability of failure because Baglung must compete with Kathmandu and Pokhara salaries, managed with a contingency of contracted visiting specialists while the permanent posts are filled.

LFA: Assumptions and Risks: Response



Figure 5.12. Assumptions and risks response matrix, Social Development Plan. Baglung IUDP team, 2082 BS.

Table 5.26. Risk register, Social Development Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Specialist recruitment fails against Kathmandu salaries	High	Medium	Mitigate and create contingency plan	Housing incentive package plus contracted visiting specialists as bridge, hospital management
R2	Communities resist school consolidation	Medium	Medium	Mitigate	Transport guarantee and preschool conversion agreed before merger, education section
R3	Federal health and education grants cut	Medium	High	Mitigate and create contingency plan	Sequence birthing centres first, phase telemedicine, municipal executive
R4	Registration drive stalls on paperwork	Low	Medium	Monitor	Quarterly registration dashboard by ward, ward

					offices
R5	Enforcement of marriage age backlashes	Medium	Medium	Mitigate	Work through schools and mothers groups, pair enforcement with re enrolment, GESI desk
R6	Ageing outpaces the care buildout	Medium	High	Mitigate and create contingency plan	Home care networks before buildings, train family caregivers, social development section

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.27. Implementation summary, Social Development Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Specialist staffing, four birthing centres, school consolidation of 12 schools, registration drive, third old age home	32.0
Phase 2	2031 to 2036	Telemedicine completion, dengue programme continuation, home care network expansion, covered halls	21.0
Phase 3	2036 to 2041	Geriatric care consolidation, sports facility completion, programme institutionalisation	13.9
Total			66.9

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent.

5. Conclusion

The social plan spends little and changes much. For NPR 66.9 crore over fifteen years it buys the specialties that make a district hospital real, a school estate that fits its pupils, a birth certificate for every child and a care net for the wards that are growing old fastest. Its success rests on two management acts, holding the consolidation line with the communities, and keeping the specialist posts filled longer than the market wants them filled.

5. Environmental Management Plan

5. Goal, objectives and strategy

The goal of the environmental plan is an environmentally balanced and climate resilient municipality. Its purpose in the first phase is a zero waste system running in all fourteen wards and an environmental record that finally has numbers. The strategy rests on three moves.

- Scale what works. The three bin system and the community forestry model are proven in the core and in 43 user groups, so the plan extends them rather than inventing new instruments.
- Measure before managing. Two monitoring stations and a complete forest register turn the sector from anecdote to data.
- Price the service. Waste collection moves to a fee based system so the fleet pays for its own operation instead of waiting on grants.

Strategic priority. Complete the hazard mapping and monitoring gap with GIS based disaster risk mapping for Wards 5, 6, 12 and 14, and scale the zero waste system to the eight wards still without formal collection.

5. Present condition and constraints

The environment sector holds the municipality's best asset and its biggest gap. The forest estate of 3,215 hectares, anchored by the 180 hectare Malika community forest in Ward 5, is the green capital. The zero waste programme is real, with the three bin system in the core, the Samanata Abhiyan Nepal agreement and the ALK Eco incineration partnership. The gaps are equally real. Eight of fourteen wards have no formal waste collection, there is no air or water quality monitoring, and forest and disaster data are absent for roughly half the wards.

Table 5.28. SWOT analysis, Environmental Management Plan

	Positive	Negative
Internal strengths	3,215 hectare forest estate with 1,401 ha government managed, 1,802 ha community forest, 7 ha leasehold and 4 ha religious forest, 43 community forest user groups proven and active, 180 hectare Malika community forest in Ward 5 as the green anchor, three bin waste segregation system already in core wards, Samanata Abhiyan Nepal agreement in place	8 of 14 wards have no formal waste collection, no air or water quality monitoring stations exist, forest and disaster data absent for roughly half the wards, waste generation at 18 tonnes per day and climbing, ALK Eco incinerator limited to 1 to 3 tonnes per day
Internal weaknesses	No sewer network and no treatment plant, open dumping still practised in outer wards, forest fire risk in dry season, Chinese pangolin habitat in Ward 5 unprotected, river water quality unknown with no monitoring baseline	Waste composition data incomplete, recycling rates low, composting not yet operational at scale, environmental impact assessment capacity limited, climate adaptation plan not yet drafted
External opportunities	DUDBC norm of 70 percent reduce, reuse and recycle, federal climate adaptation funding, community forestry model replicable to data deficient wards, agroforestry potential on 31 percent underutilised farmland, ALK Eco partnership for hazardous	Climate change increasing monsoon intensity and flood frequency, illegal logging and encroachment pressures, riverbed extraction without EIA basis, tourism development increasing waste load in peak season

	waste	
External threats	Pangre Khola flash flood in Ward 5 killed two lives, corridor landslides in Ward 14 blocking the region lifeline road annually, bazaar flooding every year from hillside runoff, Ward 12 one of the most hazard prone wards, Kali Gandaki river bank erosion	Federal environmental grants uncertain, community forest user groups facing ageing membership, tourism growth outpacing waste management capacity, climate change accelerating flood risk in the Kali Gandaki basin

Source: Baglung IUDP team analysis from EnDP, GIS hazard rasters, field survey and municipal records, 2082 BS.

The environmental discussions contributed one genuinely new technical idea the plan adopts with enthusiasm, hanging waste carriers for the toles the collection tractor cannot reach, serviced once a week or month. The full register follows.

Table 5.29. Community proposals register, environment

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Identify a new landfill area with capacity building and a treatment facility	Adopted, landfill siting study with community benefit sharing, capacity building within the eco club line	Solid waste programme, this chapter
Awareness for the three bin system and source segregation	Adopted, the eco club and awareness programme runs the three bin campaign	Solid waste programme, this chapter
Hanging waste carriers for toles the tractor cannot reach, weekly or monthly service	Adopted as a new programme line, six carrier zones on a weekly service	Solid waste programme, this chapter
Identify disaster patches for flood and landslide and apply bio engineering	Adopted, patch identification rides on the GIS hazard rasters of Chapter 4	Disaster Risk Reduction Plan 5.4
Embankment control where the river cuts roads	Adopted within the river bank protection line on the Kali Gandaki front	Disaster Risk Reduction Plan 5.4
Address flash flood scenarios with mitigation measures	Adopted, scenario planning added to the Pangre Khola early warning design	Disaster Risk Reduction Plan 5.4

Source: Baglung IUDP ward discussion notes, 2082 BS. Plan response by Baglung IUDP team.

5. Problem analysis

Four causes feed the core problem, eight wards outside formal collection, no monitoring stations anywhere, forest and hazard data missing for half the municipality, and eighteen tonnes a day of waste going one hundred percent to open disposal. The effects are open dumping across the outer wards, a river and air quality record that literally does not exist, and a pangolin habitat left unprotected inside the municipality's best forest.

PROBLEM ANALYSIS: THE PROBLEM TREE

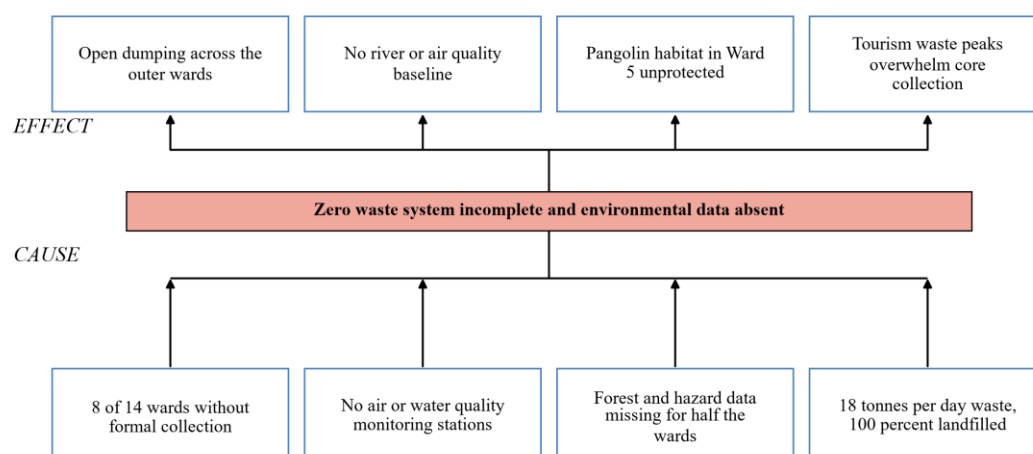


Figure 5.13. Problem analysis tree, Environmental Management Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree sets one core objective, all fourteen wards on formal zero waste with full environmental monitoring. The means are the three bin rollout with four compactors, the transfer station with the one hectare sanitary landfill, the two quality stations at the bazaar and Balewa, and the forest register with the gazetted pangolin corridor. The ends are seventy percent diversion from landfill, quarterly public monitoring reports, and a mapped, protected forest estate.

OBJECTIVE ANALYSIS

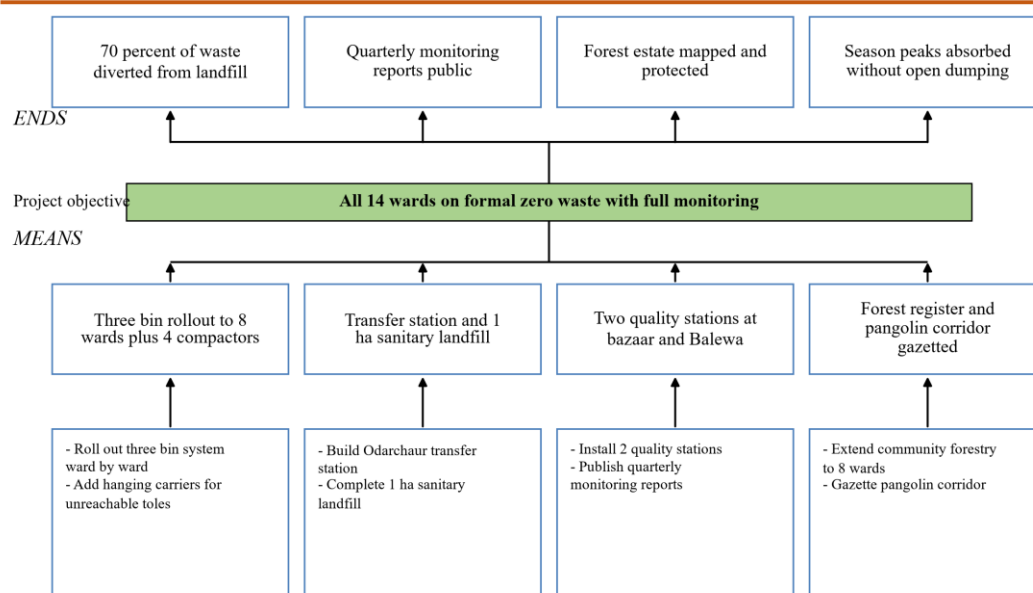


Figure 5.14. Objective analysis tree, Environmental Management Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Full outsourcing to private operators scores well on speed but weakens the fee base and the user group linkage that makes hill waste systems stick. An awareness campaign alone is cheap and does nothing. The municipal zero waste scale up, run with user groups and the existing partners, wins.

Table 5.30. Alternative options scored against five criteria, Environmental Management Plan

Criterion	A. Outsource all collection	B. Municipal zero waste scale up	C. Awareness campaign only
Cost efficiency	Medium	High	High
Chance of success	Medium	High	Low
Speed of delivery	High	Medium	Low
GESI impact	Medium	High	Low
Environmental risk	Medium	High	Low
Total score (1 to 3 per criterion)	11	14	7

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Outsource all collection to private operators	Medium	Medium	High	Medium	Medium	11
Municipal zero waste scale up	High	High	Medium	High	High	14
Awareness campaign only	High	Low	Low	Low	Low	7

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.15. Alternative analysis heat grid, Environmental Management Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

5. Solid waste management

Waste generation is about 18 tonnes per day and climbing with the bazaar economy. The DUDBC norm targets 70 percent reduce, reuse and recycle, and only 30 percent to landfill. The plan therefore scales the three bin system ward by ward, builds the transfer station at Odarchaur, adds the collection fleet, and completes the sanitary landfill with a recycling platform and compost plant. The ALK Eco incinerator handles the 1 to 3 tonnes per day of hazardous and medical waste at a capital cost of NPR 6 to 12 million (municipal records, 2082 BS). For the toles the collection vehicle cannot reach, the ward discussions contributed the hanging waste carrier, a cable suspended container serviced weekly or monthly, and the plan adopts it as a named programme line in the community proposals register.

Table 5.31. Solid waste programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
------	----------	-----------------	------------------

Three bin rollout to all wards	8 wards	0.5 crore each	4.00
Collection fleet and containers	4 compactors	0.9 crore each	3.60
Transfer station at Odarchaur	1 site	lump sum	3.00
Sanitary landfill with recycling platform	1 ha	lump sum	8.00
ALK Eco incinerator	1 unit	lump sum	1.20
Eco club and awareness programme	5 years	0.3 crore per year	1.50
Total solid waste			21.30

Source: Baglung IUDP team estimates and the municipal waste programme, 2082 BS.



Figure 5.16. Solid waste collection and transit route across the wards.

Table 5.32. Ward wise waste generation and collection status

Ward	Waste (TPD)	Collection	System	Gap
1	1.2	Yes	Three bin, formal	None
2	4.5	Yes	Three bin, formal, ALK Eco	None
3	2.8	Yes	Three bin, formal	None
4	1.5	Yes	Three bin, formal	None
5	0.6	No	Informal dump	Full collection needed

6	0.7	No	Informal dump	Full collection needed
7	0.9	No	Informal dump	Full collection needed
8	0.6	No	Informal dump	Full collection needed
9	0.8	No	Informal dump	Full collection needed
10	0.7	No	Informal dump	Full collection needed
11	0.3	No	Informal dump	Full collection needed
12	1.2	No	Informal dump	Full collection needed
13	1.5	Partial	Three bin partial	Complete coverage
14	0.9	Partial	Three bin partial	Complete coverage
Total	18.2	42%		8 wards without formal collection

Source: Baglung IUDP team estimates from EnDP sheet and municipal waste survey, 2082 BS. TPD is tonnes per day.

5. Forest, water and climate

The forest plan protects the estate and adds value to it. The community forestry model is proven in 43 user groups, and the plan extends it to the data deficient wards, adds agroforestry on the 31 percent of farmland reported underutilised, and maps the Chinese pangolin habitat of Ward 5 into a conservation corridor. The river plan adds the monitoring line. No air or water quality station exists, so the first phase installs two simple stations, one at the bazaar and one at the Balewa river front.

Table 5.33. Forest estate by type and ward

Forest type	Area (ha)	Share	Wards	Management
Government managed	1,401.43	43.6%	Wards 5, 7, 9, 11, 12	DFO Baglung
Community forest	1,801.91	56.0%	43 user groups across 12 wards	Community forest user groups
Leasehold forest	7.44	0.2%	Wards 3, 10	Leasehold groups
Religious forest	4.22	0.1%	Wards 1, 6	Temple committees
Total	3,215.00	100%	14 wards	Mixed

Source: EnDP sheet, Baglung IUDP DataSets. Malika community forest in Ward 5 covers 180 ha alone.

Table 5.34. Forest, water quality and climate programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Community forest extension to 8 wards	8 plans	0.25 crore each	2.00
Agroforestry and private woodlot support	200 ha	0.02 crore per ha	4.00

Air and water quality stations	2 stations	0.5 crore each	1.00
Climate adaptation fund for hill wards	5 years	0.8 crore per year	4.00
Total forest and climate			11.00

Source: Baglung IUDP team estimates, EnDP sheet data.

5. Logical framework

Table 5.35. Logframe matrix (LFM), Environmental Management Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Environmentally balanced and climate resilient municipality		70 percent diversion and 14 of 14 wards served by 2031	Municipal annual report and scorecard	R1: Landfill site faces community opposition (Medium probability, High impact)
Project Purpose Zero waste in all wards and complete environmental data by 2031	●	All wards collected, quarterly reports public from 2030	Waste records, forest user group reports, station logs	R2: Incineration permits delayed (Medium probability, Medium impact)
Expected Outputs (Results) - Formal collection in 14 wards with segregation - Landfill, transfer station and incineration operating - Two monitoring stations reporting quarterly			Waste records, forest user group reports, station logs	R3: Forest user group membership ageing (Low probability, Medium impact)
Activities - Roll out three bin system - Build transfer station and landfill - Install quality stations		Facilities completed per annual programme	Project completion reports	R4: Season tourism waste outpaces capacity (Medium probability, Medium impact)
Inputs NPR 18.0 crore phase one 2026 to 2031 of NPR 32.3 crore over three phases, municipal and federal sources			Budget red book and financial reports	R5: Climate intensified rainfall damages works (Medium probability, High impact)

Source: Baglung IUDP team, 2082 BS.

5. Assumptions and risk response

Six assumptions carry the environmental plan. The landfill site is the one with real conflict potential, scored medium probability and high impact with a contingency of an alternative site search already scoped at Odarchaur and Jaimini border plots.

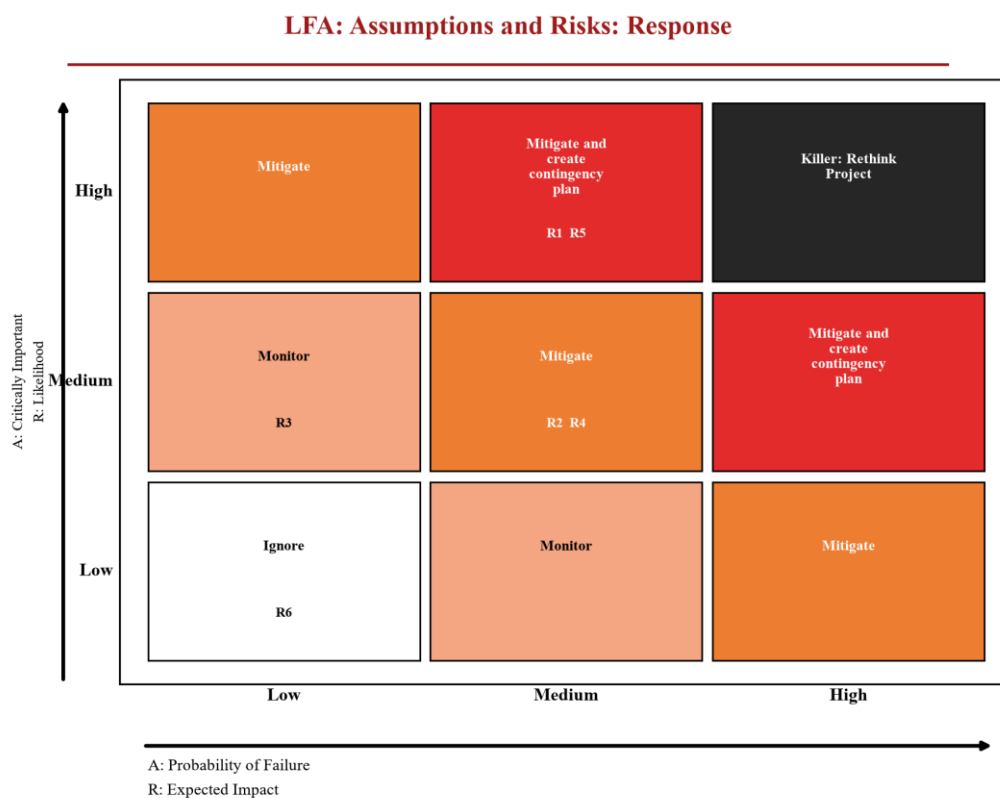


Figure 5.17. Assumptions and risks response matrix, Environmental Management Plan. Baglung IUDP team, 2082 BS.

Table 5.36. Risk register, Environmental Management Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Landfill site faces community opposition	Medium	High	Mitigate and create contingency plan	Compensations and benefit sharing agreed pre construction, alternative site scoped, environment cell
R2	Incineration permits delayed	Medium	Medium	Mitigate	File EIA in year one, interim contract with outside incineration, environment cell
R3	Forest user group membership ageing	Low	Medium	Monitor	Youth sub committees in each user group,

					forestry section
R4	Season tourism waste outpaces capacity	Medium	Medium	Mitigate	Seasonal collection surge contract, extra containers at Panchakot, sanitation section
R5	Climate intensified rainfall damages works	Medium	High	Mitigate and create contingency plan	Drainage designed to 20 year storm, DRRM contingency fund, DRRM committee
R6	Fleet procurement delayed	Low	Low	Ignore	No action beyond the annual scorecard review, municipal works

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.37. Implementation summary, Environmental Management Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Three bin rollout to 8 wards, fleet, transfer station, landfill, two monitoring stations	18.0
Phase 2	2031 to 2036	Compost and recycling platform completion, agroforestry scale up	9.0
Phase 3	2036 to 2041	Climate adaptation continuation, estate consolidation	5.3
Total			32.3

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent.

5. Conclusion

The environmental plan is the cheapest credibility the municipality can buy. For NPR 32.3 crore it converts an open dump culture into a measured, fee supported service in every ward, and gives the forest estate the legal protection its user groups have already earned in practice. Its one hard test is the landfill site, and the plan names that conflict in its risk register rather than discovering it at construction.

5. Disaster Risk Reduction Plan

5. Goal, objectives and strategy

The goal of the disaster plan is a disaster and climate resilient municipality. Its purpose in the first phase is that every ward knows its hazards, the two killer corridors carry early warning, and the building code has teeth. The strategy rests on three moves.

- Map first, build second. The GIS rasters already exist, so ward risk registers and the evacuation system are completed before major structural spending.
- Protect the two lifelines, the corridor road and the river front, with bio engineering and bank works sized to a 20 year storm.
- Enforce through the permit. The building code rides on the permit process of Chapter 8, not on inspection campaigns the municipality cannot staff.

Strategic priority. GIS based disaster risk mapping for the high risk wards 5, 6, 12 and 14, linked to the evacuation system and the building code.

5. Present condition and constraints

The hazard profile is dominated by water and slope. The Pangre Khola flash flood in Ward 5 took two lives. Ward 14 suffers corridor landslides almost every monsoon, blocking the region's lifeline road. Ward 12 is recorded as one of the most hazard prone wards of the municipality. The bazaar floods every year from hillside runoff. The modelled flood and landslide rasters give the plan its spatial base.

Table 5.38. SWOT analysis, Disaster Risk Reduction Plan

	Positive	Negative
Internal strengths	GIS based flood and landslide rasters completed for the municipality, ward level hazard records maintained by DRRM committee, search and rescue training already conducted for 200 persons, river bank protection works started on Kali Gandaki front, building code awareness campaigns in core wards	Hazard mapping incomplete for Wards 5, 6, 12 and 14, no early warning systems on Pangre Khola or corridor, evacuation centres not yet equipped, bio engineering on corridor not started, building code enforcement weak in rural wards
Internal weaknesses	Ward 14 corridor landslides blocking the region lifeline road almost every monsoon, Pangre Khola flash flood in Ward 5 killed two lives, bazaar floods every year from hillside runoff, Ward 12 recorded as one of the most hazard prone wards, no flood insurance or risk transfer mechanism	DRRM committee capacity limited, search and rescue gear outdated, no floodplain zoning enforced, construction in hazard zones continuing, emergency communication system not installed
External opportunities	Federal DRRM grants for hazard mapping and early warning, building code enforcement drive linked to new construction permits, bio engineering techniques proven in corridor stabilisation, climate adaptation funding for river bank protection, GIS capacity from institutional chapter for risk mapping	Climate change increasing monsoon intensity and flood frequency, population decline reducing the tax base for DRRM investment, federal grants declining, political cycles interrupting long term DRRM programmes

External threats	Seismic risk across the Mid-Hill belt with old unreinforced masonry building stock, corridor landslides worsening with climate change, glacial lake outburst flood potential upstream in the Kali Gandaki basin, Kali Gandaki river bank erosion threatening the bazaar edge, flash flood frequency increasing on tributaries	Insurance market not available for municipal infrastructure, contractor capacity limited for bio engineering works, community resistance to relocation from hazard zones, federal building code standards not yet adopted locally
------------------	---	---

Source: Baglung IUDP team analysis from EnDP, GIS hazard rasters, ward disaster records and field survey, 2082 BS.

5. Problem analysis

Four causes define the exposure, hazard mapping missing for the four worst wards, no early warning on Pangre Khola or the corridor, only two under equipped evacuation centres, and a building code weakly enforced. The core problem is high hazard exposure running ahead of mapping, warning and response. The effects are already in the record, two lives lost at Pangre Khola, the lifeline road blocked annually at Ward 14, and a bazaar that floods every single monsoon.

PROBLEM ANALYSIS: THE PROBLEM TREE

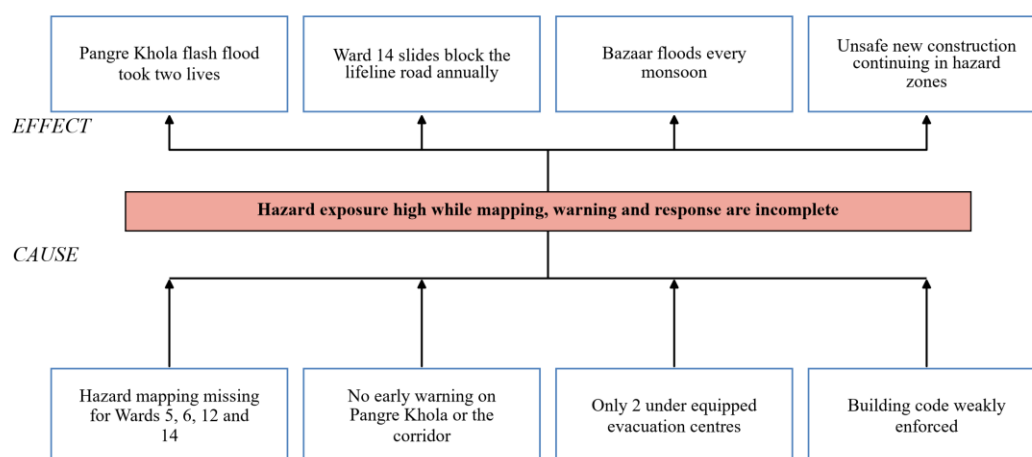


Figure 5.18. Problem analysis tree, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree targets mapped hazards, equipped response and an enforced code by 2031. The means are ward risk registers on the existing GIS layers, two early warning systems, six equipped evacuation centres and twenty kilometres of bio engineering with ten kilometres of bank protection. The ends are a register and evacuation plan in every ward, stabilised corridor and river bank, and two hundred trained responders drilling twice a year.

OBJECTIVE ANALYSIS

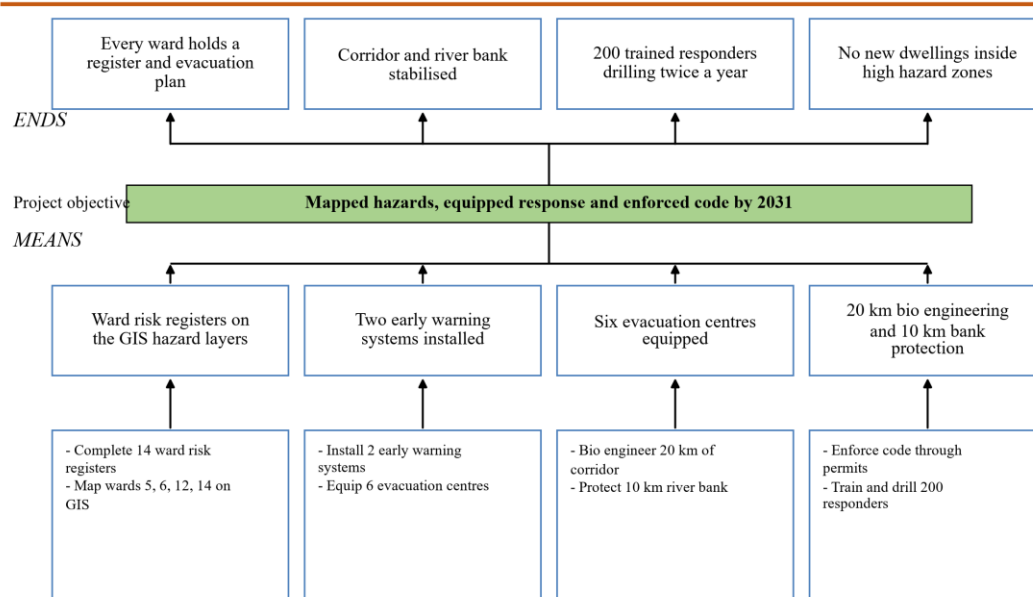


Figure 5.19. Objective analysis tree, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Structural works alone spend heavily before anyone knows where the risk sits. Relocating hazard zone households is socially and fiscally unrealistic at this scale. The mapped and targeted option, warning systems plus registers plus works where the rasters say it matters, wins on every criterion.

Table 5.39. Alternative options scored against five criteria, Disaster Risk Reduction Plan

Criterion	A. Structural works only	B. Mapping, warning and targeted works	C. Relocate hazard zone households
Cost efficiency	Low	High	Low
Chance of success	Medium	High	Low
Speed of delivery	Medium	Medium	Low
GESI impact	Low	Medium	Medium
Environmental risk	Low	High	Medium
Total score (1 to 3 per criterion)	7	13	7

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Structural works only	Low	Medium	Medium	Low	Low	7
Mapping, warning and targeted works	High	High	Medium	Medium	High	13
Relocate hazard zone households	Low	Low	Low	Medium	Medium	7

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.20. Alternative analysis heat grid, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

Table 5.40. Ward wise hazard exposure matrix

Ward	Flood risk	Landslide risk	Seismic zone	Historical events	Priority
1	High	Low	Moderate	River bank erosion	High
2	Very high	Low	Moderate	Annual bazaar flooding	Critical
3	Moderate	Low	Moderate	Hillside runoff flooding	High
4	Moderate	Low	Moderate	Corridor flooding	Medium
5	High	Moderate	High	Pangre Khola flash flood (2 deaths)	Critical
6	Low	Moderate	High	Slope instability	Medium
7	Low	Moderate	High	Minor landslides	Low
8	Low	Moderate	Moderate	Slope instability	Low
9	Low	High	High	Hill erosion, remoteness	Medium
10	Low	Moderate	Moderate	Lake buffer zone	Medium
11	Low	High	High	Hill erosion, remoteness	Medium
12	Moderate	High	High	One of most hazard prone wards	Critical
13	Moderate	High	Moderate	Corridor landslides, flood	High
14	Moderate	Very high	Moderate	Annual corridor landslides	Critical

Source: Baglung IUDP team GIS hazard rasters and ward disaster records, EnDP sheet.

Table 5.41. Disaster risk reduction programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Hazard mapping and ward risk registers	14 wards	0.1 crore each	1.40
Evacuation centres equipped	6 centres	0.6 crore each	3.60
Early warning on Pangre Khola and corridor	2 systems	0.5 crore each	1.00
Landslide bio engineering, corridor	20 km	0.25 crore per km	5.00
River bank protection, Kali Gandaki front	10 km	0.8 crore per km	8.00
Search and rescue training and gear	200 persons	lump sum	1.50
Building code enforcement drive	14 wards	0.15 crore each	2.10
Total DRR			22.60

Source: Baglung IUDP team estimates on the EnDP disaster summary and the GIS hazard rasters.

5. Logical framework

Table 5.42. Logframe matrix (LFM), Disaster Risk Reduction Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Disaster and climate resilient municipality		Zero hazard deaths after 2031, corridor open every monsoon	Municipal annual report and scorecard	R1: Corridor road authority does not cooperate (Medium probability, High impact)
Project Purpose Hazards mapped, response equipped and the code enforced by 2031	●	14 registers, 2 warnings live, code enforced from 2030	DRRM committee reports, GIS risk layers, drill logs	R2: Federal DRRM grants delayed (Medium probability, Medium impact)
Expected Outputs (Results) - 14 ward risk registers and evacuation plans - Two early warning systems running - Six equipped centres and 200 trained responders	●	6 centres equipped, 200 responders, drills twice yearly	DRRM committee reports, GIS risk layers, drill logs	R3: Community resists code enforcement (Medium probability, Medium impact)

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Activities - Map hazards on the GIS - Install warning systems - Equip centres and train responders		Systems and works completed per annual programme	Project completion reports	R4: Upstream glacial flood exceeds all design (Low probability, High impact)
Inputs NPR 14.0 crore phase one 2026 to 2031 of NPR 22.6 crore over three phases, federal DRRM and municipal sources		DRRM funds utilised above 85 percent	Budget red book and financial reports	R5: Equipment procurement delayed (Low probability, Low impact)

Source: Baglung IUDP team, 2082 BS.

5. Assumptions and risk response

Six assumptions carry the disaster plan. The corridor road authority is the critical external actor, scored medium probability and high impact with a contingency of provincial mediation and a phased works package that starts on municipal segments.

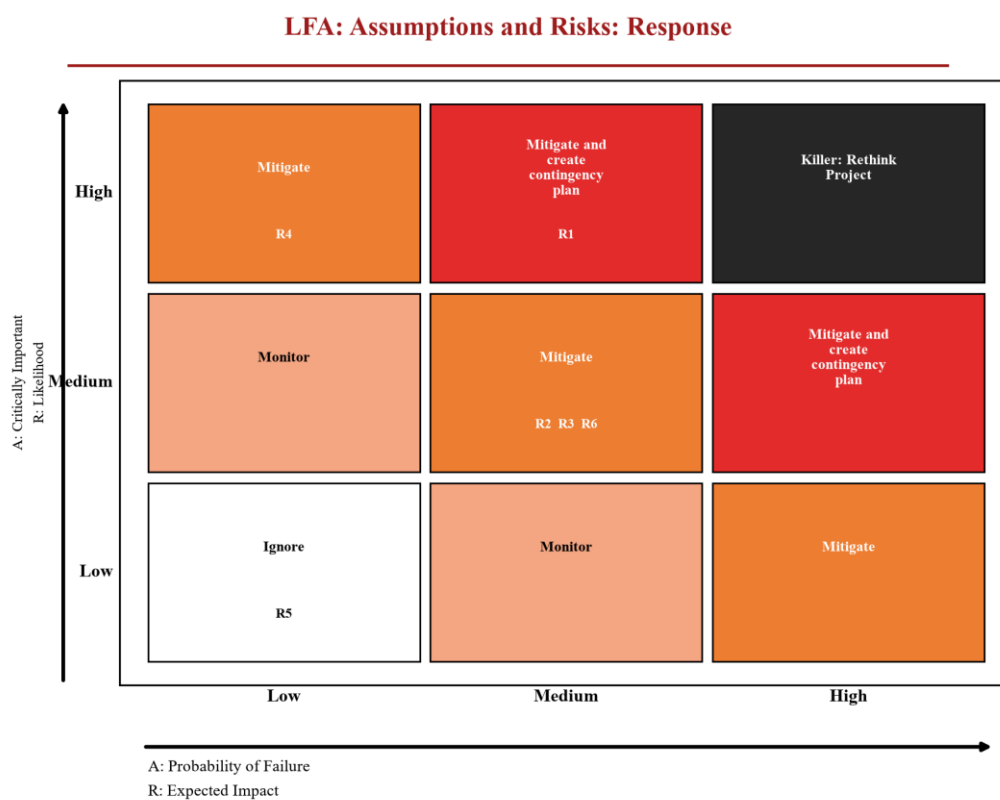


Figure 5.21. Assumptions and risks response matrix, Disaster Risk Reduction Plan. Baglung IUDP team, 2082 BS.

Table 5.43. Risk register, Disaster Risk Reduction Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Corridor road authority does not cooperate	Medium	High	Mitigate and create contingency plan	Provincial mediation, start on municipal segments, phased agreement, DRRM committee
R2	Federal DRRM grants delayed	Medium	Medium	Mitigate	Sequence registers and warning first, works follow grants, finance section
R3	Community resists code enforcement	Medium	Medium	Mitigate	Permit linked incentives, retrofit demonstrations, building section
R4	Upstream glacial flood exceeds all design	Low	High	Mitigate	Warning system covers the reach, evacuation drills assume extreme event, DRRM committee
R5	Equipment procurement delayed	Low	Low	Ignore	No action beyond the annual scorecard review, municipal works
R6	Drill programme lapses after year one	Medium	Medium	Mitigate	Drill calendar in the ward minimum conditions, annual scorecard line, DRRM committee

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.44. Implementation summary, Disaster Risk Reduction Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Ward registers, two early warning systems, six evacuation centres, first corridor bio engineering tranche	14.0
Phase 2	2031 to 2036	Remaining bio engineering, river bank protection completion	6.0

Phase 3	2036 to 2041	Maintenance regime, code enforcement institutionalisation	2.6
Total			22.6

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent.

5. Conclusion

The disaster plan buys down the municipality's oldest debt, a hazard load that has been paid in lives and blocked roads for decades. For NPR 22.6 crore it maps the risk it already knows informally, warns the two corridors that kill, and puts a register and a drill in every ward. Its success is measured negatively, by the floods that stop costing lives and the monsoons that stop closing the road.

5. Tourism Development Plan

5. Goal, objectives and strategy

The goal of the tourism plan is tourism revenue for the municipality and its people. Its purpose in the first phase is that the demand which already stands at Panchakot, the temple and the bridge begins paying wages, leases and royalties instead of passing through. The strategy rests on three moves.

- Concede, do not construct. The three flagship products are licensed to private operators on municipal land, because the municipality cannot carry the capital and should not try.
- Bundle the day visitors into circuits. The heritage precinct, the homestay line and the agro belt exist to turn a three hour visit into a one night stay.
- Standardise before marketing. Booking, safety and quality standards come first, so the reputation the circuit earns is the one it can keep.

Strategic priority. Convert existing visitor demand into overnight stays and municipal revenue by 2031 through concessions on the river, cliff and ridge.

5. Present condition and constraints

The economy analysis showed a thin modern sector. Industry, ICT and finance hold about 7 to 8 percent of employment, and Ward 2 carries 44.5 percent of all registered firms in trade alone. Tourism is the one sector where the municipality already holds proven demand. Panchakot counts 5,000 to 7,000 visitors a day in season. Kalika Bhagawati draws 500 to 700. The Golden Bridge draws 800 to 1,500. The visitors come, they stay a few hours, and the money leaves with them. The plan exists to make them stay longer and spend more (field survey, 2082 BS).

Table 5.45. SWOT analysis, Tourism Development Plan

	Positive	Negative
Internal strengths	Panchakot draws 5,000 to 7,000 visitors per day in season, Kalika Bhagawati draws 500 to 700, Golden Bridge draws 800 to 1,500, 567 metre Gandaki Golden Bridge is Nepal longest suspension bridge, 11 registered homestays in Ward 10, Ward 6 orange crop worth 1 crore last year	Visitors stay few hours and money leaves, no overnight accommodation infrastructure at Panchakot, homestay occupancy only 4 of 11 operating, no cable car or ropeway, no adventure products beyond the bridge viewpoint, no heritage precinct pedestrianisation

Internal weaknesses	Day visitor model with no revenue capture, no river infrastructure for rafting, no bungee or adventure products on the Baglung side, heritage quarter not pedestrianised, food and craft outlets limited, marketing and booking system absent	Season concentrated in monsoon and post monsoon, access roads limited in hill wards, no air connectivity, civil aviation approval process uncertain, no tourism development cell in municipal office
External opportunities	30,000 to 40,000 commercial rafting trips per year in Nepal market, Kushma bungee proven demand across the river, Manakamana and Chandragiri cable car models for PPP, Sirubari and Ghalegaun homestay occupancy at 60 to 80 percent in season, Dhulikhel agro tourism lifting farm margins 30 percent	Kushma already holds the gorge jump market, Trisuli dominates rafting, Pokhara adventure cluster absorbing weekend market, civil aviation and tourism approvals required, operator competition from established destinations
External threats	Kushma bungee as direct competitor on the same gorge, Pokhara absorbing the international tourism market, seasonality limiting year round revenue, road access vulnerable to monsoon landslides, climate change affecting river flow patterns	Federal tourism budget uncertain, domestic weekend market finite, security concerns affecting adventure tourism, environmental impact of tourism on gorge ecosystem, community opposition to commercial development near temples

Source: Baglung IUDP team analysis from BCCI registry, field survey, Nepal Tourism Statistics 2023 and GIS, 2082 BS.

The ward discussions added a cultural voice to the tourism chapter, outreach and branding for the municipality's cultural activities. The register below records it with the plan response.

Table 5.46. Community proposals register, tourism and culture

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Outreach and branding of cultural activities and programmes	Adopted, cultural branding campaign within the booking and marketing system line	Plan and programmes, this chapter
Youth instructor skills in bungee, rafting and cable car	Adopted, certification tied to the flagship concessions with guaranteed placement	Economic Development Plan 5.6

Source: Baglung IUDP ward discussion notes, 2082 BS. Plan response by Baglung IUDP team.

5. Problem analysis

Four causes sustain the leakage. The demand hub at Panchakot has no overnight product, only four of eleven registered homestays actually operate, the river, cliff and ridge carry no access products at all, and the day visitor flow passes over no levy of any kind. The core problem is proven demand that leaves without staying or paying. The effects follow, municipal tourism revenue near zero, bazaar hospitality running under capacity, and young people who see no career in the one sector where their town holds an advantage.

PROBLEM ANALYSIS: THE PROBLEM TREE

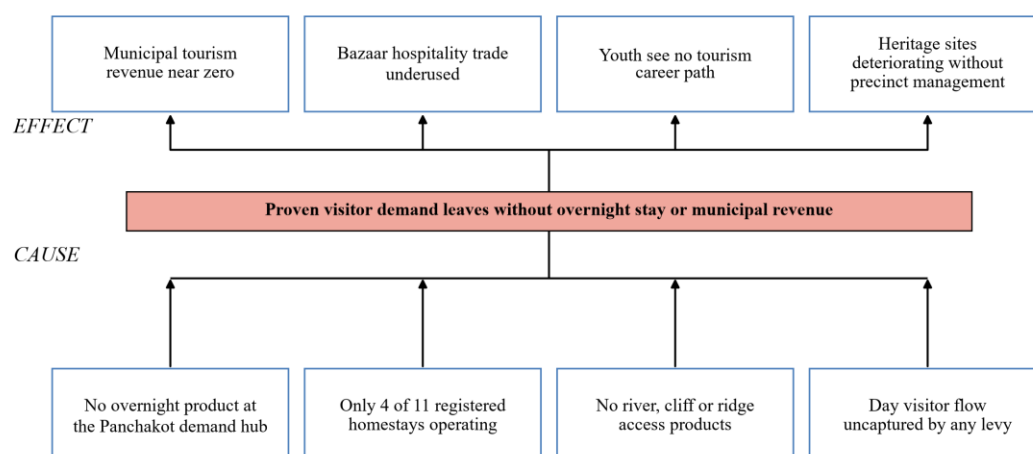


Figure 5.22. Problem analysis tree, Tourism Development Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree aims at one conversion, existing demand turned into stays, jobs and municipal revenue by 2031. The means are the rafting corridor and gorge bungy under concession, the cable car public private partnership to the ridge, the heritage precinct with the homestay revival, and the booking and standards system that binds them into one circuit. The ends are NPR 3 to 4 crore of annual municipal take, twelve homestays running at sixty percent occupancy, and a thousand tourism jobs for local youth.

OBJECTIVE ANALYSIS

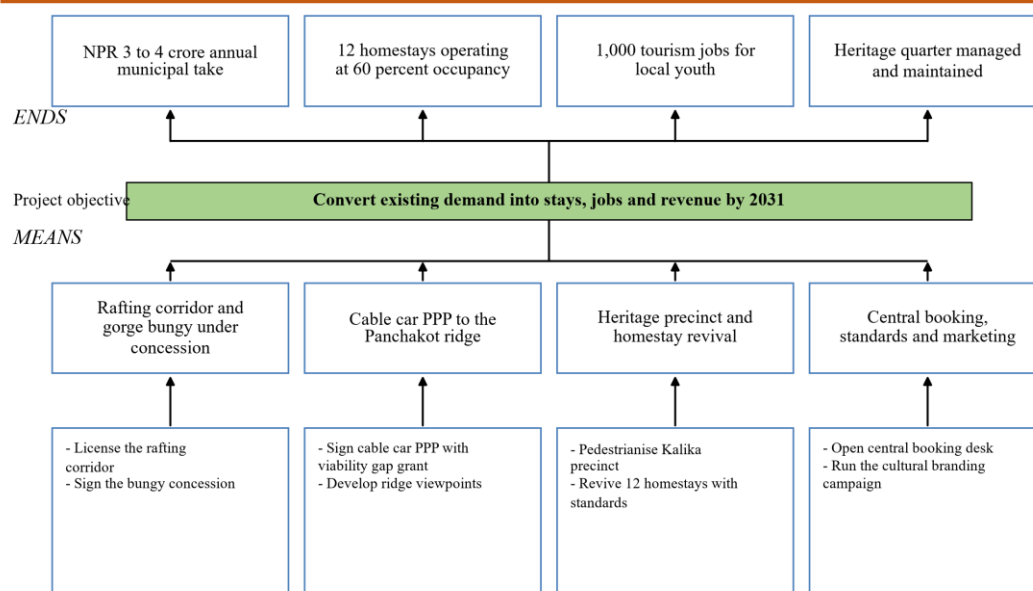


Figure 5.23. Objective analysis tree, Tourism Development Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

The municipality building and operating every product fails the fiscal test, it cannot carry NPR 238 crore of capital. Marketing without infrastructure would advertise products that do not exist. The concession model on the proven demand hubs wins, the municipality contributes land and approvals, the operator contributes capital and operations.

Table 5.47. Alternative options scored against five criteria, Tourism Development Plan

Criterion	A. Municipality builds and operates	B. PPP concessions on demand hubs	C. Marketing only
Cost efficiency	Low	High	High
Chance of success	Low	High	Low
Speed of delivery	Low	Medium	High
GESI impact	Medium	High	Low
Environmental risk	Medium	Medium	High
Total score (1 to 3 per criterion)	7	13	11

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS


	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Municipality builds and operates all products	Low	Low	Low	Medium	Medium	7
PPP concessions on the proven demand hubs	High	High	Medium	High	Medium	13
Marketing only, no infrastructure	High	Low	High	Low	High	11

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.24. Alternative analysis heat grid, Tourism Development Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

The strategy has two halves. The demand half fixes the visitor experience at the places that already draw crowds. The supply half builds the products that turn day visitors into overnight guests. Eight products are screened in this chapter. Three of them, the rafting corridor, the bungy and the cable car, are developed to sub project level in Chapter 7.

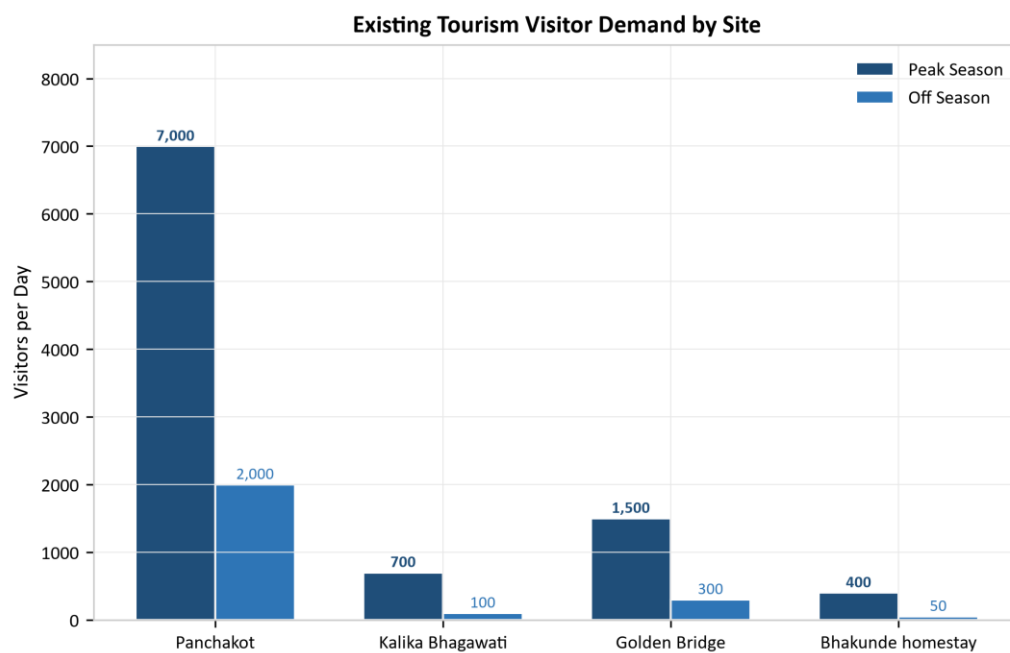

Source: Key informant interviews and site managers, field survey 2082 BS.

Figure 5.25. Existing tourism visitor demand by site. Panchakot dominates with 5,000 to 7,000 visitors a day in season.



Figure 5.26. The Gandaki gorge and the bungy anchor site near Kushma, visible from the Baglung side. Photo: Wikimedia Commons, CC BY-SA 4.0, 2026.

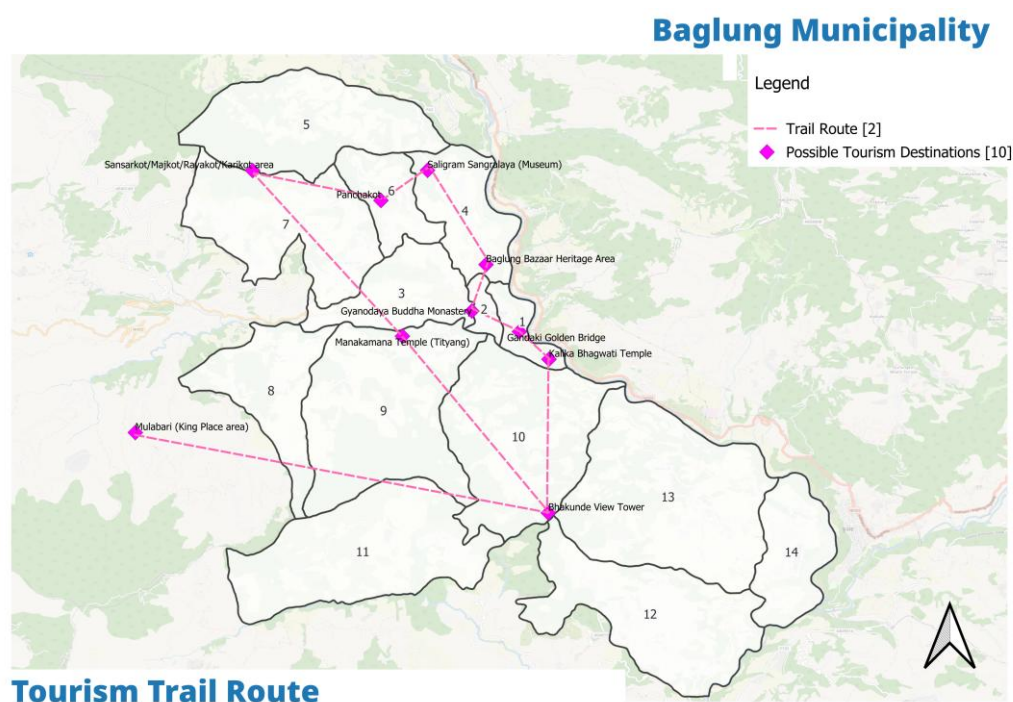


Figure 5.27. Tourism trail route and the attractions it links.

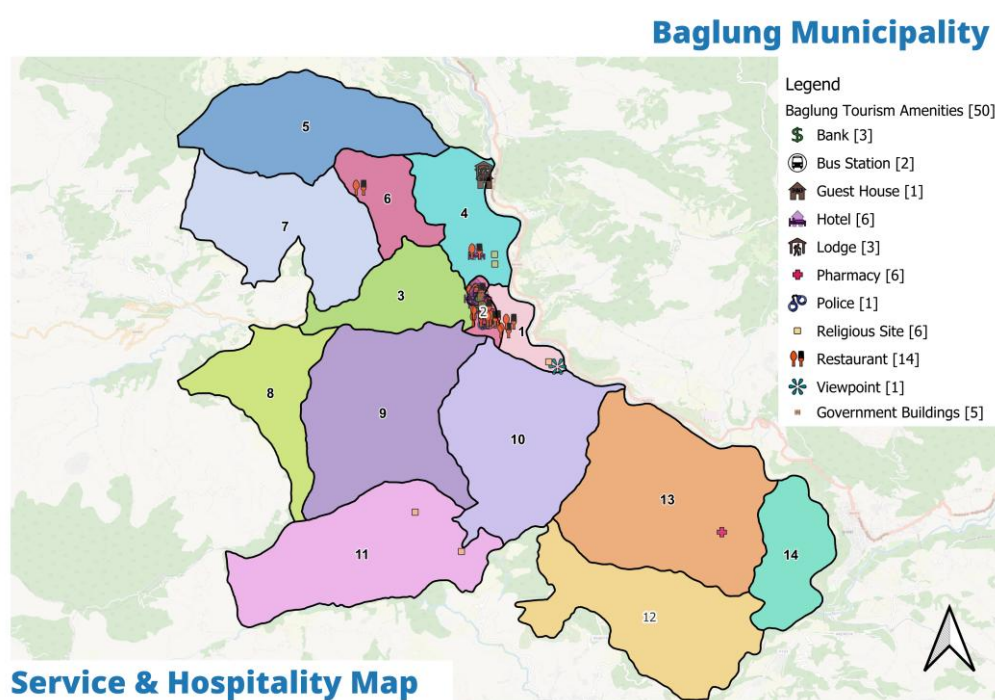


Figure 5.28. Service and hospitality establishments across the wards.

5. The eight tourism products

Product A, the Kali Gandaki rafting corridor. The river through Baglung is a proven rafting reach, and the corridor runs from a put in at Balewa in Ward 13 to the Ramrekha take out near Ward 1, about 25 kilometres of grade two to three water through the gorge in season (Nepal Rafting Association river inventory). The product needs ramps above the flood line, changing rooms, a guide training line for local youth and a booking and safety system.

Evidence box. Trisuli, Bhote Koshi and Marsyangdi rafting draw roughly 30,000 to 40,000 commercial trips a year in Nepal and the Nepal Tourism Board lists river sports among the fast growing adventure segments (Nepal Tourism Statistics, 2023). What transfers is the season pattern and the safety regime. What does not transfer is any assumption that Baglung can match Trisuli volume, because the access is hillier and the season shorter. The realistic first decade is 3,000 to 8,000 rafters a year.

Product B, the Kali Gandaki gorge bungy. Across the river in Kushma, Parbat, the Cliff bungy has operated a 228 metre jump since 2020 and the site has become the district's signature attraction. Baglung holds the opposite bank of the same gorge. The product is a second jump site with a licensed operator, a safety audit regime and a bridge park bundle that includes the viewpoint, a cafe and the heritage trailhead.

Evidence box. The Cliff at Kushma charges between NPR 7,000 and 9,000 per jump and reported strong domestic demand in its first seasons (The Cliff Nepal public records and media reporting, 2020 to 2024). What transfers is the operating model, private operator on municipal land with a royalty. What does not transfer is the assumption that demand is unlimited, the market is the domestic youth and the weekend, and the site must be bundled with other products to justify the trip.

Product C, the Panchakot cable car. Panchakot already holds the demand. The cable car converts that demand into reliable revenue and year round access. The alignment runs from the bazaar edge in Ward 4 to the Panchakot ridge in Ward 6, about 1.6 kilometres and roughly 700 metres of lift. The capital is large, so the plan screens it as a PPP with a municipal land lease, a revenue royalty and a federal viability gap grant, a structure the financial appraisal of Chapter 7 tests in full.



Figure 5.29. Ward 2 campus area, the ridge access corridor for the proposed cable car alignment. Photo: Baglung Group field team, 2082 BS.

Evidence box. Manakamana cable car (1998) and Chandragiri cable car (2018) both moved their sites from seasonal pilgrimage traffic to year round destinations, and Chandragiri now draws several hundred thousand visitors a year (Chandragiri Hills company reporting). What transfers is the geometry of the deal and the ridge development package. What does not transfer is the volume, Baglung has a smaller market and the project must price for the domestic weekend.

Product D, the Kalika Bhagawati heritage precinct. Kalika Bhagawati is one of the important Shakti Peeths of the region and sits at the head of the heritage quarter. The product is a pedestrian precinct, heritage lighting, shopfront regulation, a ticket pool for the temple and the adjacent sites, and the trail link to the Golden Bridge.



Figure 5.30. *Kalika Bhagawati Temple in Ward 1, the heritage precinct anchor. Photo: Baglung Municipality, used with permission, 2026.*



Figure 5.31. *Two tier brick shrine with festive flags, a node of the proposed heritage circuit. Photo: Baglung Group field team, 2082 BS.*

Product E, the Baraha Lake eco homestay circuit. Ward 10 holds 11 registered homestays and only 4 operate, while Baraha Lake draws 150 to 300 visitors a day in peak. The product is a homestay revival programme, trail signage, a central booking desk and a quality standard, linked to the orange orchards and the ridge walks. Sirubari and Ghalegaun demonstrate that hill homestays reach 60 to 80 percent occupancy in season when the booking system works (NTB homestay programme documentation).



Figure 5.32. Focus group discussion with community members on the homestay and eco-tourism circuit. Photo: Baglung Group field team, 2082 BS.

Product F, the Orange Valley agro tourism belt. Ward 6 sold one crore rupees of oranges last year and Wards 5, 7 and 8 all list oranges among their major crops (EDP sheet, Baglung IUDP DataSets). The product is a picking season package, a juice and marmalade processing unit, and a farm stay line along the orchards.



Figure 5.33. Farm economy visit in Ward 6, the agro-tourism and orange belt. Photo: Baglung Group field team, 2082 BS.

Product G, the suspension bridge adventure hub. The 567 metre Gandaki Golden Bridge is Nepal's longest suspension bridge and already a landmark. The product bundles it with the zipline and sky cycling lines that the bridge geometry allows, a viewpoint cafe and the trailhead link to the heritage quarter.

Product H, the hill trail running and paragliding ridge. The ridges above Kathekhola and the hill wards carry the wind and the views. The product is a marked trail running circuit that uses the existing trails, with one paragliding spur tested against the WorldClim wind data in the team GIS. Syangja and Pokhara licensing show the legal path, a Nepal Civil Aviation Authority licensed operator with a municipal landing fee.

5. Product selection and cost

The eight products were scored on three filters, land suitability from the GIS, ward readiness from the visitor counts and the homestay and road base, and fiscal return from the unit rate capital against the per visitor net. Three products scored highest and are developed in Chapter 7, the rafting corridor, the bungy and the cable car. They cover the river, the cliff and the ridge, they use the two proven demand hubs, and they can be licensed under the existing tourism and civil aviation rules. The other five run as programmes in this chapter with cost lines and phasing.

Table 5.48. Visitor flow and revenue projection by product

Product	Current visitors/year	Year 5 target	Average spend (NPR)	Gross revenue NPR crore
A. Rafting corridor	0 (new)	8,000 rafters	6,000 per rafter	4.80
B. Gorge bungy	0 (new)	10,000 jumps	7,500 per jump	7.50
C. Panchakot cable car	5,000 to 7,000/day season	150,000 riders/year	500 per ticket	7.50
D. Kalika heritage precinct	500 to 700/day season	200,000 visitors/year	200 per visit	4.00
E. Baraha homestay circuit	150 to 300/day peak	15,000 guest nights/year	1,500 per night	2.25
F. Orange agro tourism	0 (new)	10,000 visitors/year	800 per visit	0.80
G. Bridge adventure hub	800 to 1,500/day	50,000 visitors/year	1,000 per visit	5.00
H. Trail running and paragliding	0 (new)	2,000 participants	3,000 per participant	0.60

Source: Baglung IUDP team estimates from field survey and benchmarking against Trisuli, Kushma and Manakamana.

Table 5.49. Heritage and cultural site inventory

Site	Ward	Type	Visitor count	Conservation status	Action needed
Kalika Bhagawati Temple	1	Shakti Peeth	500 to 700/day season	Good, active committee	Heritage precinct, pedestrianise
Gandaki Golden Bridge	1	Suspension bridge	800 to 1,500/day	Structurally sound	Bridge park, adventure hub
Baraha Lake	10	Religious lake	150 to 300/day peak	Needs buffer zone	Eco-homestay circuit
Panchakot ridge	6	Hilltop viewpoint	5,000 to 7,000/day season	Informal access only	Cable car, viewpoint upgrade

Kundule temple	13	Heritage temple	Occasional	Neglected	Restoration, trail link
Bangechaur ground	2	Sports ground	Event based	Functional	Preserve from encroachment
Kathekhola gorge	14	River gorge	Occasional	Natural	Riverfront development
Malika community forest	5	Community forest	Low	Well managed by CFUG	Eco-tourism, pangolin trail

Source: Baglung IUDP team field survey and municipal heritage records, 2082 BS.




Figure 5.34. Temple facade with brick ornaments and prayer flags, the craftsmanship the heritage zone guidelines of Chapter 8 protect. Photo: Baglung Group field team, 2082 BS.

Table 5.50. Tourism programme cost summary

Product	Capital (NPR crore)	Municipal share	Private or PPP share
A. Rafting corridor	20.0	35 percent	65 percent
B. Gorge bungy	13.0	10 percent	90 percent
C. Panchakot cable car	70.0	10 percent	90 percent
D. Kalika heritage precinct	35.0	70 percent	30 percent
E. Baraha homestay circuit	20.0	60 percent	40 percent
F. Orange agro tourism	25.0	50 percent	50 percent
G. Bridge adventure hub	40.0	30 percent	70 percent

H. Trail running and paragliding	15.0	40 percent	60 percent
Total tourism	238.0	about 35 percent	about 65 percent

Source: Baglung IUDP team unit rate estimates. DPR level estimates in Chapter 7 for A, B and C.

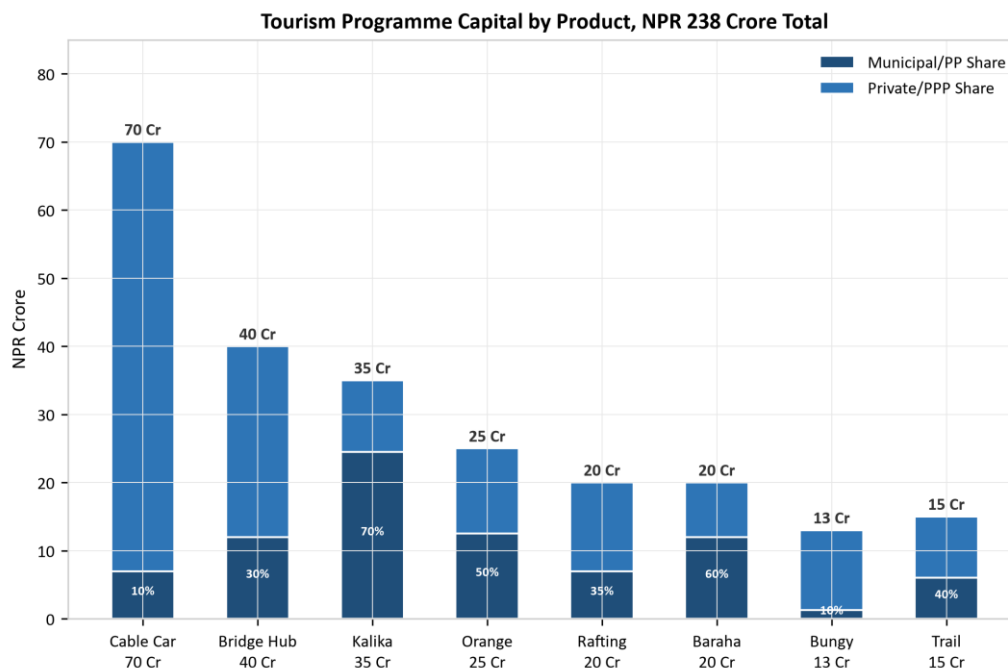

Source: Baglung IUDP team, Table 5.16. Planning accuracy plus or minus 30 percent.

Figure 5.35. Tourism programme capital by product. The cable car dominates at NPR 70 crore, with the bridge hub at NPR 40 crore.


5. Logical framework

Table 5.51. Logframe matrix (LFM), Tourism Development Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Tourism revenue for the municipality and its people		NPR 4 crore royalties and 150,000 cable riders by 2031	Municipal annual report and scorecard	R1: Kushma bungy substitutes demand (Medium probability, High impact)
Project Purpose Existing demand converted to overnight stays and municipal revenue by 2031		3,000 rafters, 10,000 jumps, 12 homestays by 2031	License fees, ticket audits, visitor counters, homestay register	R2: Civil aviation approvals delayed (Medium probability, High impact)

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Expected Outputs (Results) - River, cliff and ridge products licensed and running - Heritage and homestay circuit live - Municipal royalty stream flowing	●	Concessions signed, precinct open, booking desk live	License fees, ticket audits, visitor counters, homestay register	R3: Seasonality caps utilisation (High probability, Medium impact)
Activities - Issue concessions - Pedestrianise heritage precinct - Revive homestays with booking desk		Licences and contracts per concession schedule	Project completion reports	R4: Operator default on concession (Low probability, Medium impact)
Inputs NPR 78.0 crore phase one 2026 to 2031 of NPR 238.0 crore over three phases, mostly private and PPP capital		Municipal share disbursed above 85 percent	Budget red book and financial reports	R5: Corridor road closures cut access (Medium probability, High impact)

Source: Baglung IUDP team, 2082 BS.

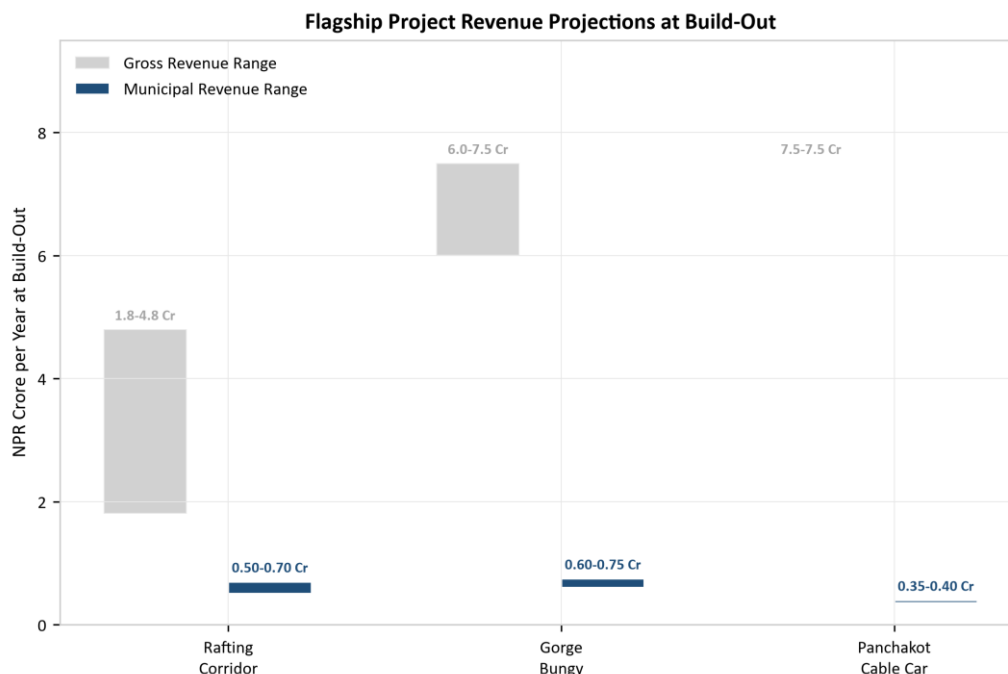

Source: Baglung IUDP team DPR estimates, Chapter 7. Planning accuracy plus or minus 30 percent.

Figure 5.36. Flagship project revenue projections at build-out. The municipal take is the royalty, not the gross revenue. Planning accuracy plus or minus 30 percent.

5. Assumptions and risk response

Six assumptions carry the tourism plan. Three sit in the red band. The Kushma substitution risk is managed by positioning the Baglung site as the complement with the bridge park bundle, the approvals risk by sequencing the file in year one, and the road access risk by tying the concession schedule to the corridor works of Chapter 5.1.

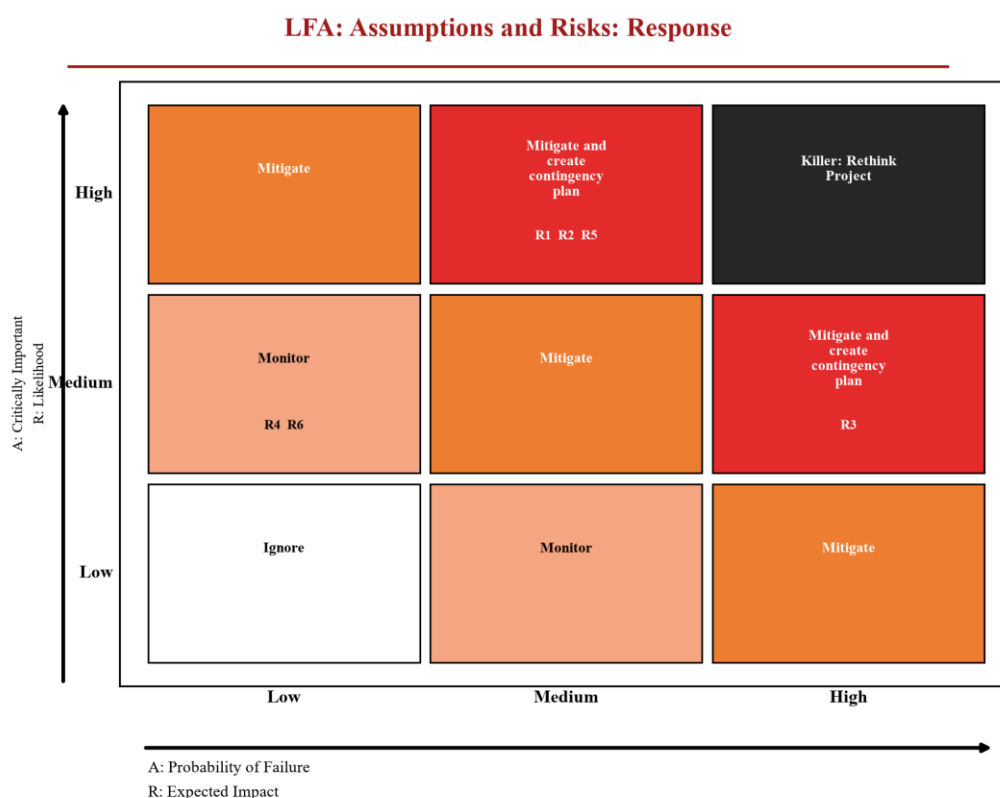


Figure 5.37. Assumptions and risks response matrix, Tourism Development Plan. Baglung IUDP team, 2082 BS.

Table 5.52. Risk register, Tourism Development Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Kushma bungy substitutes demand	Medium	High	Mitigate and create contingency plan	Position as complement with bridge park bundle, demand study before concession signing, tourism cell
R2	Civil aviation approvals delayed	Medium	High	Mitigate and create contingency plan	File in year one, sequence bungy first as it needs the lighter approval, tourism cell
R3	Seasonality caps utilisation	High	Medium	Mitigate and create contingency plan	Off season products in the heritage and agro

					lines, event calendar, tourism cell
R4	Operator default on concession	Low	Medium	Monitor	Performance bond and step in rights in the concession contract, PPP cell
R5	Corridor road closures cut access	Medium	High	Mitigate and create contingency plan	Tie concession milestones to the Chapter 5.1 corridor works, DRRM committee
R6	Community opposition near temples	Low	Medium	Monitor	Heritage zone guidelines of Chapter 8, temple committee revenue share, tourism cell

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.53. Implementation summary, Tourism Development Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Rafting and bungy licensed and operating, heritage precinct, homestay revival, booking and standards system	78.0
Phase 2	2031 to 2036	Cable car construction and opening, bridge adventure hub, orange agro belt build out	105.0
Phase 3	2036 to 2041	Paragliding ridge, trail running circuit completion, product refresh	55.0
Total			238.0

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent. Most capital is private, the municipal share is about NPR 83 crore.

5. Conclusion

The tourism plan is the revenue wager of this IUDP, and the financial appraisal of Chapter 7 prices it honestly. The bungy is bankable on its own numbers. The rafting corridor is viable as a package. The cable car needs the federal viability gap grant and an honest tariff review, and the plan says so before the contract is signed, not after. What the municipality contributes is land, approvals and standards.

What it gets back is a royalty stream, roughly a thousand jobs, and a reason for its young people to stay.

5. Economic Development Plan

5. Goal, objectives and strategy

The goal of the economic plan is a resilient, competitive and inclusive local economy. Its purpose in the first phase is that the corridor wards begin processing what the hill wards already grow, and that Ward 2's trade dominance starts paying for the infrastructure it uses. The strategy rests on three moves.

- Keep Ward 2 as the commercial and logistics hub, and make its parking, warehousing and routing problems a revenue question, not just a traffic one.
- Put the processing where the road and the flat land are, agro clusters in Wards 13 and 14, so the orange, dairy, spice, poultry and fish lines of the hills gain a market link.
- Tie every training seat to a named job line in tourism or processing, because certification without placement is just emigration with extra steps.

Strategic priority. Ward 2 stays the commercial and logistics hub. Wards 3 and 4 become the secondary business districts. Wards 13 and 14 carry the agro processing clusters. Wards 5 to 12 feed the value chains from the farm.

5. Present condition and constraints

The economy is concentrated, thin and leaking. Ward 2 carries 44.5 percent of the 1,219 registered firms and the wholesale trade that serves Myagdi, Parbat and Mustang. The modern sector is thin, manufacturing counts 20 firms and half the workforce still farms small plots. The leakage is the youth drain, 14.4 percent of residents absent abroad and 70.5 percent of them gone for foreign employment (NPHC 2021).

Table 5.54. SWOT analysis, Economic Development Plan

	Positive	Negative
Internal strengths	Ward 2 carries 44.5 percent of 1,219 registered firms, BCCI registry of 1,219 firms, orange crop in Ward 6 worth 1 crore last year, 77,971 chickens, 13,991 goats and 6,509 buffaloes, fish production 39,600 kg in Wards 3, 4, 12 and 13	Modern sector thin at 7 to 8 percent of employment, manufacturing only 20 firms, half the workforce still farms small plots, 14.4 percent residents absent abroad, 70.5 percent of absent for foreign employment, leakage of youth and capital to foreign employment
Internal weaknesses	Economy concentrated in Ward 2 retail trade, no agro processing clusters, no digital market platform, no logistics hub, business formalisation incomplete with 489 firms in others and services, irrigation covers only one quarter of farmland	No industrial zone designated, no MSME incubation centre, no skills training tied to local employment, no value chain from farm to market, remittance economy creating speculative consumption not productive investment
External opportunities	Corridor wards 4, 13 and 14 with flat land and road access for agro processing, tourism creating demand for local food and craft products, federal MSME support programmes, digital commerce platforms now affordable, skills training linked to	Retail saturation in Ward 2 bazaar, youth emigration reducing the labour force, climate change affecting agricultural productivity, market access limited by road quality, competition from Pokhara and Butwal for regional trade

	tourism and agro lines	
External threats	Foreign employment pull on the 15 to 34 age pool of 20,500, retail trade vulnerable to online competition, agricultural price volatility, climate change reducing crop yields, road access disruptions from monsoon landslides	Federal economic development grants uncertain, private investment hesitant outside Ward 2, land prices rising in corridor due to speculation, BCCI registry showing stagnation in new firm registration, economic leakage to Kathmandu and Pokhara markets

Source: Baglung IUDP team analysis from EDP, BCCI registry, field survey and demographic analysis, 2082 BS.

Table 5.55. Community proposals register, economic

Community proposal (ward discussions, 2082 BS)	Plan response	Where addressed
Single orange family agro processing unit sited in Wards 5, 6 and 7	Partially adopted, the plan sites clusters on the corridor where road and flat land allow truck movement, but the siting study will test a Ward 6 collection hub feeding the corridor plant	Agro processing, this chapter
High value crop identification for each ward	Adopted within the irrigation and farm storage programme with the agriculture section	Agro processing, this chapter

Source: Baglung IUDP ward discussion notes, 2082 BS. Plan response by Baglung IUDP team.

5. Problem analysis

Four causes produce the core problem. Nearly half the registered firms sit in one ward, there is no processing, cold chain or feed mill anywhere in the municipality, only a quarter of the farmland is irrigated, and seven in ten absent residents are gone for foreign work. The result is an economy concentrated in Ward 2 retail and leaking abroad. The effects are the thin modern sector at 7 to 8 percent of jobs, farm margins that stay flat despite real output in oranges, livestock and fish, and the continuing drain on the 15 to 34 age pool.

PROBLEM ANALYSIS: THE PROBLEM TREE

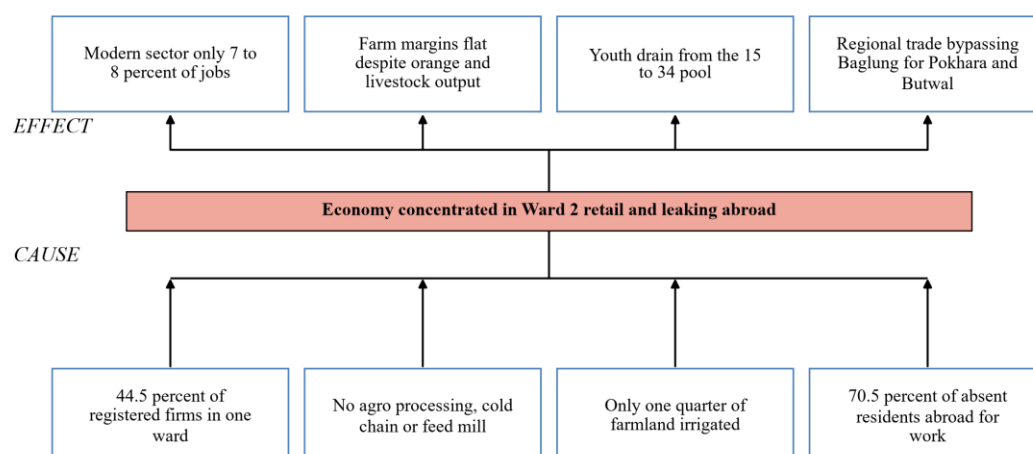


Figure 5.38. Problem analysis tree, Economic Development Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree aims at a diversified economy of trade, processing and tourism by 2031. The means are the Ward 2 logistics and digital market, the agro processing clusters in Wards 13 and 14, irrigation and farm storage in the hill wards, and skills training tied to the tourism and processing job lines. The ends are farm income up twenty percent, a thousand trained and placed youth, and three clusters producing for the regional market.

OBJECTIVE ANALYSIS

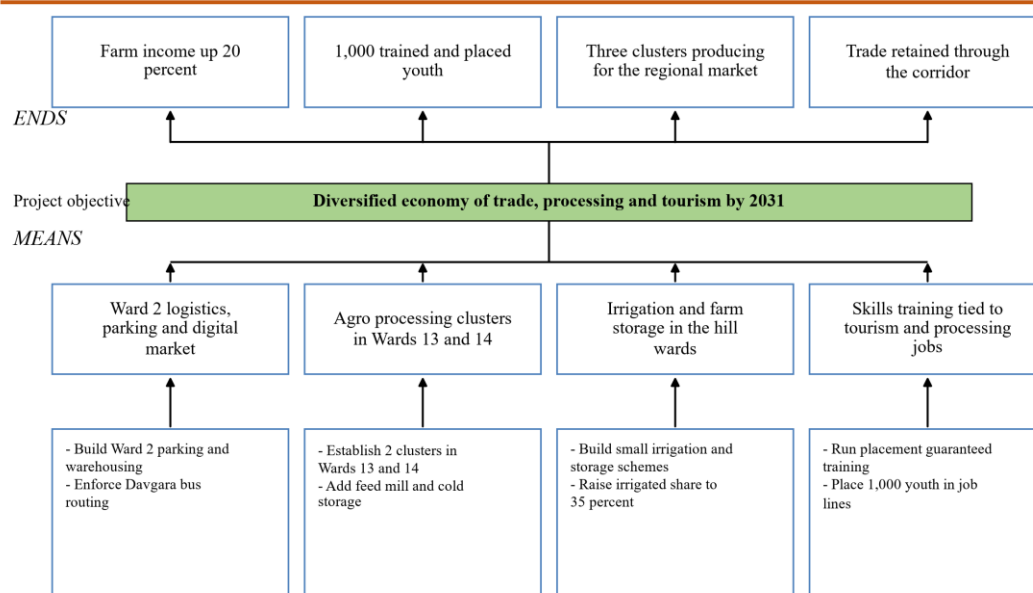


Figure 5.39. Objective analysis tree, Economic Development Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Retail expansion alone deepens the concentration it should fix. An industrial park attraction bid spends scarce capital chasing an investor who has a whole province to choose from. The corridor agro

processing and logistics strategy builds on the land, the road and the produce the municipality already has.

Table 5.56. Alternative options scored against five criteria, Economic Development Plan

Criterion	A. Retail expansion only	B. Corridor agro processing and logistics	C. Industrial park attraction bid
Cost efficiency	Medium	High	Low
Chance of success	Medium	High	Low
Speed of delivery	High	Medium	Low
GESI impact	Low	High	Medium
Environmental risk	Medium	Medium	Medium
Total score (1 to 3 per criterion)	10	13	7

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Retail expansion only	Medium	Medium	High	Low	Medium	10
Corridor agro processing and logistics	High	High	Medium	High	Medium	13
Industrial park attraction bid	Low	Low	Low	Medium	Medium	7

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.40. Alternative analysis heat grid, Economic Development Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

5. Trade and the logistics hub

The plan strengthens Ward 2 with traffic management, parking, warehousing and a digital market platform. The Davgara bus park becomes the logistics node once routing is enforced. The Chamber registry line adds a business formalisation drive, because 489 of the 1,219 firms sit in the others and services category and the informal retail is unregistered. The digital commerce line follows the smart city budget, with an online wholesale catalogue for the bazaar traders.

5. Agro processing and the farm economy

The farm economy already produces. The orange line in Ward 6 turned one crore rupees last year. The livestock line counts 77,971 chickens, 13,991 goats and 6,509 buffaloes, and fish production reaches 39,600 kilograms in Wards 3, 4, 12 and 13. What is missing is the processing and the market link. The plan creates agro processing clusters in the corridor wards, one dairy and juice line, one spice and herb line for the timmur and ginger of Wards 9 and 11, and one feed mill for the poultry belt. The community discussions proposed a single orange processing unit in Wards 5 to 7, and the siting study will test a Ward 6 collection hub feeding the corridor plant, so the orchard belt gets the first link of the

chain even though the main plant sits where trucks can run. The irrigation line matters too, only one quarter of farmland is irrigated, so the plan adds the small scale storage and drip schemes the hill wards can actually maintain, with a high value crop identification round for each ward.

Table 5.57. Agro processing value chain by product

Product	Source wards	Current volume	Processing type	Target market	NPR crore
Orange juice and marmalade	6, 5, 7	1 crore sales/year	Juice line, packaging	Regional retail, Pokhara	8.0
Dairy and cheese	7, 8, 9, 10	6,509 buffaloes	Milk processing, packaging	Baglung, Myagdi	10.0
Spice and herb (timmur, ginger)	9, 11	Small volume	Drying, grading, packaging	National wholesale	6.0
Poultry feed mill	3, 6, 8	77,971 chickens	Feed formulation, bagging	Local farmers	5.0
Fish processing	3, 4, 12, 13	39,600 kg	Cold storage, packaging	Regional retail	4.0
Total agro processing					33.0

Source: Baglung IUDP team estimates from EDP sheet and field survey. Private sector share is significant.



Figure 5.41. Livestock shed and farm house cattle, the buffalo line that feeds the proposed dairy cluster. Photo: Baglung Group field team, 2082 BS.



Figure 5.42. Farm machine, rice thresher, the mechanisation gap the processing clusters and MSME line address. Photo: Baglung Group field team, 2082 BS.

Table 5.58. Economic programme cost summary

Programme	Capital (NPR crore)
Ward 2 logistics, parking and digital market	25.0
Agro processing clusters in Wards 13 and 14	40.0
Irrigation and farm storage, hill wards	35.0
Business formalisation and MSME support	8.0
Skills training tied to tourism and agro lines	12.0
Total economic	120.0

Source: Baglung IUDP team unit rate estimates, EDP sheet data and BCCI registry.



Figure 5.43. Fish pond with protective netting, the aquaculture line that produced 39,600 kilograms last year. Photo: Baglung Group field team, 2082 BS.

5. Workforce and the youth question

The youth drain will not reverse with a slogan. The plan ties every training line to a revenue line. Skills certification in river guiding, bungy operations, cable car maintenance and homestay management feeds the tourism chapter. Agro processing skills feed the clusters. Pre departure counselling for the youth who still leave, and a return investment product for the remittance economy, complete the loop. The 15 to 34 pool holds at about 20,500 and replenishes from the 5 to 14 bulge, so the window is the next five years.

5. Logical framework

Table 5.59. Logframe matrix (LFM), Economic Development Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Resilient, competitive and inclusive local economy		Farm income up 20 percent and 1,000 placed by 2031	Municipal annual report and scorecard	R1: Remittance pull on youth continues (High probability, Medium impact)
Project Purpose Economy diversified beyond retail into processing and tourism by 2031		2 clusters producing, logistics hub open, routing enforced	BCCI registry, cluster production records, placement tracking	R2: Road closures disrupt market access (Medium probability, High impact)

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Expected Outputs (Results) - Ward 2 logistics hub operating - Three agro processing clusters producing - 1,000 youth trained and placed	●	3 clusters, cold storage live, placement above 70 percent	BCCI registry, cluster production records, placement tracking	R3: Cluster investors do not come (Medium probability, High impact)
Activities - Build logistics and parking - Establish clusters - Run tied skills training			Project completion reports	R4: Crop disease or climate shock hits orchards (Medium probability, Medium impact)
Inputs NPR 55.0 crore phase one 2026 to 2031 of NPR 120.0 crore over three phases, municipal, federal and private sources		Economic programme utilisation above 85 percent	Budget red book and financial reports	R5: Trainees migrate after certification (Medium probability, Medium impact)

Source: Baglung IUDP team, 2082 BS.

5. Assumptions and risk response

Six assumptions carry the economic plan. The deepest is the remittance pull, scored high probability and medium impact because no municipal plan reverses a national labour market. The plan manages it by making the local option real rather than by arguing against the foreign one.

LFA: Assumptions and Risks: Response



Figure 5.44. Assumptions and risks response matrix, Economic Development Plan. Baglung IUDP team, 2082 BS.

Table 5.60. Risk register, Economic Development Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Remittance pull on youth continues	High	Medium	Mitigate and create contingency plan	Placement guaranteed training seats, return investment product, economic development section
R2	Road closures disrupt market access	Medium	High	Mitigate and create contingency plan	Cluster siting on the corridor, cold storage buffer stock, DRRM committee
R3	Cluster investors do not come	Medium	High	Mitigate and create contingency plan	Shell buildings first, anchor tenant recruitment through BCCI, phased cluster build, PPP cell
R4	Crop disease or climate shock hits orchards	Medium	Medium	Mitigate	Crop insurance linkage, variety diversification, agriculture

					section
R5	Trainees migrate after certification	Medium	Medium	Mitigate	Placement bonds with employers, wage benchmark review, skills section
R6	Land speculation prices out the clusters	Medium	Medium	Mitigate	Municipal land bank of Chapter 5.1, cluster zoning in the bylaws, planning section

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.61. Implementation summary, Economic Development Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Ward 2 logistics and parking, first two agro clusters, irrigation and storage start, formalisation drive	55.0
Phase 2	2031 to 2036	Balewa logistics completion, third cluster, feed mill, digital market scale up	45.0
Phase 3	2036 to 2041	Value chain consolidation, MSME incubation handover to the Chamber	20.0
Total			120.0

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent.

5. Conclusion

The economic plan does not try to invent a new economy. It connects the one that exists, the oranges, the buffalo milk, the timmur, the poultry and the fish of the hill wards, to the processing, storage and market they lack, and it gives the trade core of Ward 2 the logistics it needs to keep its regional role. The honest measure of success is placement, a thousand young people in jobs that exist because this plan built their workplace.

5. Financial Development Plan

5. Goal, objectives and strategy

The goal of the financial plan is sustainable fiscal autonomy. Its purpose in the first phase is an own source revenue line growing fast enough to fund the plan's municipal share without betting on grants that keep shrinking. The strategy rests on three moves.

- Expand the base, not the rate. The GIS property register, the leasing contracts and the tourism royalties add taxpayers and payers instead of squeezing the existing ones harder.
- Make the assets pay. The Davgara bus park services its own debt the day routing is enforced, and the corridor leases do the same for the tourism land.
- Pool the capital. The tukra yojana parcels end, and the NPR 10.4 crore of ward and municipal allocations moves to the corridor works where money actually scales.

Strategic priority. Three moves. Pool the fragmented ward allocations into trunk projects. Commercialise the Davgara bus park to service its debt. Expand own source revenue with GIS property tax, PPP leasing and the riverbed levies.

5. Present condition and constraints

The fiscal base is improving and still fragile. The approved budget of FY 2083/84 totals NPR 114.95 crore, down 12.2 percent from the year before because federal grants shrank. Own source revenue rose 21.7 percent to NPR 18.00 crore and the autonomy rate, internal revenue plus revenue sharing as a share of the budget, improved from 23.6 to 29.2 percent. The structure is the problem, 70.8 percent of the budget depends on intergovernmental transfers, the TDF debt on the Davgara bus park commits NPR 3.50 crore a year, and the capital dilutes into small ward parcels.

Table 5.62. SWOT analysis, Financial Development Plan

	Positive	Negative
Internal strengths	Own source revenue rose 21.7 percent to NPR 18.00 crore in FY 2083/84, autonomy rate improved from 23.6 to 29.2 percent, GIS property map ready from team work, digital tax system ongoing, business formalisation drive from economic chapter, approved budget NPR 114.95 crore	Budget shrank 12.2 percent because federal grants fell, 70.8 percent of budget depends on intergovernmental transfers, TDF debt on Davgara bus park commits NPR 3.50 crore a year, budget utilisation at 70.95 percent, capital diluting into small ward parcels
Internal weaknesses	Revenue structure dependent on federal transfers, no tourism royalty stream yet, riverbed material leasing not yet formalised, property tax GIS coverage incomplete, heavy vehicle levy not yet enforced, service charges under collected	Ward allocations fragmented into tukra yojana parcels, procurement capacity limited, financial reporting not yet digitised, audit backlog, no medium term expenditure framework
External opportunities	GIS property tax extendable to unregistered units in core, riverbed material leasing on Kali Gandaki and Kathekhola now policy open in FY 2083/84, tourism royalties starting in year two, commercialisation of Davgara bus park, Town Development Fund debt facility for trunk works	Federal grants shrank 14.5 percent in FY 2083/84, provincial transfers uncertain, TDF debt servicing competing with new investment, donor fatigue for municipal infrastructure, population decline reducing the grant base
External threats	Federal fiscal transfers declining as the primary revenue source, TDF debt on Davgara bus park creating structural deficit, ward political resistance to pooling allocations, inflation increasing construction costs, exchange rate risk on imported materials for flagship projects	Political cycles interrupting revenue reform, compliance risk on property tax expansion, tourism revenue dependent on operator performance, climate disasters requiring emergency capital reallocation, economic slowdown reducing tax base

Source: Baglung IUDP team analysis from FDP, municipal budget FY 2083/84, TDF records and field survey, 2082 BS.

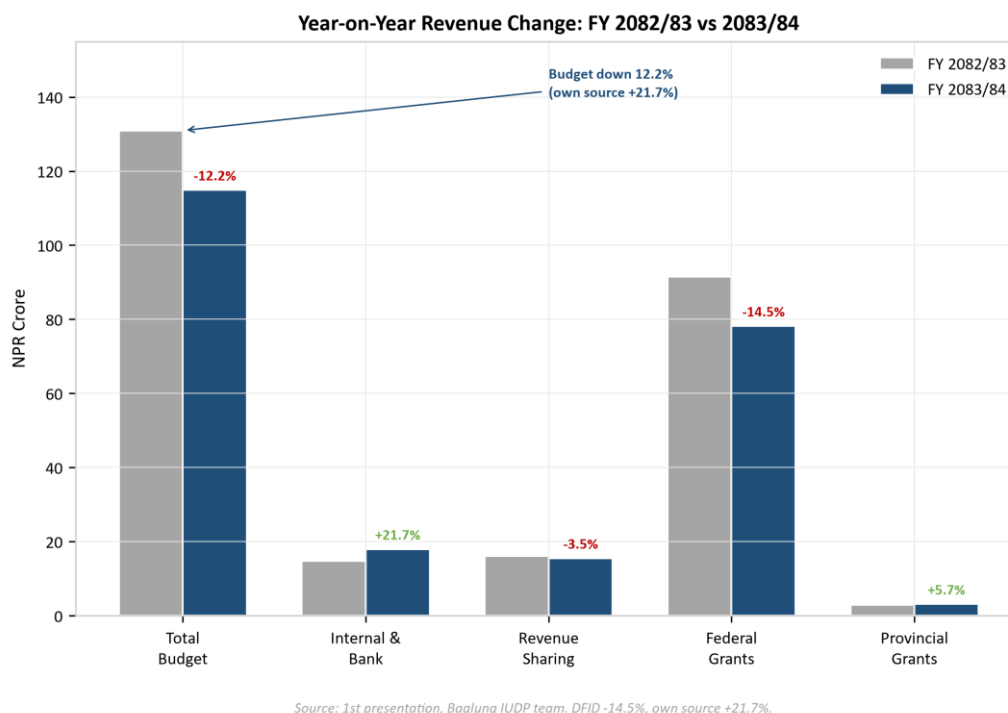


Figure 5.45. Year-on-year revenue change, FY 2082/83 to 2083/84. Federal grants fell 14.5 percent while own source rose 21.7 percent.

5. Problem analysis

Four causes hold the fiscal base down. Seven in ten rupees arrive as transfers, the Davgara debt takes NPR 3.5 crore a year while the park earns nothing, the property register is incomplete without GIS, and the ward allocations fragment what little capital remains. The core problem is a fiscal base dependent on transfers with its own capital scattered. The effects are the 12.2 percent single year budget fall, a bus park that cannot service its own loan, and trunk projects that cannot be funded at all.

PROBLEM ANALYSIS: THE PROBLEM TREE

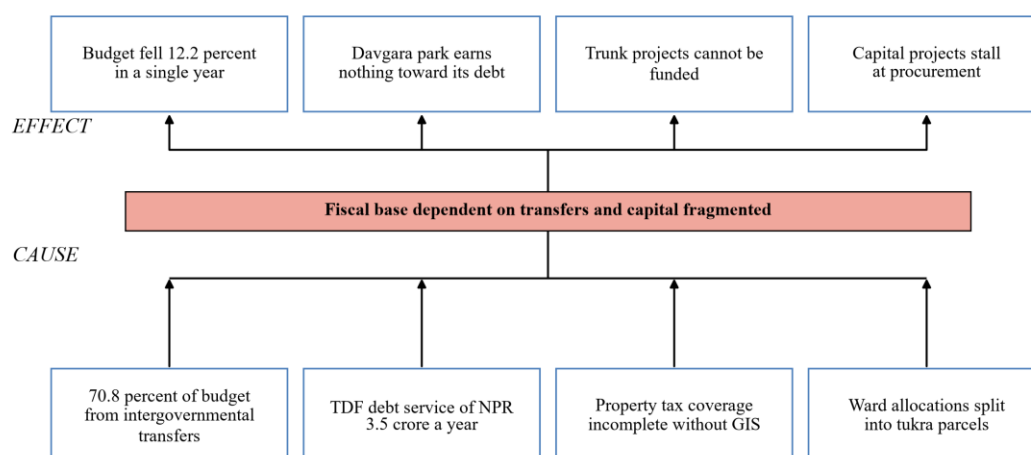


Figure 5.46. Problem analysis tree, Financial Development Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree sets one number, own source revenue at forty percent of the budget by 2031. The means are the GIS property tax with digital collection, riverbed and material leasing under EIA based contracts, tourism royalties from year two, and the pooling of ward allocations into corridor works. The ends are autonomy up from 29.2 to forty percent, the Davgara debt serviced from operations, and zero new tukra parcels.

OBJECTIVE ANALYSIS

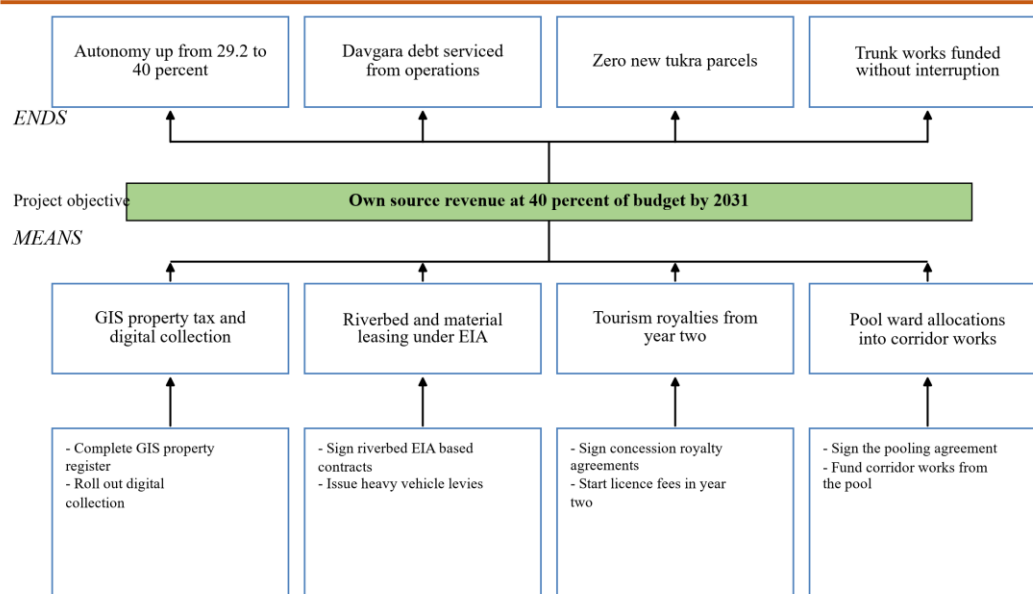


Figure 5.47. Objective analysis tree, Financial Development Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Raising rates on the existing base is fast and politically expensive, and it exhausts a base that is already compliant. Borrowing against future transfers merely mortgages the structural problem. Expanding the base with the GIS register, the leasing contracts and the royalty streams is slower but compounding, and it is the option adopted.

Table 5.63. Alternative options scored against five criteria, Financial Development Plan

Criterion	A. Raise rates on existing base	B. Expand the base with GIS and new streams	C. Borrow against future transfers
Cost efficiency	Low	High	Low
Chance of success	Medium	High	Low
Speed of delivery	High	Medium	Low
GESI impact	Low	Medium	Low
Environmental risk	Medium	High	Low
Total score (1 to 3 per criterion)	9	13	5

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Raise tax rates on the existing base	Low	Medium	High	Low	Medium	9
Expand the base with GIS and new streams	High	High	Medium	Medium	High	13
Borrow more against future transfers	Low	Low	Low	Low	Low	5

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.48. *Alternative analysis heat grid, Financial Development Plan. Baglung IUDP team, 2082 BS.*

5. Plan and programmes


5. Revenue mobilisation

The revenue plan has five lines. First, the GIS property map, already possible from the team GIS, extends property tax to the unregistered units of the core. Second, the digital tax system continues and adds the business formalisation drive from the economic chapter. Third, the riverbed material leasing on the Kali Gandaki and Kathekhola follows the EIA and IEE based contracts the FY 2083/84 policy already opens. Fourth, the heavy vehicle levy pays the road damage it causes. Fifth, the tourism royalty stream from Chapter 5.5 starts flowing in year two of the first phase.

Table 5.64. Own source revenue path, 2026 to 2031

Revenue line	FY 2083/84 (NPR crore)	2031 target (NPR crore)
Property tax with GIS coverage	3.50	7.50
Business and enterprise tax	4.20	6.50
Riverbed and natural material leasing	0.80	2.50
Tourism royalties and licenses	0.00	4.00
Vehicle and infrastructure levies	0.50	1.50
Service charges and fees	2.00	3.00
Other own source items, incl. one time bank balance	7.00	0.00
Total own source	18.00	25.00

Source: Baglung IUDP team estimates on the municipal budget red book FY 2083/84. The FY 2083/84 column reconciles to the NPR 18.00 crore internal revenue and bank balance line of Chapter 3, of which NPR 7.00 crore is one time bank balance and is not counted in the recurrent 2031 target. Targets are planning estimates.

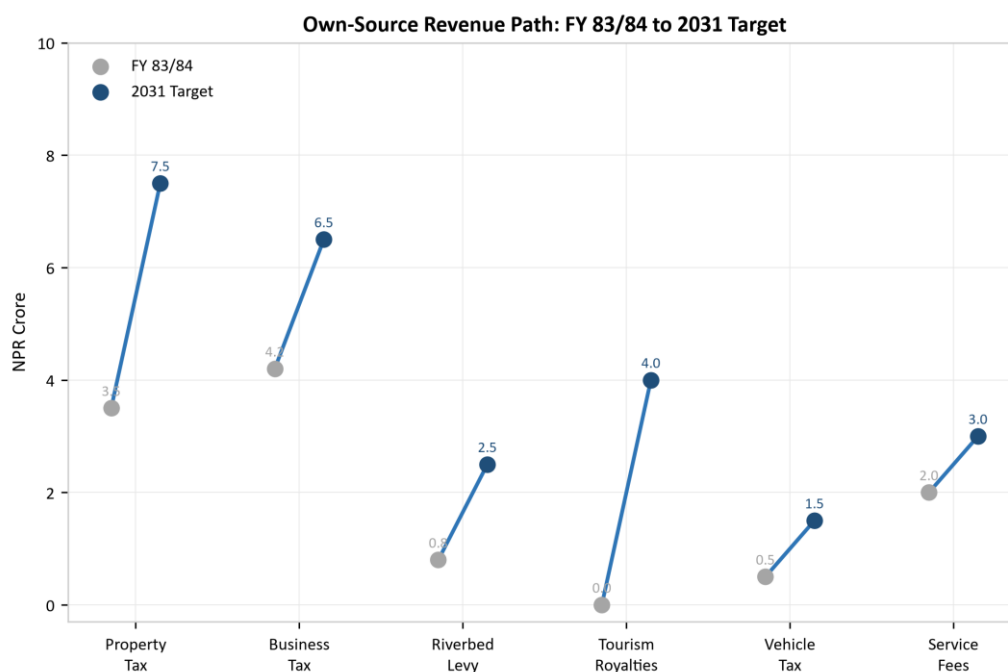

Source: Baglung IUDP team estimates, Table 5.20. Planning accuracy plus or minus 30 percent.

Figure 5.49. Own-source revenue slope from FY 2083/84 to 2031 target. Tourism royalties are the new line, growing from zero to NPR 4 crore.

5. Expenditure reform

The expenditure side is the other half of the autonomy problem. The plan ends the tukra yojana by pooling the NPR 6.40 crore ward allocations and the NPR 4.00 crore municipal pool into the corridor projects of Chapter 5.1. The debt is serviced by enforcing bus routing at the Davgara park so the terminal earns. The under execution problem, 70.95 percent budget utilisation in FY 81/82, gets a procurement and capacity line in the institutional chapter.


5. Logical framework

Table 5.65. Logframe matrix (LFM), Financial Development Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Sustainable fiscal autonomy		Own source share 40 percent in the FY 2031/32 red book	Municipal annual report and scorecard	R1: Compliance backlash on new tax lines (Medium probability, Medium impact)
Project Purpose Own source revenue from 29.2 to 40 percent of budget by 2031	●	Collection at 85 percent of billed, park revenue NPR 3.5 crore	Annual audit, revenue ledger, project completion reports	R2: Federal transfers fall faster than assumed (Medium probability, High impact)

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Expected Outputs (Results) - GIS property register and digital collection live - Leasing and royalty streams contracted - Capital pooled into trunk projects	●	Register complete, leasing and royalty contracts signed	Annual audit, revenue ledger, project completion reports	R3: Council reverses the pooling decision (Medium probability, High impact)
Activities - Complete GIS property map - Sign leasing contracts - Enforce pooling in the budget call		Reform milestones per annual revenue plan	Project completion reports	R4: Royalty flows start later than year two (Medium probability, Medium impact)
Inputs Funded from revenue gains, no separate capital line		Revenue gains tracked in the annual audit	Budget red book and financial reports	R5: Audit findings block new borrowing (Low probability, Medium impact)

Source: Baglung IUDP team, 2082 BS.

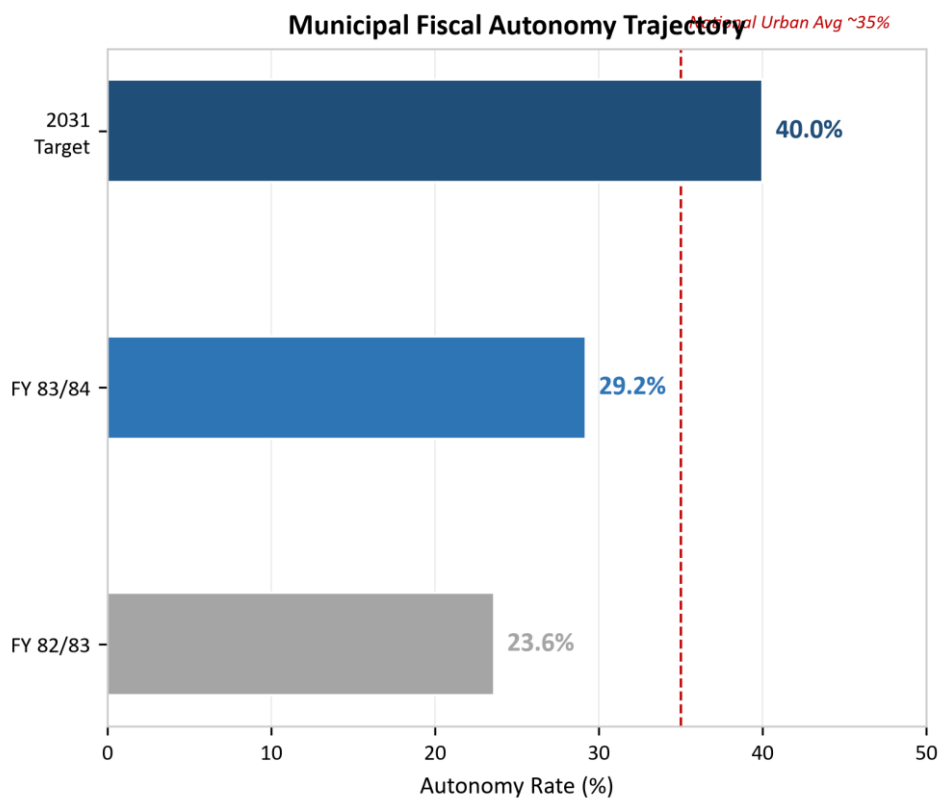

Source: 1st presentation, Baglung IUDP team. FY 82/83 to 83/84 observed; 2031 target.

Figure 5.50. Municipal fiscal autonomy trajectory from 23.6 to 29.2 to the 40 percent target by 2031.

5. Assumptions and risk response

Six assumptions carry the financial plan, and two are political. The council can reverse the pooling decision after the election that follows the plan's adoption, and the federal transfers can fall faster than the revenue reform can compensate. Both carry contingency plans, a phased pooling schedule signed before the budget call, and a trunk works programme that can pause between packages without abandoning works half built.

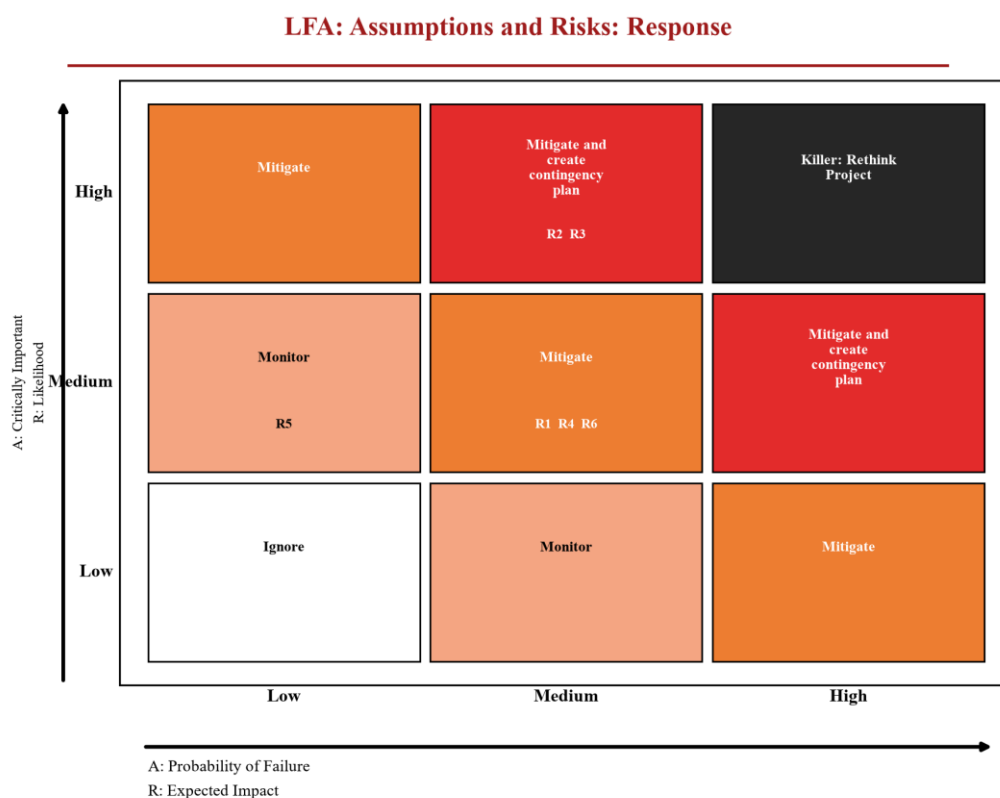


Figure 5.51. Assumptions and risks response matrix, Financial Development Plan. Baglung IUDP team, 2082 BS.

Table 5.66. Risk register, Financial Development Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
R1	Compliance backlash on new tax lines	Medium	Medium	Mitigate	Phased rollout with public hearings, grievance desk, revenue section
R2	Federal transfers fall faster than assumed	Medium	High	Mitigate and create contingency plan	Trunk works packaged to pause cleanly, TDF window reserved, finance section
R3	Council reverses the pooling decision	Medium	High	Mitigate and create contingency plan	Pooling agreement signed before the budget call, ward benefit statement

					published annually, executive office
R4	Royalty flows start later than year two	Medium	Medium	Mitigate	Concession schedule with signing deadlines, interim licence fees, tourism cell
R5	Audit findings block new borrowing	Low	Medium	Monitor	Audit clearance plan in year one, TDF liaison, finance section
R6	Inflation erodes the revenue targets	Medium	Medium	Mitigate	Annual rate indexation clause, unit rate revision, revenue section

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.67. Implementation summary, Financial Development Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	GIS property register, digital collection, leasing contracts, royalty agreements, pooling agreement	0.0
Phase 2	2031 to 2036	Revenue system consolidation, medium term expenditure framework	0.0
Phase 3	2036 to 2041	Fiscal autonomy consolidation, review of rates and bases	0.0
Total			0.0

Source: MSIP Table 6.1, Baglung IUDP team. The financial plan is a reform programme carried by the revenue gains it produces, so it carries no separate capital line.

5. Conclusion

Every other chapter of this plan spends money. This one raises it. The path from 29.2 to forty percent own source revenue runs through a property register that already exists as a GIS layer, a leasing policy the budget already opens, and a royalty stream the flagship concessions create. The plan's fiscal honesty is its protection, it commits only what the base can plausibly deliver, and it names the two political risks that could stop it.

5. Institutional Development Plan

5. Goal, objectives and strategy

The goal of the institutional plan is a municipally led, technically capable government. Its purpose in the first phase is that the planning, GIS and PPP functions exist inside the municipality, because every flagship in this plan fails if it must be run forever by outside consultants. The strategy rests on three moves.

- Recruit the four technical posts in year one and train twenty staff against them, using the federal paperless governance budget as the entry funding.
- Build the data bank and the GIS property database before the projects need them, so the permits, the taxes and the scorecard all draw on one base.
- Stand up the PPP cell with the concession pipeline of Chapter 5.5 as its first caseload, and a GESI desk with participation targets beside it.

Strategic priority. Build the in house planning and GIS capacity so that the flagship projects become municipally led. Use the federal paperless governance budget of FY 2083/84 as the entry point.

5. Present condition and constraints

The institutional base is mature on paper and thin in people. The municipality holds 72 local laws, runs a LISA governance score of 84 out of 100 and carries a sister city partnership with Windham Eco Global Village in Australia. The gaps are technical. Planning and GIS positions sit vacant, the spatial database is incomplete, and the flagship projects, Panchakot and the Kundule temple, run on external money and external management. Women's participation in decision making remains thin.

Table 5.68. SWOT analysis, Institutional Development Plan

	Positive	Negative
Internal strengths	72 local laws in place, LISA governance score 84 out of 100, sister city partnership with Windham Eco Global Village in Australia, citizen charter displayed in core wards, public hearings held annually, digital e governance system partial in Ward 2	Planning and GIS positions sit vacant, spatial database incomplete, flagship projects Panchakot and Kundule temple run on external money and management, women participation in decision making thin, ward office staffing gaps across 14 wards
Internal weaknesses	No in house planning and GIS capacity, data bank not yet operational, procurement capacity limited, coordination with line agencies occasional in most wards, annual planning not yet fully participatory in rural wards, grievance handling mechanism incomplete	Municipal data not yet integrated into decision support system, staff training programme not systematic, PPP and project management cell not yet established, GESI desk not yet functional, budget for institutional programme only NPR 8.3 crore
External opportunities	Federal paperless governance budget in FY 2083/84 as entry point, GIS technology now affordable for property mapping, digital platforms enabling citizen engagement, sister city partnership offering technical exchange, federal planning standards providing the framework	Staff turnover in technical positions, federal institutional reform mandates competing with local capacity, political interference in procurement, donor driven projects bypassing municipal systems, capacity building programmes not yet linked to performance
External threats	Technical staff attracted to	Population decline reducing the

	Kathmandu and Pokhara salaries, budget cuts to institutional programme in lean years, political cycles disrupting continuity of reform, federal mandates arriving faster than implementation capacity, corruption risks in PPP procurement	administrative base, ward political dynamics resisting centralisation of planning, coordination failures between municipal and ward levels, data privacy and security concerns in digital systems, climate disasters requiring rapid institutional response
--	--	---

Source: Baglung IUDP team analysis from IDP, LISA assessment, field survey and institutional review, 2082 BS.

5. Problem analysis

Four causes keep the institution thin, the vacant planning and GIS posts, the incomplete spatial database, flagship projects managed from outside, and women under represented in decision making. The core problem is a municipality mature on paper but dependent on outsiders for its technical work. The effects are project dependence on consultants, budgeting that cannot be data driven, and a GESI duty that remains under delivered.

PROBLEM ANALYSIS: THE PROBLEM TREE

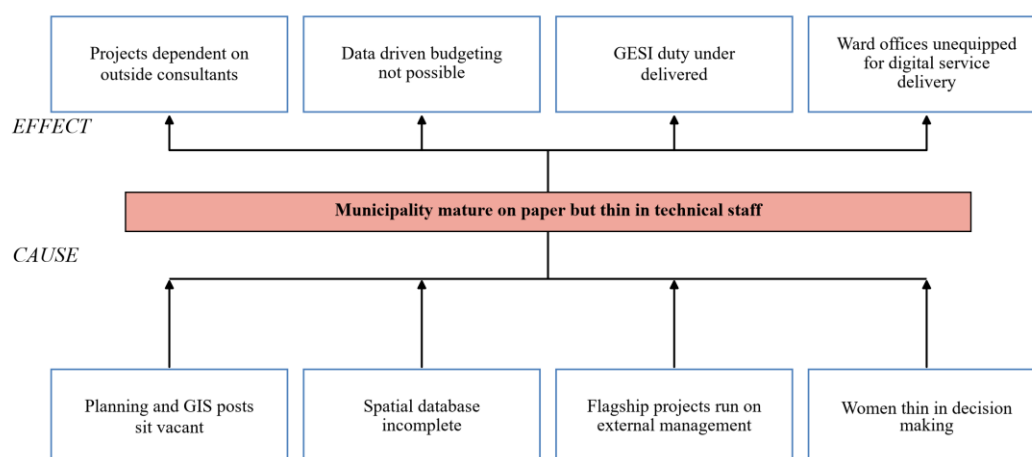


Figure 5.52. Problem analysis tree, Institutional Development Plan. Baglung IUDP team, 2082 BS.

5. Objective analysis

The objective tree targets in house planning, GIS and PPP capacity by 2031. The means are the four technical posts, the data bank with its decision support system, the PPP and project management cell, and the GESI desk with participation targets. The ends are flagships led by the municipality, a scorecard fed by municipal data, and half the seats in ward committees held by women.

OBJECTIVE ANALYSIS

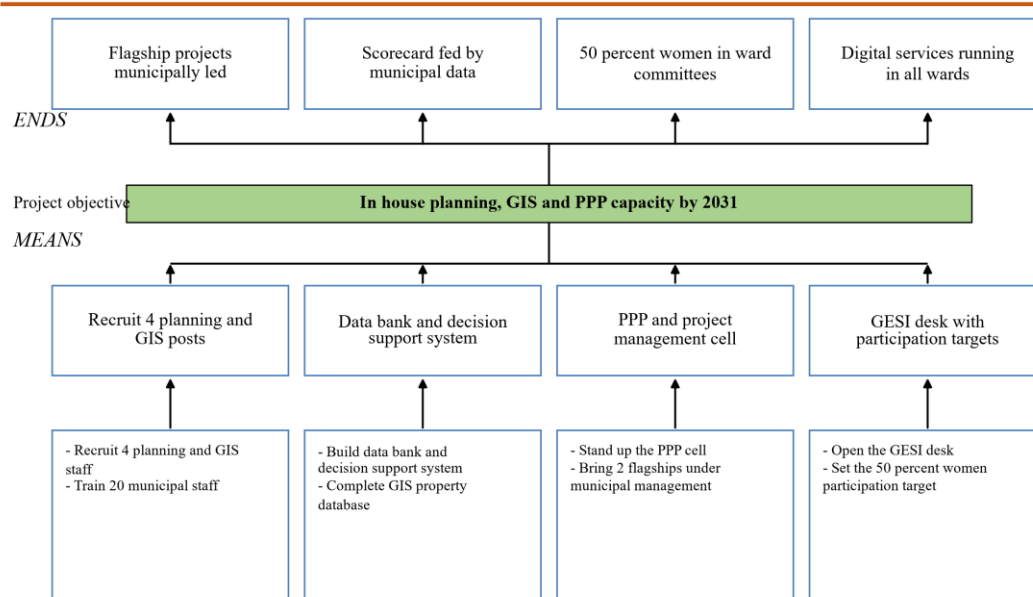


Figure 5.53. Objective analysis tree, Institutional Development Plan. Baglung IUDP team, 2082 BS.

5. Alternative analysis

Outsourcing planning to consultants delivers drawings but no capability, and it is the habit this plan exists to break. Waiting for provincial deputation is waiting. Building the in house capacity costs more in the first budget and less in every budget after.

Table 5.69. Alternative options scored against five criteria, Institutional Development Plan

Criterion	A. Outsource to consultants	B. Build in house capacity	C. Wait for provincial deputation
Cost efficiency	Medium	High	Low
Chance of success	Low	High	Low
Speed of delivery	High	Medium	Low
GESI impact	Low	High	Low
Environmental risk	Medium	High	Low
Total score (1 to 3 per criterion)	9	14	5

Source: Baglung IUDP team scoring, 2082 BS.

ALTERNATIVE ANALYSIS

	Cost efficiency	Chance of success	Speed of delivery	GESI impact	Environmental risk	Total score
Outsource planning to consultants	Medium	Low	High	Low	Medium	9
Build in house capacity	High	High	Medium	High	High	14
Wait for provincial deputation	Low	Low	Low	Low	Low	5

Criteria scored 1 to 3 per criterion from sector evidence. Chosen option outlined in dark red.

Figure 5.54. Alternative analysis heat grid, Institutional Development Plan. Baglung IUDP team, 2082 BS.

5. Plan and programmes

Table 5.70. Ward wise staffing gap and e governance readiness

Ward	Sanctioned staff	Filled	Vacancy	e governance	Priority action
1	5	3	2	No	Fill vacancies, digital revenue
2	12	10	2	Yes (high)	Maintain, expand GIS
3	6	5	1	Partial	Complete digital system
4	5	4	1	Partial	Complete digital system
5	4	4	0	No	Install basic digital system
6	4	4	0	No	Install basic digital system
7	4	4	0	No	Install basic digital system
8	4	4	0	No	Install basic digital system
9	4	4	0	No	Install basic digital system
10	4	4	0	No	Install basic digital system
11	3	3	0	No	Install basic digital system
12	5	4	1	Partial	Complete digital system
13	4	4	0	No	Install basic digital system
14	4	4	0	No	Install basic digital system

Source: IDP sheet, Baglung IUDP DataSets. Total vacancy across municipality is 7 posts.

Table 5.71. Institutional programme

Work	Quantity	Unit rate (NPR)	Cost (NPR crore)
Planning and GIS staff recruitment	4 posts	0.25 crore per year	1.00
Staff training on GIS, e governance and procurement	5 years	0.3 crore per year	1.50
Municipal data bank and decision support system	1 system	lump sum	2.00
GIS property and infrastructure database	1 project	lump sum	1.50
Women's participation and GESI desk	5 years	0.2 crore per year	1.00
PPP and project management cell	5 years	0.25 crore per year	1.25
Total institutional			8.25

Source: Baglung IUDP team estimates and the municipal institutional review, 2082 BS.

5. Logical framework

Table 5.72. Logframe matrix (LFM), Institutional Development Plan

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Overall Goal (Objective) Municipally led, technically capable government		4 posts filled and 2 flagships under municipal management	Municipal annual report and scorecard	R1: Trained staff poached by higher tiers (High probability, Medium impact)
Project Purpose Technical gaps filled and services digitised by 2031	●	GIS database live, scorecard fed by municipal data from 2030	Staff records, training reports, system logs	R2: Budget for new posts delayed (Medium probability, Medium impact)
Expected Outputs (Results) - 4 technical posts filled and 20 staff trained - Data bank and GIS database live - PPP cell managing the flagships	●	20 staff trained, PPP cell running, GESI desk open	Staff records, training reports, system logs	R3: Political turnover disrupts reform (Medium probability, High impact)

Narrative Summary		Objectively Verifiable Indicators	Means (Source) of Verifications	Important Assumptions (and Risks)
Activities - Recruit and train - Build data systems - Stand up the PPP cell		Recruitment and systems per annual establishment plan	Project completion reports	R4: Systems unused without training (Medium probability, Medium impact)
Inputs NPR 8.3 crore phase one 2026 to 2031, municipal and federal paperless governance funds		Institutional budget utilisation above 85 percent	Budget red book and financial reports	R5: Procurement challenges slow the PPP cell (Low probability, Medium impact)

Source: Baglung IUDP team, 2082 BS.

5. Assumptions and risk response

Six assumptions carry the institutional plan. The sharpest is staff retention, scored high probability of failure because the municipality trains people into the exact qualifications the provincial and federal tiers recruit for. The contingency is a retention package of training bonds and project authority rather than salary matching the municipality cannot win.

LFA: Assumptions and Risks: Response

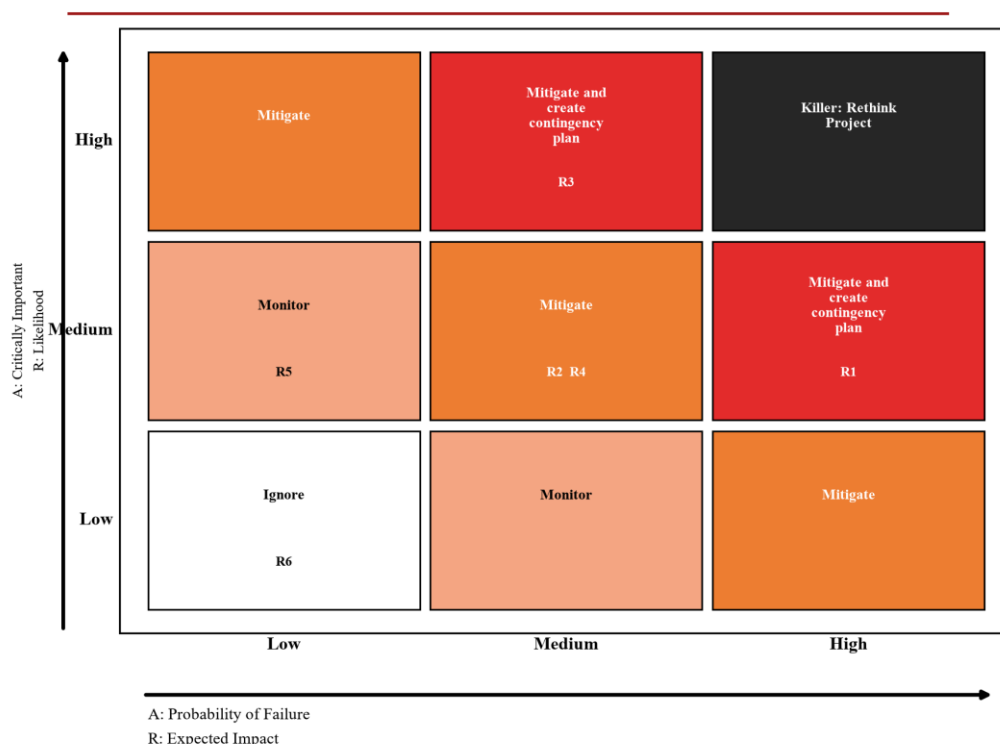


Figure 5.55. Assumptions and risks response matrix, Institutional Development Plan. Baglung IUDP team, 2082 BS.

Table 5.73. Risk register, Institutional Development Plan

ID	Assumption or risk	Probability	Impact	Response	Mitigation and owner
----	--------------------	-------------	--------	----------	----------------------

R1	Trained staff poached by higher tiers	High	Medium	Mitigate and create contingency plan	Training bonds, project authority and publication credit, retention review each year, executive office
R2	Budget for new posts delayed	Medium	Medium	Mitigate	Phase recruitment two plus two, contract staff as bridge, administration section
R3	Political turnover disrupts reform	Medium	High	Mitigate and create contingency plan	Reform items adopted as council policy not executive preference, all party orientation, municipal assembly
R4	Systems unused without training	Medium	Medium	Mitigate	Training tied to system licences, help desk in year one, IT focal person
R5	Procurement challenges slow the PPP cell	Low	Medium	Monitor	Standard concession documents, legal review retainer, PPP cell
R6	Sister city support tapers	Low	Low	Ignore	No action beyond the annual scorecard review, administration section

Source: Baglung IUDP team risk workshop, 2082 BS.

5. Implementation summary

Table 5.74. Implementation summary, Institutional Development Plan

Phase	Period	Focus	Cost (NPR crore)
Phase 1	2026 to 2031	Four posts, data bank, GIS database, PPP cell, GESI desk, training of 20 staff	8.3
Phase 2	2031 to 2036	Systems consolidation, training continuation within operating budget	0.0
Phase 3	2036 to 2041	Institutional completion and handover to operating budgets	0.0

Total			8.3
-------	--	--	-----

Source: MSIP Table 6.1, Baglung IUDP team. Planning stage plus or minus 30 percent.

5. Conclusion

The institutional plan is small money and decisive leverage. For NPR 8.3 crore the municipality buys the four functions every other chapter assumes, the planner who runs the permit, the GIS officer who feeds the tax roll, the PPP cell that signs the concessions and the GESI desk that holds the plan to its inclusion duty. If this chapter fails, the others drift back to consultants and the municipality remains a client in its own development.

6. Multi Sector Investment Plan

6.1 The fifteen year programme


The Multi Sector Investment Plan brings the eight thematic plans into one financial frame. The totals are planning stage estimates at unit rates, with an accuracy band of plus or minus 30 percent, and they are meant for budgeting, not for procurement. The programme is phased in three five year windows that match the local government cycle.

Table 6.1. MSIP summary by sector, NPR crore

Sector plan	Phase 1 (2026 to 2031)	Phase 2 (2031 to 2036)	Phase 3 (2036 to 2041)	Total
5.1 Physical	226.0	180.0	145.3	551.3
5.2 Social	32.0	21.0	13.9	66.9
5.3 Environment	18.0	9.0	5.3	32.3
5.4 Disaster risk reduction	14.0	6.0	2.6	22.6
5.5 Tourism	78.0	105.0	55.0	238.0
5.6 Economic	55.0	45.0	20.0	120.0
5.7 Financial	0.0	0.0	0.0	0.0
5.8 Institutional	8.3	0.0	0.0	8.3
Total	431.3	366.0	242.1	1,039.4


Source: Baglung IUDP team MSIP tables. Unit rate estimates, plus or minus 30 percent.

MSIP 15-Year Total by Sector, NPR Crore

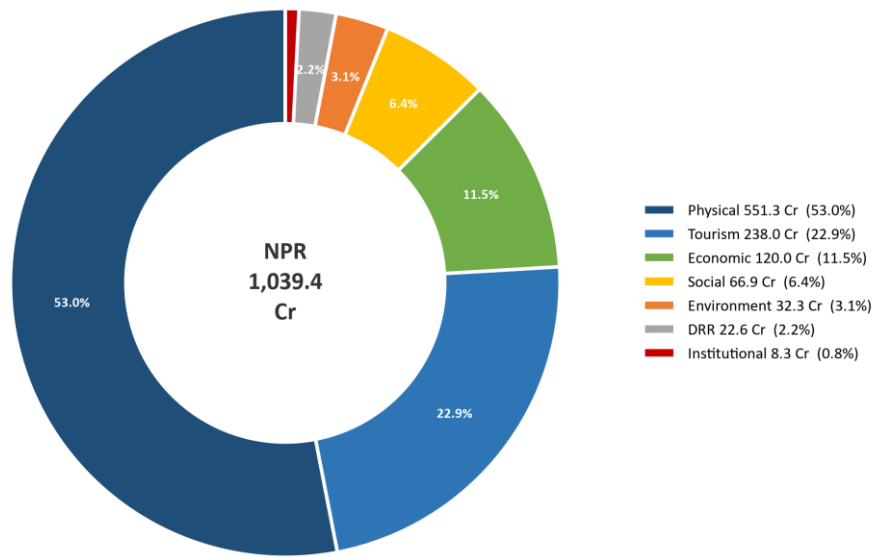

Source: Baglung IUDP team, Table 6.1. Unit rate estimates, plus or minus 30 percent.

Figure 6.1. MSIP 15-year total by sector. Physical infrastructure dominates at 53 percent, followed by tourism at 23 percent.

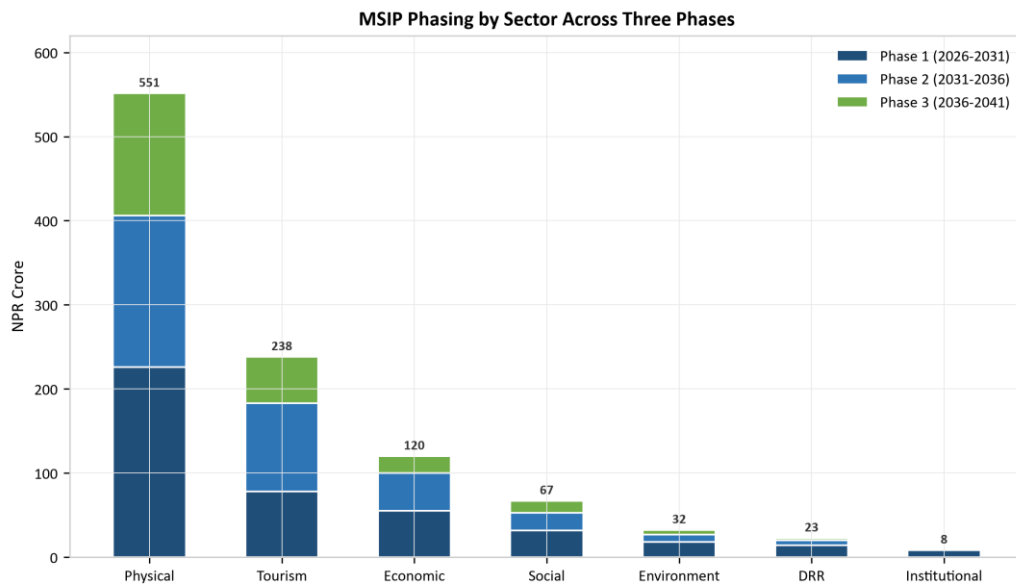

Source: Baglung IUDP team, Table 6.1. Phase 1 is the action phase.

Figure 6.2. MSIP phasing by sector across three phases. Phase 1 is the action phase at NPR 431.3 crore.

The tourism share dominates the second phase because the cable car lands there. The physical share dominates the first phase because the flood control, the water and the roads cannot wait. The split is deliberate. The first phase builds the trust and the revenue base, the second phase spends it.


6.2 Funding sources

The funding composition is built from the sector tables, not assumed. Municipal own funds and pooled ward budgets cover the public share lines in the physical, social, environment, DRR, economic and institutional plans, about NPR 260 crore. Federal and provincial transfers cover the grant eligible trunk works, about NPR 570 crore. Private and PPP capital covers the tourism programme at 65 percent and the private housing share, about NPR 180 crore. Development partners and the Town Development Fund cover the residual, about NPR 29.4 crore.

Table 6.2. Funding composition of the MSIP

Source	NPR crore	Share
Municipal own funds and pooled ward budgets	260.0	25 percent
Federal and provincial transfers	570.0	55 percent
Private and PPP capital	180.0	17 percent
Development partners and TDF	29.4	3 percent
Total	1,039.4	100 percent

Source: Baglung IUDP team estimates derived from the sector tables of Chapter 5.

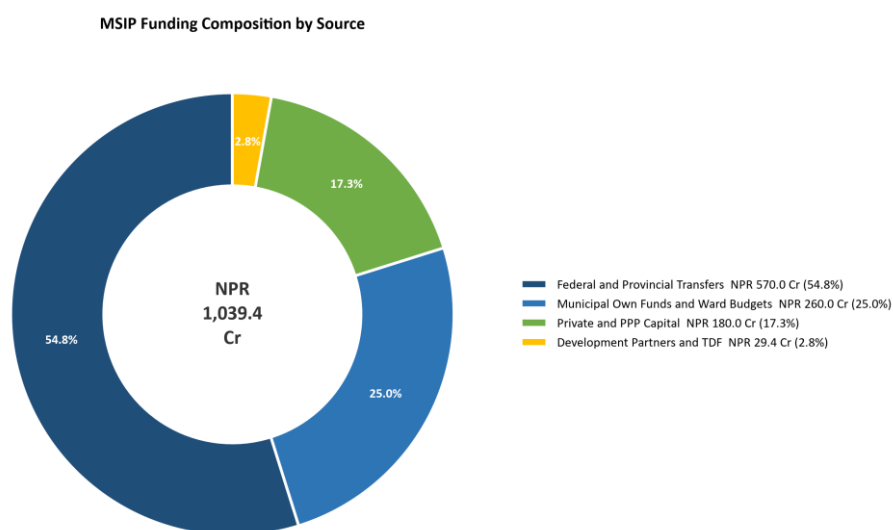

Source: Baglung IUDP team, Table 6.2. Derived from sector tables, Chapter 5.

Figure 6.3. MSIP funding composition. Federal and provincial transfers cover 55 percent, municipal own funds 25 percent, private and PPP 17 percent.

6.3 Phasing logic and the year one actions

19. Year one 2026. Approve the plan, create the PPP and tourism cell, start the bazaar flood control design, fill the GIS posts, issue the rafting and bungy expressions of interest.
20. Phase one 2026 to 2031. Flood control, water and sewerage, ward road blacktop, waste to all wards, rafting and bungy operating, heritage precinct, revenue reform, scorecard running.

21. Phase two 2031 to 2036. Cable car, agro processing clusters, Balewa logistics, second fire station, district sports facility, corridor housing.
22. Phase three 2036 to 2041. Bridge adventure hub, paragliding ridge, medical college support, institutional completion, plan review and the next IUDP cycle.

The plan review in 2031 is not optional. The census of that year resets the population base, the scorecard in Chapter 9 will show which programmes delivered, and the review decides the second phase in full knowledge of the first.

7. Flagship projects

Three projects carry the tourism and revenue wager of this plan. Each is developed here to sub project level with site logic, capital cost at unit rates, revenue model, delivery structure, risks and a full financial appraisal. The cost figures are planning stage estimates, plus or minus 30 percent, and each project needs a full DPR and environmental assessment before procurement. The site logic in each case was checked against the GIS rasters of Chapter 4. The appraisal in each section prices the concession from the operator side, states the municipal fiscal flow separately, and is honest about which projects are bankable and which are not.

7. Kali Gandaki rafting corridor

7. Concept and site logic

The corridor runs about 25 kilometres of the Kali Gandaki from the Balewa put in near Ward 13 down to the Ramrekha take out near Ward 1. The river reach holds grade two to three water through the gorge, the same stretch the operators already use above Kushma, and the monsoon months deliver the flow. The flood rasters of Chapter 4 were used to place the put in and take out above the modelled flood line, because the river is the hazard as much as the asset.



Figure 7.1. *The Kali Gandaki gorge from the bazaar plateau, the river corridor for the rafting product. Photo: Wikimedia Commons, (c) Michal Salaban, CC BY-SA 2.5, 2026.*

The product bundle has five parts. The river infrastructure, the put in ramp at Balewa, the take out ramp at Ramrekha, the changing rooms and the guard posts. The fleet, twelve rafts with full safety gear. The people, a guide training line that certifies local youth through the Nepal Rafting Association standard. The system, a booking desk, a river gauge and a weather and flow rule that stops trips in flood. The link, the shuttle service between the two points and the homestay line in the corridor wards.

7. Capital cost and revenue

Table 7.1. Rafting corridor capital cost

Item	Quantity	Unit rate (NPR)	Cost (NPR crore)
Put in and take out ramps with access roads	2 sites	2.5 crore each	5.00
Facility buildings, changing rooms, guard posts	2 sites	1.0 crore each	2.00
Raft fleet and safety gear	12 rafts	0.3 crore per raft	3.60
River gauge and early warning	2 stations	0.25 crore each	0.50
Guide training and certification	40 guides	0.1 crore each	4.00
Booking system, signage, marketing	lump sum	lump sum	3.00
Shuttle service establishment	2 vehicles	0.45 crore each	0.90
Environmental works and tree line	lump sum	lump sum	1.00
Total			20.00

Source: Baglung IUDP team unit rate estimates.

The revenue model is conservative. The visitor range starts from the national rafting market, about 30,000 to 40,000 commercial trips a year across the Trisuli, Bhote Koshi and Marsyangdi runs (Nepal Tourism Statistics, 2023), and discounts for the hill access and the shorter season, which lands the Baglung range at 3,000 rafters in year one growing to 8,000 by year five. At an average trip price of NPR 6,000, the gross sits between NPR 1.8 and 4.8 crore a year. The municipal take is the lease, the ramp fees and the guide certification fees, about 12 to 15 percent of gross, which is NPR 0.5 to 0.7 crore a year at build out. The homestay nights in Wards 10, 13 and 14 add the community share that the plan tracks separately.

7. Delivery and risks

- Delivery. A private operator under a 10 year concession on municipal land, with the municipality holding the ramps and the safety standard.
- Risk one, flood. Managed by the gauge and flow rule, the take out above the flood line, and a full season calendar that respects the monsoon.
- Risk two, safety. The guide certification, the life jacket regime and the emergency response plan with the district police and the hospital.
- Risk three, seasonality. The off season is covered by the heritage and agro programmes of Chapter 5.5, so the corridor is one product in a circuit, not the circuit itself.

- Risk four, river competition. The corridor must price below the Trisuli packages and above the cost line, with the gorge as the differentiator.

7. Financial appraisal

The appraisal runs the concession over ten years at a 12 percent discount rate, with the operator loan priced at 10 percent and equity expected to earn 15 percent. The municipal grant of NPR 7.0 crore builds the public ramps and works, so the concession IRR is computed on the operator capital of NPR 13.0 crore, and the municipal return is stated separately as the fiscal flow. All figures are planning stage, plus or minus 30 percent.

Table 7.2. Rafting corridor financing structure

Source	NPR crore	Share	Terms
Municipal grant for public ramps and works	7.00	35.0 percent	Grant, no repayment
Operator equity	3.90	19.5 percent	19.5 percent of total
Operator bank loan	9.10	45.5 percent	10 percent, 8 year equal principal
Total	20.00	100 percent	

Source: Baglung IUDP team financing plan on the concession structure of Chapter 7.

Table 7.3. Rafting corridor staffing schedule

Post	Nos	Monthly NPR	Annual NPR crore
Corridor manager	1	60,000	0.07
Safety officer	2	35,000	0.08
River guide, seasonal 5 months	12	25,000	0.15
Shuttle driver	2	30,000	0.07
Booking desk	2	20,000	0.05
Total			0.43

Source: Baglung IUDP team staffing plan on Nepal Rafting Association norms.

Table 7.4. Rafting corridor revenue basis

Year	rafters	Price NPR	Fare revenue	Lease revenue	Total revenue NPR crore
Year 1	3,000	6,000	1.80	0.00	1.80
Year 2	4,000	6,000	2.40	0.00	2.40
Year 3	5,000	6,000	3.00	0.00	3.00
Year 5	8,000	6,000	4.80	0.00	4.80
Year 10	8,000	6,000	4.80	0.00	4.80

Source: demand model of Chapter 7. Volumes are rafters a year, price NPR 6,000 a trip.

Table 7.5. Rafting corridor working capital

Working capital item	NPR crore
Operating expenses, first year	0.72
Coverage assumed	30 days
Working capital requirement	0.06
Financing	Operator overdraft at 10 percent

Source: Baglung IUDP team financial model.

Table 7.6. Rafting corridor income statement, ten years

Item	Rev	Opex	EBITDA	Dep	Interest	EBT	Tax	Profit	Margin
Year 1	1.80	0.72	1.08	1.80	0.91	-1.63	0.00	-1.63	-91%
Year 2	2.40	0.96	1.44	1.80	0.80	-1.16	0.00	-1.16	-48%
Year 3	3.00	1.20	1.80	1.80	0.68	-0.68	0.00	-0.68	-23%
Year 4	3.90	1.56	2.34	1.80	0.57	-0.03	0.00	-0.03	-1%
Year 5	4.80	1.92	2.88	1.80	0.45	0.62	0.12	0.50	10%
Year 6	4.80	1.92	2.88	1.80	0.34	0.74	0.15	0.59	12%
Year 7	4.80	1.92	2.88	1.80	0.23	0.85	0.17	0.68	14%
Year 8	4.80	1.92	2.88	1.80	0.11	0.97	0.19	0.77	16%
Year 9	4.80	1.92	2.88	1.80	0.00	1.08	0.22	0.86	18%
Year 10	4.80	1.92	2.88	1.80	0.00	1.08	0.22	0.86	18%

Source: Baglung IUDP team financial model. NPR crore. Planning stage plus or minus 30 percent.

Table 7.7. Rafting corridor cash flow projection, ten years

Year	Profit	Dep	Loan principal	Maint capex	Working capital	Net cash flow	Closing balance
Year 1	-1.63	1.80	1.14	0.00	0.06	-1.03	-1.03
Year 2	-1.16	1.80	1.14	0.00	0.04	-0.53	-1.56
Year 3	-0.68	1.80	1.14	0.00	0.07	-0.09	-1.65
Year 4	-0.03	1.80	1.14	0.00	0.10	0.54	-1.11
Year 5	0.50	1.80	1.14	0.00	0.10	1.06	-0.05
Year 6	0.59	1.80	1.14	3.60	0.10	-2.45	-2.50
Year 7	0.68	1.80	1.14	0.00	0.10	1.25	-1.25
Year 8	0.77	1.80	1.14	0.00	0.10	1.34	0.09
Year 9	0.86	1.80	0.00	0.00	0.10	2.57	2.65
Year 10	0.86	1.80	0.00	0.00	0.00	2.66	5.32

Source: Baglung IUDP team financial model. NPR crore.

Table 7.8. Rafting corridor loan amortisation

Year	Opening	Interest	Principal	Closing
Year 1	9.10	0.91	1.14	7.96
Year 2	7.96	0.80	1.14	6.82
Year 3	6.82	0.68	1.14	5.69
Year 4	5.69	0.57	1.14	4.55
Year 5	4.55	0.45	1.14	3.41
Year 6	3.41	0.34	1.14	2.27
Year 7	2.27	0.23	1.14	1.14
Year 8	1.14	0.11	1.14	-0.00

Source: Baglung IUDP team financial model. NPR crore. Equal principal repayment.

Table 7.9. Rafting corridor break-even

Break-even item	Value
Price per unit NPR	6,000
Variable cost ratio	40 percent
Contribution per unit NPR	3,600
Cash fixed costs NPR crore	1.34
Full fixed costs with depreciation NPR crore	3.14
Cash break-even (rafters a year)	3,722
Full break-even (rafters a year)	8,722
Steady state volume (rafters a year)	8,000

Source: Baglung IUDP team financial model. Cash break-even excludes depreciation.

Table 7.10. Rafting corridor weighted average cost of capital

Source	NPR crore	Share of total	Cost	Weighted
Operator bank loan	9.10	45.5 percent	10.0 percent	4.55 percent
Operator equity	3.90	19.5 percent	15.0 percent	2.92 percent
Grant and municipal in kind	7.00	35.0 percent	0.0 percent	0.00 percent
Blended cost of private capital				11.50 percent
Appraisal discount rate used				12.0 percent

Source: Baglung IUDP team financial model. Equity priced at 15 percent expected return.

Table 7.11. Rafting corridor returns summary

Return measure	Value
Concession IRR on operator investment	7.9 percent

Equity IRR on operator equity	4.2 percent
Concession NPV at 12 percent, NPR crore	-2.42
Equity NPV at 12 percent, NPR crore	-2.29
Simple payback, operator investment	7.5 years
Discounted payback at 12 percent	beyond 10 years
Municipal fiscal flow at build out, NPR crore a year	0.65

Source: Baglung IUDP team financial model. Concession view on operator capital, pre tax. Grants are public capital whose return is the fiscal flow and the community income, so they sit outside the concession IRR.

Table 7.12. Rafting corridor net present value at 12 percent

Year	Net cash flow	Discount factor	Present value
Construction	-13.00	1.0000	-13.00
Year 1	1.08	0.8929	0.96
Year 2	1.44	0.7972	1.15
Year 3	1.80	0.7118	1.28
Year 4	2.34	0.6355	1.49
Year 5	2.88	0.5674	1.63
Year 6	-0.72	0.5066	-0.36
Year 7	2.88	0.4523	1.30
Year 8	2.88	0.4039	1.16
Year 9	2.88	0.3606	1.04
Year 10	2.88	0.3220	0.93
Concession NPV at 12 percent			-2.42

Source: Baglung IUDP team financial model. NPR crore, operator concession view, pre tax.

Table 7.13. Rafting corridor sensitivity analysis

Scenario	Concession IRR	Concession NPV at 12 percent
Base case	7.9 percent	-2.42
Volume minus 25 percent	1.6 percent	-5.52
Volume plus 25 percent	13.1 percent	0.68
Price minus 20 percent	3.0 percent	-4.90
Operating ratio plus 5 points	5.9 percent	-3.45
Rafters at the 10,000 upper band	22.1 percent	5.52

Source: Baglung IUDP team financial model. One variable moved at a time.

Appraisal finding. The corridor is a viable public investment and a modest private one. The concession IRR of 7.9 percent sits below the 12 percent hurdle, so the corridor will not attract capital on its financials alone, and the plan does not pretend otherwise. What justifies it is the package, the

municipal grant carries the public ramps, the operator carries the fleet, the fiscal flow of about NPR 0.65 crore a year at build out is earned on municipal capital already committed to river safety works, and the homestay line adds community income the concession does not capture. The recommendation is to proceed, with the guide training line front loaded because it is the component with the highest local employment per rupee.

7. Kali Gandaki gorge bungy

7. Concept and site logic

The bungy site sits on the Baglung bank of the Kali Gandaki gorge opposite the Kushma jump, in the Ramrekha and Maldhunga belt of Ward 1. The gorge wall there offers the vertical drop the product needs, and the site is already served by the corridor road and the Kalika precinct trail. The landslide and fault rasters of Chapter 4 were used to exclude the unstable benches, and the structure is anchored to the bedrock line the DEM shows at the gorge edge.

The product bundle has four parts. The jump structure, a steel tower and platform with the 120 to 150 metre free drop the site allows, engineered to the international bungy standard. The bridge park, the ticketing, the cafe, the photo and video line and the viewing deck. The operation, a licensed operator with a certified rigging team and a rescue protocol. The link, the heritage trail that connects the site to Kalika and the bazaar.

7. Capital cost and revenue

Table 7.14. Bungy capital cost

Item	Quantity	Unit rate (NPR)	Cost (NPR crore)
Tower, platform and anchors	1 structure	lump sum	6.50
Access road and parking	1 site	lump sum	1.50
Bridge park buildings	1 site	lump sum	2.50
Safety systems and rescue gear	lump sum	lump sum	0.80
Operator setup and certification	lump sum	lump sum	1.20
Environmental and landscape works	lump sum	lump sum	0.50
Total			13.00

Source: Baglung IUDP team unit rate estimates benchmarked against the Kushma installation.

The revenue model follows the Kushma evidence. The range of 8,000 to 10,000 jumps a year scales from the Kushma operating record, where the single jump site runs on the domestic weekend market, and adjusts for the Baglung side with the bridge park bundle. At an average of 100 jumps a day across the season and NPR 7,500 per jump, the gross runs NPR 6.0 to 7.5 crore. The municipal take is the land lease, the park entry and a royalty of about 10 percent of gross, which is NPR 0.6 to 0.75 crore a year. The photo and video line and the cafe add the margin that makes the concession attractive to an operator.

7. Delivery and risks

- Delivery. A 15 year concession with a proven operator, the municipality contributing the land and the access, the operator the structure and the licence.
- Risk one, safety. The single greatest risk of the whole plan. Mitigated by the international standard, the certified rigging team, the daily inspection log and the insurance requirement.
- Risk two, civil aviation and tourism approvals. The concession contract conditions the operator's approvals and the municipality supports the file.
- Risk three, demand. The domestic weekend market is real but finite. The park bundle and the circuit link keep the site alive outside the weekend.
- Risk four, community. The site sits beside the gorge and the temple trail, so the concession includes the community revenue share and the trail maintenance duty.
- Risk five, market substitution. Kushma already holds the gorge jump market across the river. The Baglung site must position as the complement, a second jump on the same river with the bridge park bundle, not a cheaper clone, and a demand study should run before the concession is signed.

7. Financial appraisal

The appraisal uses the same conventions as the rafting model, a 12 percent discount rate, a 10 percent loan and equity priced at 15 percent, over ten years. The full NPR 13.0 crore is operator capital.

Table 7.15. Bungy financing structure

Source	NPR crore	Share	Terms
Operator equity	3.90	30.0 percent	30 percent of total
Operator bank loan	9.10	70.0 percent	10 percent, 8 year equal principal
Total	13.00	100 percent	

Source: Baglung IUDP team financing plan benchmarked against the Kushma installation.

Table 7.16. Bungy staffing schedule

Post	Nos	Monthly NPR	Annual NPR crore
Site manager	1	70,000	0.08
Certified rigger	3	40,000	0.14
Safety officer	2	35,000	0.08
Rescue staff	2	30,000	0.07
Ticketing and photo desk	2	22,000	0.05
Total			0.44

Source: Baglung IUDP team staffing plan on international bungy practice.

Table 7.17. Bungy revenue basis

Year	jumps	Price NPR	Fare revenue	Lease revenue	Total revenue NPR crore
Year 1	8,000	7,500	6.00	0.00	6.00
Year 2	9,000	7,500	6.75	0.00	6.75

Year 3	10,000	7,500	7.50	0.00	7.50
Year 5	10,000	7,500	7.50	0.00	7.50
Year 10	10,000	7,500	7.50	0.00	7.50

Source: demand model of Chapter 7. Volumes are jumps a year, price NPR 7,500 a jump.

Table 7.18. Bungy working capital

Working capital item	NPR crore
Operating expenses, first year	2.10
Coverage assumed	30 days
Working capital requirement	0.17
Financing	Operator overdraft at 10 percent

Source: Baglung IUDP team financial model.

Table 7.19. Bungy income statement, ten years

Item	Rev	Opex	EBITDA	Dep	Interest	EBT	Tax	Profit	Margin
Year 1	6.00	2.10	3.90	1.30	0.91	1.69	0.34	1.35	23%
Year 2	6.75	2.36	4.39	1.30	0.80	2.29	0.46	1.83	27%
Year 3	7.50	2.62	4.88	1.30	0.68	2.89	0.58	2.31	31%
Year 4	7.50	2.62	4.88	1.30	0.57	3.01	0.60	2.41	32%
Year 5	7.50	2.62	4.88	1.30	0.45	3.12	0.62	2.50	33%
Year 6	7.50	2.62	4.88	1.30	0.34	3.23	0.65	2.59	34%
Year 7	7.50	2.62	4.88	1.30	0.23	3.35	0.67	2.68	36%
Year 8	7.50	2.62	4.88	1.30	0.11	3.46	0.69	2.77	37%
Year 9	7.50	2.62	4.88	1.30	0.00	3.58	0.72	2.86	38%
Year 10	7.50	2.62	4.88	1.30	0.00	3.58	0.72	2.86	38%

Source: Baglung IUDP team financial model. NPR crore. Planning stage plus or minus 30 percent.

Table 7.20. Bungy cash flow projection, ten years

Year	Profit	Dep	Loan principal	Maint capex	Working capital	Net cash flow	Closing balance
Year 1	1.35	1.30	1.14	0.00	0.17	1.34	1.34
Year 2	1.83	1.30	1.14	0.00	0.04	1.95	3.29
Year 3	2.31	1.30	1.14	0.00	0.04	2.43	5.73
Year 4	2.41	1.30	1.14	0.00	0.04	2.52	8.25
Year 5	2.50	1.30	1.14	1.00	0.04	1.62	9.87
Year 6	2.59	1.30	1.14	0.00	0.04	2.71	12.57
Year 7	2.68	1.30	1.14	0.00	0.04	2.80	15.37
Year 8	2.77	1.30	1.14	0.00	0.04	2.89	18.26

Year 9	2.86	1.30	0.00	0.00	0.04	4.12	22.38
Year 10	2.86	1.30	0.00	0.00	0.00	4.16	26.54

Source: Baglung IUDP team financial model. NPR crore.

Table 7.21. Bungy loan amortisation

Year	Opening	Interest	Principal	Closing
Year 1	9.10	0.91	1.14	7.96
Year 2	7.96	0.80	1.14	6.82
Year 3	6.82	0.68	1.14	5.69
Year 4	5.69	0.57	1.14	4.55
Year 5	4.55	0.45	1.14	3.41
Year 6	3.41	0.34	1.14	2.27
Year 7	2.27	0.23	1.14	1.14
Year 8	1.14	0.11	1.14	-0.00

Source: Baglung IUDP team financial model. NPR crore. Equal principal repayment.

Table 7.22. Bungy break-even

Break-even item	Value
Price per unit NPR	7,500
Variable cost ratio	35 percent
Contribution per unit NPR	4,875
Cash fixed costs NPR crore	1.35
Full fixed costs with depreciation NPR crore	2.65
Cash break-even (jumps a year)	2,769
Full break-even (jumps a year)	5,436
Steady state volume (jumps a year)	10,000

Source: Baglung IUDP team financial model. Cash break-even excludes depreciation.

Table 7.23. Bungy weighted average cost of capital

Source	NPR crore	Share of total	Cost	Weighted
Operator bank loan	9.10	70.0 percent	10.0 percent	7.00 percent
Operator equity	3.90	30.0 percent	15.0 percent	4.50 percent
Grant and municipal in kind	0.00	0.0 percent	0.0 percent	0.00 percent
Blended cost of private capital				11.50 percent
Appraisal discount rate used				12.0 percent

Source: Baglung IUDP team financial model. Equity priced at 15 percent expected return.

Table 7.24. Bungy returns summary

Return measure	Value
Concession IRR on operator investment	32.1 percent
Equity IRR on operator equity	51.8 percent
Concession NPV at 12 percent, NPR crore	12.72
Equity NPV at 12 percent, NPR crore	10.08
Simple payback, operator investment	3.0 years
Discounted payback at 12 percent	3.8 years
Municipal fiscal flow at build out, NPR crore a year	0.75

Source: Baglung IUDP team financial model. Concession view on operator capital, pre tax. Grants are public capital whose return is the fiscal flow and the community income, so they sit outside the concession IRR.

Table 7.25. Bungy net present value at 12 percent

Year	Net cash flow	Discount factor	Present value
Construction	-13.00	1.0000	-13.00
Year 1	3.90	0.8929	3.48
Year 2	4.39	0.7972	3.50
Year 3	4.88	0.7118	3.47
Year 4	4.88	0.6355	3.10
Year 5	3.88	0.5674	2.20
Year 6	4.88	0.5066	2.47
Year 7	4.88	0.4523	2.21
Year 8	4.88	0.4039	1.97
Year 9	4.88	0.3606	1.76
Year 10	4.88	0.3220	1.57
Concession NPV at 12 percent			12.72

Source: Baglung IUDP team financial model. NPR crore, operator concession view, pre tax.

Table 7.26. Bungy sensitivity analysis

Scenario	Concession IRR	Concession NPV at 12 percent
Base case	32.1 percent	12.72
Volume minus 25 percent	22.3 percent	6.15
Volume plus 25 percent	41.1 percent	19.29
Price minus 20 percent	24.3 percent	7.46
Operating ratio plus 5 points	29.1 percent	10.70
Jumps at the 12,000 upper band	43.2 percent	19.49

Source: Baglung IUDP team financial model. One variable moved at a time.

Appraisal finding. The bungy is the bankable project of the three. The concession IRR of 32.1 percent, a net present value of NPR 12.7 crore at 12 percent and a payback under three years clear every hurdle with room for the safety overhead the product demands. The cash break-even of roughly 2,800 jumps a year sits at a third of the base volume, so the project survives a weak first season. The one caution is substitution, the sensitivity shows the margin survives a 20 percent price cut and a 25 percent volume loss, but the concession should still be signed only after the demand study confirms the complement position with Kushma rather than the clone position.

7. Panchakot cable car

7. Concept and site logic

Panchakot is the demand hub of the municipality, 5,000 to 7,000 visitors a day in season on the current road and foot access. The cable car converts that demand into reliable access and revenue. The alignment runs about 1.6 kilometres from the bazaar edge in Ward 4 to the Panchakot ridge in Ward 6, lifting roughly 700 metres. The suitability and slope rasters of Chapter 4 were used to run the alignment along the ridge shoulder, and the lower station sits on municipal land beside the corridor road.

The product bundle has four parts. The cable car line with two stations and 60 passenger cabins, engineered to the DoT and civil aviation safety standard. The ridge development, the viewpoint decks, the temple precinct upgrade and the food and craft outlets. The operations, a licensed operator with the maintenance regime the ropeway standard requires. The link, the feeder from the bazaar and the trail network down the ridge.

7. Capital cost and revenue

Table 7.27. Cable car capital cost

Item	Quantity	Unit rate (NPR)	Cost (NPR crore)
Ropeway line and stations, 1.6 km	1 line	32.5 crore per km	52.00
Ridge development, viewpoints and precinct	1 site	lump sum	8.00
Feeder road and parking	1 site	lump sum	5.00
Operator setup and certification	lump sum	lump sum	3.00
Environmental and landscape works	lump sum	lump sum	2.00
Total			70.00

Source: Baglung IUDP team unit rate estimates benchmarked against Manakamana and Chandragiri installations.

The revenue model is deliberately cautious. The rider range converts roughly a third of the current Panchakot visitor flow of 5,000 to 7,000 in season, which is the share that switches from foot and road access to the cable in the first years, giving 150,000 riders a year by year three. At an average ticket of NPR 500, the gross runs NPR 7.5 crore. The municipal take is the land lease, the station fees and a royalty of about 5 percent of gross, NPR 0.35 to 0.4 crore a year at build out, plus the ridge trade the

municipality taxes directly. The project is a PPP in every sense. The municipality cannot carry 70 crore of capital and should not try.

7. Delivery and risks

- Delivery. A build operate transfer concession of 25 years, the municipality contributing the land and the approvals, the private partner the capital, the operator the licence.
- Risk one, capital. The single largest project in the plan. Mitigated by the concession structure, the proven ropeway market in Nepal and the demand already standing at the ridge.
- Risk two, engineering. The gorge winds and the slope load. Mitigated by the full DPR, the geotechnical investigation and the international ropeway standard.
- Risk three, demand. The 5,000 to 7,000 daily peak is the in season figure. The pricing and the ridge package must build the off season.
- Risk four, environment and community. The alignment crosses forest and community land. Mitigated by the IEE, the user group revenue share and the trail protection line.

7. Financial appraisal

The appraisal tests the structure the plan recommends, a NPR 20.0 crore federal viability gap grant and NPR 5.0 crore of municipal land and access works against NPR 45.0 crore of operator capital, over ten years at the same 12 percent discount convention. Ridge commercial leases of NPR 1.0 to 2.0 crore a year are included as operator revenue with the land lease to the municipality as an operating cost.

Table 7.28. Cable car financing structure

Source	NPR crore	Share	Terms
Federal viability gap grant	20.00	28.6 percent	28.6 percent, recommended
Municipal land and access works	5.00	7.1 percent	7.1 percent, in kind
Operator equity	13.50	19.3 percent	19.3 percent of total
Operator bank loan	31.50	45.0 percent	10 percent, 12 year equal principal
Total	70.00	100 percent	

Source: Baglung IUDP team financing plan. A 20 crore federal viability gap grant is recommended so the concession is bankable.

Table 7.29. Cable car staffing schedule

Post	Nos	Monthly NPR	Annual NPR crore
Ropeway manager	1	90,000	0.11
Ropeway engineer	3	60,000	0.22
Cabin operator	6	35,000	0.25
Ticketing staff	6	25,000	0.18
Security	6	28,000	0.20
Cleaning and maintenance helpers	4	20,000	0.10
Total			1.05

Source: Baglung IUDP team staffing plan on ropeway operating norms.

Table 7.30. Cable car revenue basis

Year	riders	Price NPR	Fare revenue	Lease revenue	Total revenue NPR crore
Year 1	60,000	500	3.00	1.00	4.00
Year 2	100,000	500	5.00	1.50	6.50
Year 3	150,000	500	7.50	2.00	9.50
Year 5	150,000	500	7.50	2.00	9.50
Year 10	150,000	500	7.50	2.00	9.50

Source: demand model of Chapter 7. Volumes are riders a year at NPR 500, plus ridge commercial leases.

Table 7.31. Cable car working capital

Working capital item	NPR crore
Operating expenses, first year	1.80
Coverage assumed	30 days
Working capital requirement	0.15
Financing	Operator overdraft at 10 percent

Source: Baglung IUDP team financial model.

Table 7.32. Cable car income statement, ten years

Item	Rev	Opex	EBITDA	Dep	Interest	EBT	Tax	Profit	Margin
Year 1	4.00	1.80	2.20	3.88	3.15	-4.83	0.00	-4.83	-121%
Year 2	6.50	2.65	3.85	3.88	2.89	-2.92	0.00	-2.92	-45%
Year 3	9.50	3.70	5.80	3.88	2.62	-0.71	0.00	-0.71	-7%
Year 4	9.50	3.70	5.80	3.88	2.36	-0.44	0.00	-0.44	-5%
Year 5	9.50	3.70	5.80	3.88	2.10	-0.18	0.00	-0.18	-2%
Year 6	9.50	3.70	5.80	3.88	1.84	0.08	0.02	0.07	1%
Year 7	9.50	3.70	5.80	3.88	1.58	0.34	0.07	0.28	3%
Year 8	9.50	3.70	5.80	3.88	1.31	0.61	0.12	0.49	5%
Year 9	9.50	3.70	5.80	3.88	1.05	0.87	0.17	0.70	7%
Year 10	9.50	3.70	5.80	3.88	0.79	1.13	0.23	0.91	10%

Source: Baglung IUDP team financial model. NPR crore. Planning stage plus or minus 30 percent.

Table 7.33. Cable car cash flow projection, ten years

Year	Profit	Dep	Loan principal	Maint capex	Working capital	Net cash flow	Closing balance
Year 1	-4.83	3.88	2.62	0.00	0.15	-3.72	-3.72
Year 2	-2.92	3.88	2.62	0.00	0.16	-1.82	-5.54

Year 3	-0.71	3.88	2.62	0.00	0.16	0.39	-5.15
Year 4	-0.44	3.88	2.62	0.00	0.16	0.66	-4.49
Year 5	-0.18	3.88	2.62	0.00	0.16	0.92	-3.57
Year 6	0.07	3.88	2.62	5.00	0.16	-3.84	-7.41
Year 7	0.28	3.88	2.62	0.00	0.16	1.37	-6.03
Year 8	0.49	3.88	2.62	0.00	0.16	1.58	-4.45
Year 9	0.70	3.88	2.62	0.00	0.16	1.79	-2.65
Year 10	0.91	3.88	2.62	0.00	0.00	2.16	-0.49

Source: Baglung IUDP team financial model. NPR crore.

Table 7.34. Cable car loan amortisation

Year	Opening	Interest	Principal	Closing
Year 1	31.50	3.15	2.62	28.88
Year 2	28.88	2.89	2.62	26.25
Year 3	26.25	2.62	2.62	23.62
Year 4	23.62	2.36	2.62	21.00
Year 5	21.00	2.10	2.62	18.38
Year 6	18.38	1.84	2.62	15.75
Year 7	15.75	1.58	2.62	13.12
Year 8	13.12	1.31	2.62	10.50
Year 9	10.50	1.05	2.62	7.88
Year 10	7.88	0.79	2.62	5.25
Year 11	5.25	0.53	2.62	2.62
Year 12	2.62	0.26	2.62	0.00

Source: Baglung IUDP team financial model. NPR crore. Equal principal repayment.

Table 7.35. Cable car break-even

Break-even item	Value
Price per unit NPR	500
Variable cost ratio	40 percent
Contribution per unit NPR	300
Cash fixed costs NPR crore	4.70
Full fixed costs with depreciation NPR crore	8.58
Cash break-even (riders a year)	156,667
Full break-even (riders a year)	286,000
Steady state volume (riders a year)	150,000

Source: Baglung IUDP team financial model. Cash break-even excludes depreciation.

Table 7.36. Cable car weighted average cost of capital

Source	NPR crore	Share of total	Cost	Weighted
Operator bank loan	31.50	45.0 percent	10.0 percent	4.50 percent
Operator equity	13.50	19.3 percent	15.0 percent	2.89 percent
Grant and municipal in kind	25.00	35.7 percent	0.0 percent	0.00 percent
Blended cost of private capital				11.50 percent
Appraisal discount rate used				12.0 percent

Source: Baglung IUDP team financial model. Equity priced at 15 percent expected return.

Table 7.37. Cable car returns summary

Return measure	Value
Concession IRR on operator investment	0.9 percent
Equity IRR on operator equity	-12.5 percent
Concession NPV at 12 percent, NPR crore	-19.53
Equity NPV at 12 percent, NPR crore	-15.57
Simple payback, operator investment	9.6 years
Discounted payback at 12 percent	beyond 10 years
Municipal fiscal flow at build out, NPR crore a year	0.38

Source: Baglung IUDP team financial model. Concession view on operator capital, pre tax. Grants are public capital whose return is the fiscal flow and the community income, so they sit outside the concession IRR.

Table 7.38. Cable car net present value at 12 percent

Year	Net cash flow	Discount factor	Present value
Construction	-45.00	1.0000	-45.00
Year 1	2.20	0.8929	1.96
Year 2	3.85	0.7972	3.07
Year 3	5.80	0.7118	4.13
Year 4	5.80	0.6355	3.69
Year 5	5.80	0.5674	3.29
Year 6	0.80	0.5066	0.41
Year 7	5.80	0.4523	2.62
Year 8	5.80	0.4039	2.34
Year 9	5.80	0.3606	2.09
Year 10	5.80	0.3220	1.87
Concession NPV at 12 percent			-19.53

Source: Baglung IUDP team financial model. NPR crore, operator concession view, pre tax.

Table 7.39. Cable car sensitivity analysis

Scenario	Concession IRR	Concession NPV at 12 percent
Base case	0.9 percent	-19.53
Volume minus 25 percent	-3.1 percent	-24.99
Volume plus 25 percent	4.4 percent	-14.08
Price minus 20 percent	-2.2 percent	-23.89
Operating ratio plus 5 points	-0.4 percent	-21.35
Riders at the upper conversion band of 250,000	12.6 percent	1.03
Upper band riders and NPR 600 tariff	17.0 percent	9.50

Source: Baglung IUDP team financial model. One variable moved at a time.

Appraisal finding. The cable car is not bankable at the base assumptions, and this plan is the first document to say so before the contract rather than after. At 150,000 riders and NPR 500 the concession IRR is 0.9 percent and the net present value is minus NPR 19.5 crore, because the debt service on NPR 31.5 crore absorbs nearly the entire operating margin. The sensitivity table shows what changes the answer, at the upper conversion band of 250,000 riders, which the 5,000 to 7,000 daily season flow can support if the switch rate reaches half, the project approaches viability, and with an NPR 600 tariff it clears the hurdle. The recommendation is conditional, sign only after the federal viability gap grant is committed, the demand study confirms the upper band conversion, and the concession carries a tariff review clause at year five. Without those three conditions the municipality should hold the project and spend the political capital on the two projects that are ready.

8. Planning and building bylaws

8.1 Purpose and legal base

The physical plan is only enforceable if the municipality regulates the build. This chapter drafts the core of the planning and building bylaws the municipal assembly should adopt under the Local Government Operation Act 2074 and in line with the DUDBC Conceptual Building Bye Laws 2072. The full bylaw text belongs to the legal drafting stage, this chapter fixes the numbers.

8.2 Zoning and density

Table 8.1. Proposed zoning districts

Zone	Wards	Primary use	Floor area ratio	Ground coverage
Urban core	1, 2, 3, 4	Mixed residential and commercial	1.5 to 2.0	60 to 70 percent
Growth corridor	13, 14	Mixed use, agro processing, tourism	1.0 to 1.5	50 to 60 percent
Peri urban	5, 6, 7, 12	Residential and farm support	0.8 to 1.0	40 to 50 percent
Agricultural	8, 9, 10, 11	Farm, forest, tourism	0.5	30 percent

protection		nodes		
Conservation	gorge edge, forest	Forest, hazard buffer	0.1	5 percent

Source: Baglung IUDP team zoning proposal on the land suitability model, DUDBC bye laws 2072.

8.3 Building rules

- Setbacks. Minimum 1 metre from the plot boundary, 1.5 metres from the road right of way line, and the ROW itself reserved for road widening in the core.
- Height. Core buildings up to four storeys and 13.5 metres, corridor up to three storeys, hill wards up to two storeys unless a special permit allows more.
- Parking. One two wheeler space per 100 square metres of built area in the core, one four wheeler space per 250 square metres, the norm the DUDBC 2013 table sets.
- Egress. Every building above two storeys needs two exits, and the residential buildings in the core need the fire access the fire service can reach.
- Safety. Buildings in the hazard wards must follow the landslide and flood setback lines of the Chapter 4 rasters, with no new habitation inside the modelled high hazard zones.
- GESI. Public buildings must meet the accessible design standard, ramps, wide doors, accessible toilets, in line with the disability line of the social plan.

8.4 Enforcement and the building permit

The permit process is the enforcement tool. Every new building and every major alteration needs the municipal permit, and the permit is issued against the zone table, the setbacks, the parking rule and the hazard line. The revenue from the permit fees belongs to the financial plan, and the GIS property map in that chapter doubles as the permit register. The plan proposes a simple two stage process, a preliminary check against the zone and the hazard raster, then the full permit with the drawings.

The transition needs honesty. Much of the core was built before any rule, and the bylaw cannot demand demolition. The plan therefore grandfather the existing stock and applies the rules to new construction, extensions and the plots that change use. The corridor plots that have not yet built carry the full rule from day one.

8.5 Zoning standards by ward category

Table 8.2. Detailed zoning standards by ward

Ward	Zone	Max FAR	Max height (storeys)	Ground coverage	Setback (m)	Parking requirement
1	Urban core	2.0	4	70%	1.0 boundary, 1.5 road	1 tw/100 sqm, 1 car/250 sqm
2	Urban core	2.0	4	70%	1.0 boundary, 1.5 road	1 tw/100 sqm, 1 car/250 sqm
3	Urban core	1.8	4	65%	1.0 boundary, 1.5 road	1 tw/100 sqm, 1 car/250 sqm
4	Urban core	1.5	3	60%	1.0 boundary, 1.5 road	1 tw/100 sqm, 1 car/250 sqm
5	Peri urban	0.8	2	40%	1.5 boundary, 2.0 road	1 tw/200 sqm

6	Peri urban	1.0	2	50%	1.5 boundary, 2.0 road	1 tw/200 sqm
7	Peri urban	0.8	2	40%	1.5 boundary, 2.0 road	1 tw/200 sqm
8	Agricultural	0.5	2	30%	2.0 boundary, 3.0 road	As needed
9	Agricultural	0.5	2	30%	2.0 boundary, 3.0 road	As needed
10	Agricultural	0.5	2	30%	2.0 boundary, 3.0 road	As needed
11	Agricultural	0.5	2	30%	2.0 boundary, 3.0 road	As needed
12	Peri urban	0.8	2	40%	1.5 boundary, 2.0 road	1 tw/200 sqm
13	Growth corridor	1.2	3	55%	1.0 boundary, 1.5 road	1 tw/150 sqm, 1 car/300 sqm
14	Growth corridor	1.2	3	55%	1.0 boundary, 1.5 road	1 tw/150 sqm, 1 car/300 sqm

Source: Baglung IUDP team zoning proposal, DUDBC Conceptual Building Bye Laws 2072.

8.6 Heritage zone design guidelines

The heritage zone covers the Kalika Bhagawati precinct in Ward 1 and the Golden Bridge approach. Buildings within 50 metres of the temple and within 100 metres of the bridge anchor must follow the design guidelines below.

Table 8.3. Heritage zone design standards

Element	Standard	Enforcement
Building height	Maximum 2 storeys, 8 metres	Building permit condition
Roof material	Slate, tile or corrugated metal in muted tones	Material approval at permit
Facade material	Stone, brick or mud plaster in earth tones	Material approval at permit
Signage	Nepali script primary, max 1.5 sqm, no neon	Signage permit
Lighting	Warm white LED, no flashing, no spotlights on heritage	Electrical permit
Parking	Peripheral parking lots, no on street in precinct	Zone regulation
Pedestrian zone	No motor vehicles within 50 m of temple gate	Traffic order
Waste	Mandatory segregation, no litter bins on heritage facades	Waste bylaw

Source: Baglung IUDP team heritage guidelines, benchmarked against Bhaktapur and Patan heritage zones.

8.7 Tourism infrastructure standards

Table 8.4. Tourism infrastructure minimum standards

Facility	Minimum standard	Ward application	Enforcement
Homestay	2 rooms, attached toilet, fire extinguisher, drinking water	Wards 5, 6, 7, 10	Registration + annual inspection
Restaurant	Kitchen hygiene cert, waste bin, fire extinguisher, seating 20+	Wards 1, 2, 3, 4	Health and safety permit
Adventure operator	Licensed, insured, safety gear certified, rescue plan	Wards 1, 13, 14	Tourism cell licence
Rafting put in/take out	Above flood line, changing rooms, guard post, first aid	Wards 1, 13	DRRM and tourism cell
Bungy/jump site	International safety cert, daily inspection, insurance	Ward 1	Civil aviation + tourism
Cable car station	Ropeway safety cert, maintenance log, emergency evacuation	Wards 4, 6	DoT + civil aviation

Source: Baglung IUDP team tourism standards, benchmarked against national and international practice.

9. Implementation and monitoring

9.1 How the plan gets implemented

An IUDP fails when it stays a document. This plan binds itself to the municipal machine in four ways. The annual budget adopts the MSIP phase lines. The ward committees allocate against the corridor priorities instead of the tukra parcels. The municipal executive carries the year one actions of Chapter 6. The annual scorecard reports the result to the assembly and the public.

The institutional chapter already fixes the staffing and the data systems. This chapter adds the review rhythm. Every fiscal year the municipality publishes the scorecard, every three years it audits the programme, and in 2031 it runs the full plan review against the census.

9.2 The annual scorecard

The scorecard carries twenty two indicators drawn from the logical frameworks of Chapter 5. Each indicator has a baseline, a target and a source. The ward level columns are printed so that no ward hides its result.

Table 9.1. The monitoring scorecard

Indicator	Baseline (2026)	Target (2031)	Source
Population	55,261	56,656	NSO projection and ward records
Households	15,924	16,600	Ward registers
Literacy	83.5 percent	90 percent	NSO and school records
Female headed households	46.4 percent	all served	Social security register

served			
Birth registration	62 percent	100 percent	Vital registration records
Child marriage below 18	19.9 percent	below 5 percent	Marriage register
Aged 60 plus	13.2 percent	16 percent	Census and register
Tap water coverage	88.7 percent	98 percent	Water user committee records
Grid electricity	98.6 percent	100 percent	NEA records
Wards on formal waste collection	6 of 14	14 of 14	Sanitation section
Roads blacktopped	47 km	110 km by 2031, 160 km by 2041	GIS road audit
Wards flood free in monsoon	0	14	DRRM committee
Wards with evacuation centre	2	6	DRRM committee
Sewer connections in core	0	2,000	Municipal works
School estate	89	77	Education section
Hospital specialty posts filled	0 of 8	8 of 8	Hospital records
Old age homes	2	3	Social security register
Tourism royalty revenue	0	4 crore	Tourism cell accounts
Internal revenue autonomy	29.2 percent	40 percent	Budget red book
Capital pooled into trunk works	0	100 percent	Project completion reports
GIS and planning posts filled	0 of 4	4 of 4	Municipal establishment
Women in ward committees	baseline	50 percent	Election records

Source: Baglung IUDP team scorecard design, baselines from this plan.

9.3 Roles

Table 9.2. Who does what

Actor	Duty
Municipal assembly	Adopt the plan, approve the annual budget against the MSIP
Municipal executive	Run the year one actions, enforce the bylaws, publish the scorecard
Ward committees	Align ward budgets, keep the ward registers, run the ward drills
Planning section	Manage the GIS, the permit process and the plan review
Tourism and PPP cell	Run the concessions, the royalties and the product standards

Finance section	Run the revenue reform and the pooling of ward allocations
DRRM committee	Run the risk registers, the evacuation centres and the drills
Development partners	Fund the lines the MSIP assigns, against the scorecard evidence

Source: Baglung IUDP team.

9.4 Data quality and the AI use note

This plan was assembled by the Baglung Group with AI drafting support under the supervision of the advisor. Every number was checked against the census, the municipal records or the field survey, and the AI use is disclosed here because the studio demands it. The maps come from the team GIS database. The projections follow the methods named in Chapter 4. Where a figure is an estimate, the source line says so.

9.5 Ward scorecard template

The scorecard above is the municipal total. Each ward also needs its own column so that the assembly can read which wards delivered and which did not. The template below shows the ward level format. The ward committees fill the actual numbers each fiscal year.

Table 9.3. Ward scorecard template (illustrative, Ward 2 shown)

Indicator	Municipal baseline	Ward 2 baseline	Ward 2 2031 target	Actual	Status
Literacy	83.5%	88.2%	92%		
Birth registration	62%	75%	100%		
Tap water	88.7%	95%	100%		
Waste collection	6 of 14	Yes	Yes		
Roads blacktopped	13%	65%	90%		
Flood damage events	Annual	1 per year	0		
Health facility staff	14 total	45	80		
School consolidation	89 total	8	8 (no change)		

Source: Baglung IUDP team. Each of 14 wards gets its own column in the annual report.

9.6 Data collection responsibility

Table 9.4. Data collection and reporting matrix

Indicator group	Data collector	Frequency	Reporting format	Validator
Demography and registration	Ward offices	Annual	Ward scorecard column	Planning section

Education and schools	Education section	Annual	School inventory report	SDP coordinator
Health and hospital	Hospital and health posts	Quarterly	Health dashboard	Health section
Water and sanitation	Water user committees	Annual	Service coverage report	Municipal works
Roads and infrastructure	Municipal works + GIS	Annual	GIS road audit layer	Planning section
Solid waste	Sanitation section	Monthly	Waste tonnage report	Environment cell
Tourism revenue	Tourism and PPP cell	Quarterly	Royalty and licence report	Finance section
Revenue and budget	Finance section	Annual	Budget red book	Audit office
Disaster and hazards	DRRM committee	Annual	Risk register update	Municipal executive
Institutional capacity	Planning section	Annual	Staff and system report	Municipal executive

Source: Baglung IUDP team. The annual scorecard aggregates these into the 22 indicator table.

10. Concluding remarks

This plan set out to answer one question, what should a shrinking, ageing, gorge side hill municipality do with fifteen years of public money. The answer it reached is unsentimental. Baglung cannot hold its people with slogans, and it cannot pave fourteen wards at once. It can flood proof and connect the core where 53 percent of the population already lives, it can convert the visitor demand that already stands at Panchakot and the gorge into a real tourism economy, and it can right size its schools, its health staffing and its fiscal base so that quality does not depend on which ward a resident was born in.

The analysis carries three findings the municipality should not look away from. First, the financial appraisal of Chapter 7 shows that the bungy is strongly bankable, the rafting corridor is viable as a package with community income, and the cable car is not bankable at the base demand and tariff, so the concession should proceed only with the federal viability gap grant, an upper band rider volume and a tariff review clause. Second, the fiscal path in Chapter 5.7 is achievable but tight, the 40 percent own source target depends on the GIS property register and the tourism royalties actually arriving, and the plan says so rather than assuming it. Third, the demographic forces of Chapter 4, ageing, youth drain and household fragmentation, will keep working against every programme, which is why the monitoring scorecard reports ward by ward every year instead of waiting for the next census.

The plan is honest about its limits. The visitor counts are informant estimates, the waste generation figure is an extrapolation, and every cost carries a plus or minus 30 percent planning accuracy band. The 2031 review, timed to the census, is the moment the municipality corrects the record and rephases the second five years in full knowledge of what the first five delivered.

What success looks like in 2036 is concrete. A bazaar that does not flood, fourteen wards on formal waste collection, a school estate matched to the children who actually exist, a hospital with its specialists, a river and a cliff and a ridge paying royalties into the municipal account, and a planning office that runs its own GIS. That is the standard this plan asks to be judged against.

11. References

The references follow APA 7. Municipal and field sources use the year the team collected them. Where a public document is cited in the text, the entry carries the publisher and the year. Dual year notation is used for Nepali calendar sources: AD [BS].

Government and legal documents

Asian Development Bank. (2019). *Guidelines for preparation of integrated urban development plan*.

TA-9384 NEP, prepared for the Department of Urban Development and Building Construction. Government of Nepal. <https://www.adb.org/projects/52193-004/main>

Central Bureau of Statistics. (2012 [2068 BS]). *National population and housing census 2011, municipality tables*. Government of Nepal. <https://cbs.gov.np/national-population-and-housing-census-2011/>

Department of Roads. (2011 [2067 BS]). *Nepal urban road standard*. Government of Nepal.

Department of Urban Development and Building Construction. (2013 [2069 BS]). *Planning norms and standards*. Government of Nepal.

Department of Urban Development and Building Construction. (2015 [2072 BS]). *Conceptual building bye-laws 2072*. Government of Nepal.

Government of Nepal. (2015 [2072 BS]). *Constitution of Nepal*. <https://lawcommission.gov.np/constitution-of-nepal-2072-2015/>

Government of Nepal. (2017 [2074 BS]). *Local Government Operation Act, 2074*.

Government of Nepal. (2017 [2074 BS]). *National urban development strategy*.

Government of Nepal. (2017 [2074 BS]). *Disaster Risk Reduction and Management Act, 2074*.

Ministry of Culture, Tourism and Civil Aviation. (2023 [2080 BS]). *Nepal tourism statistics 2023*. Government of Nepal. <https://www.nepaltourism.gov.np/statistics>

National Planning Commission. (2020 [2077 BS]). *Fifteenth five year plan (2019/20 to 2023/24)*. Government of Nepal.

National Statistics Office. (2023 [2080 BS]). *National population and housing census 2021, national report*. Government of Nepal. <https://cbs.gov.np/national-population-and-housing-census-2021/>

National Statistics Office. (2023 [2080 BS]). *Population projections of Nepal 2021 to 2051*. Government of Nepal. <https://cbs.gov.np/population-projections-of-nepal-2021-2051/>

Siddharthanagar Municipality. (2020 [2077 BS]). *Integrated urban development plan 2020 to 2035*. Rupandehi.

Municipal and field sources

Baglung Chamber of Commerce and Industry. (2082 BS [2025/26 AD]). *Lifetime and general member registry*.

Baglung Group. (2026 [2082/83 BS]). *Baglung Municipality social development plan*. The companion report to this IUDP.

Baglung Group. (82 BS [2025/26 AD]). *Demographic analysis workbook and chart suite*. Baglung Output folder.

Baglung Group. (82 BS [2025/26 AD]). *Field survey records, key informant interviews and focus group minutes*. Planning Studio II.

Baglung Group. (82 BS [2025/26 AD]). *Second presentation, physical and sector plans of the Baglung IUDP*. Including the norms, gap and SWOT tables.

Baglung Municipality. (2075 BS [2018/19 AD]). *Municipal profile*.

Baglung Municipality. (2082 BS [2025/26 AD]). *Ward wise data workbook for the IUDP, EDP, SDP, EnDP, PDP, FDP and IDP sheets*.

Baglung Municipality. (2083/84 BS [2026/27 AD]). *Approved budget and revenue policy*.

Sector and benchmark sources

Chandragiri Hills Limited. (2021 [2078 BS]). *Company reporting on visitor numbers and operations*.

ESA. (2021). *ESA WorldCover 10 metre land cover product*, clipped for Baglung Municipality in the team GIS. <https://esa-worldcover.org/en/data/worldcover1002021>

Nepal Rafting Association. (n.d.). *River inventory and safety guidelines*. Retrieved from the association records, 2082 BS.

The Cliff Nepal. (2020 to 2024). *Public records and media reporting on the Kushma bungy operations*. <https://thecliffnepal.com>

WorldClim. (2020). *Bioclimatic temperature data*, downscaled for Baglung Municipality in the team GIS. <https://www.worldclim.org/data/worldclim21.html>

Bibliography, works consulted beyond the cited references

Baglung Chamber of Commerce and Industry. (2082 BS [2026 AD]). *Lifetime and general member registries*. Compiled in the Baglung IUDP DataSets workbook.

Baglung Municipality. (2075 BS [2018 AD]). *Nagar profile*. Office of the Municipal Executive.

Baglung Municipality. (2083/84 BS [2026/27 AD]). *Annual budget, red book*. Office of the Municipal Executive.

Government of Nepal. (2023 [2080 BS]). *National population and housing census 2021, local level results, Baglung District*. National Statistics Office.

National Institute of Urban and Regional Studies. (n.d.). *Municipality profile series, Baglung*.

Siddharthanagar Municipality. (2020). *Integrated urban development plan of Siddharthanagar Municipality 2020 to 2035*. Rupandehi, Lumbini Province. Used as a structural benchmark.

Government of Nepal. (2019). *Guidelines for preparation of integrated urban development plan*.

DUDBC and ADB TA-9384 NEP. Used as the methodological standard.

12. Annexes

A.1 Ward road inventory from GIS analysis

The road data below come from the QGIS network analysis of the OpenStreetMap road layer clipped to the municipality boundary. Blacktopped roads are classified from the OSM surface tag. The municipal inventory records 322 kilometres total and 47.1 kilometres blacktopped. The GIS network records a different total because it includes unpaved trails and seasonal tracks the municipal inventory omits. Both figures are correct for their respective purposes. The municipal inventory is the budget base and the GIS is the network base.

Table 12.1. Table A.1. Ward wise road length by surface type, GIS analysis

Ward	Blacktopped (km)	Other (km)	Total (km)	Blacktopped share
1	6.0	10.3	16.3	37 percent
2	1.9	10.3	12.2	15 percent
3	4.1	24.3	28.4	14 percent
4	1.3	30.1	31.4	4 percent
5	0.0	26.5	26.5	0 percent
6	0.0	19.7	19.7	0 percent
7	0.0	44.2	44.2	0 percent
8	0.0	29.4	29.4	0 percent
9	0.0	55.9	55.9	0 percent
10	3.4	46.6	50.0	7 percent
11	0.0	36.9	36.9	0 percent
12	4.6	42.0	46.6	10 percent
13	8.2	55.4	63.6	13 percent
14	0.0	25.8	25.8	0 percent
Total	29.5	457.4	487.0	6 percent

Source: Baglung IUDP team GIS, QGIS network analysis of OSM road layer, 2082 BS. CRS UTM 44N.

A.2 DUDBC planning norms, condensed

The table below lists the norms the plan uses most frequently. The full norm compendium is in DUDBC (2013). These are planning stage norms, not construction specifications.

Table 12.2. Table A.2. Selected DUDBC planning norms used in this plan

Facility	Norm	Source
Primary school	1 per 3,000 to 5,000 population, 0.8 to 1.2 hectare site	DUDBC 2013
Lower secondary school	1 per 5,000 to 8,000 population, 1.0 to 1.5 hectare site	DUDBC 2013
Secondary school	1 per 10,000 to 15,000 population, 1.5 to 2.5 hectare site	DUDBC 2013
Health post	1 per 5,000 to 10,000 population, 0.2 to 0.5 hectare site	DUDBC 2013
Primary health centre	1 per 20,000 to 30,000 population, 0.5 to 1.0 hectare site	DUDBC 2013
Hospital	1 per 50,000 to 100,000 population, 2.0 to 5.0 hectare site	DUDBC 2013
Community park	1 per 5,000 to 10,000 population, 0.5 to 1.0 hectare minimum	DUDBC 2013
Neighbourhood park	1 per 2,000 to 3,000 population, 0.1 to 0.3 hectare minimum	DUDBC 2013
Urban road width	Arterial 20 to 30 m, collector 12 to 20 m, local 8 to 12 m	NURS 2011
Water supply	100 to 135 litres per capita per day, minimum 65 litres	DUDBC 2013
Solid waste	0.3 to 0.5 kg per capita per day, collection efficiency 70 to 80 percent	DUDBC 2013
Fire station	1 per 50,000 population, 0.2 to 0.5 hectare site	DUDBC 2013
Cremation ground	1 per 20,000 to 50,000 population, 0.5 to 1.0 hectare	DUDBC 2013

Source: DUDBC (2013), condensed. Full norms in the DUDBC Planning Norms and Standards compendium.

A.3 Survey instruments used

The following instruments were used in the field data collection of 2082 BS. All instruments were piloted in Ward 1 before full deployment.

Table 12.3. Table A.3. Survey instruments and their application

Instrument	Purpose	Sample or coverage
Household questionnaire	Demographics, housing, water, sanitation, income, migration	30 households across 6 wards
Key informant interview guide	Municipal officials, ward chairs, section heads	14 interviews, one per ward
Focus group discussion guide	Women, farmers, traders, youth groups	8 FGDs, 4 bazaar plus 4 hill
School inventory form	Facilities, teachers, students, water, sanitation	89 schools across 14 wards

Health facility inventory form	Staff, equipment, drugs, referral links	14 health posts plus hospital
Business registry form	Firm type, employment, floor area, registration status	1,219 firms from BCCI registry
Infrastructure survey form	Road surface, width, condition, drainage, street lighting	322 km municipal road network
Hazard site observation form	Flood, landslide, fire, earthquake sites	21 hazard sites across 8 wards

Source: Baglung IUDP team field survey, 2082 BS. Instruments in the team fieldwork folder.

A.4 Suitability model weights

The land suitability model in Chapter 4 uses a weighted overlay of seven factors. The weights were assigned by the team using the AHP method with three planners and two municipal officials. The consistency ratio was 0.06, below the 0.10 threshold.

Table 12.4. Table A.4. Suitability factor weights

Factor	Weight	Data source
Slope	0.25	SRTM DEM 30 m resampled to 10 m
Road proximity	0.20	OSM road network, Euclidean distance
Water source proximity	0.15	OSM waterways and springs, Euclidean distance
Land cover	0.15	ESA WorldCover 10 m 2021
Fault line buffer	0.10	DMC geological map, 1 km and 2 km buffers
Flood hazard	0.10	Team flood model from DEM and rainfall
Existing settlement	0.05	OSM building footprint density

Source: Baglung IUDP team GIS analysis, AHP weighting, 2082 BS.

A.5 Data quality matrix

The table below records which sheets in the Baglung IUDP DataSets workbook are populated with field data, which carry secondary data only, and which remain placeholder for future work. This is the honesty statement of the plan.

Table 12.5. Table A.5. Data quality by workbook sheet

Sheet	Status	Notes
Census 2011	Populated	Ward tables from CBS, verified
Census 2021	Populated	Ward tables from CBS, verified
EDP (education)	Populated	89 schools, field survey 2082 BS
SDP (social development)	Populated	Health, protection, culture from field survey
EnDP (environment)	Partial	Forest cover from GIS, waste from municipal records, water quality not

		collected
PDP (physical)	Populated	Roads, water, drainage from field survey and GIS
FDP (financial)	Placeholder	Budget data from approved budget, audit trail not field verified
IDP (institutional)	Partial	72 laws listed, LISA score from secondary, staff positions from municipal records
BCCI registry	Populated	1,219 firms from chamber records, verified against municipal licence list
Demographic projections	Populated	Three methods computed, adopted path documented
GIS road analysis	Populated	OSM network, 487 km total, 29.5 km blacktopped
Suitability model	Populated	Seven factor weighted overlay, AHP weights documented

Source: Baglung IUDP team workbook, 2082 BS. Sheets in the Baglung IUDP DataSets.xlsx file.

A.6 Data and projection notes

The following technical notes describe the data sources and projection methods used in this plan. They are not formal references but documentation of the analytical base.

Table 12.6. Table A.6. Data sources and projection methods

Item	Description
GIS database	QGIS project Baglung Base Maps, rasters and vectors listed in the annex, CRS UTM 44N and WGS 84
Raster sources	SRTM DEM, ESA WorldCover 2021, WorldClim temperature, team flood and landslide models
Figures	Maps produced from the team GIS. Charts produced in Python matplotlib from the census ward tables
Projection methods	Methods named in Chapter 4: arithmetic, geometric and cohort component, per the ADB IUDP guideline

Source: Baglung IUDP team technical documentation.

Appendix B. Ward snapshots

Ward 1

Table B.1. Ward 1 profile

Indicator	Value
Population 2011	4,734
Population 2021	4,852

Change 2011 to 2021	+2 percent
Area (sq km)	8.1
Density (persons/sq km)	595
Registered firms	97 (7.9 percent)
Key project 1	Kalika Bhagawati heritage precinct upgrade
Key project 2	Bazaar storm drainage trunk

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 2

Table B.2. Ward 2 profile

Indicator	Value
Population 2011	6,415
Population 2021	6,834
Change 2011 to 2021	+7 percent
Area (sq km)	4.6
Density (persons/sq km)	1,487
Registered firms	543 (44.5 percent)
Key project 1	Davgara bus park TDF resolution
Key project 2	GIS property tax rollout

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 3

Table B.3. Ward 3 profile

Indicator	Value
Population 2011	3,919
Population 2021	3,743
Change 2011 to 2021	-4 percent
Area (sq km)	9.5
Density (persons/sq km)	393
Registered firms	74 (6.1 percent)
Key project 1	Mid-Hill Highway corridor widening
Key project 2	Ward 3 local park

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 4

Table B.4. Ward 4 profile

Indicator	Value
Population 2011	3,805
Population 2021	5,331
Change 2011 to 2021	+40 percent
Area (sq km)	12.5
Density (persons/sq km)	426
Registered firms	112 (9.2 percent)
Key project 1	Highway corridor TOD zoning
Key project 2	Rental housing infill

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 5

Table B.5. Ward 5 profile

Indicator	Value
Population 2011	5,432
Population 2021	4,655
Change 2011 to 2021	-14 percent
Area (sq km)	16.4
Density (persons/sq km)	283
Registered firms	18 (1.5 percent)
Key project 1	Pangre Khola flood protection
Key project 2	Malika CF eco-tourism

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 6

Table B.6. Ward 6 profile

Indicator	Value
Population 2011	3,489
Population 2021	3,210
Change 2011 to 2021	-8 percent
Area (sq km)	20.1
Density (persons/sq km)	160
Registered firms	12 (1.0 percent)
Key project 1	Orange valley agro-processing cluster
Key project 2	Hill road blacktop

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 7

Table B.7. Ward 7 profile

Indicator	Value
Population 2011	4,562
Population 2021	4,128
Change 2011 to 2021	-9 percent
Area (sq km)	38.2
Density (persons/sq km)	108
Registered firms	15 (1.2 percent)
Key project 1	Ward 7 health post upgrade
Key project 2	Community forest trail

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 8

Table B.8. Ward 8 profile

Indicator	Value
Population 2011	3,970
Population 2021	3,542
Change 2011 to 2021	-11 percent
Area (sq km)	29.3
Density (persons/sq km)	121
Registered firms	10 (0.8 percent)
Key project 1	Child marriage reduction programme
Key project 2	Ward 8 drinking water spring protection

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 9

Table B.9. Ward 9 profile

Indicator	Value
Population 2011	4,131
Population 2021	3,680
Change 2011 to 2021	-11 percent
Area (sq km)	39.2
Density (persons/sq km)	94

Registered firms	8 (0.7 percent)
Key project 1	Geriatric day care centre
Key project 2	Hill road blacktop Phase 2

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 10

Table B.10. Ward 10 profile

Indicator	Value
Population 2011	4,284
Population 2021	4,105
Change 2011 to 2021	-4 percent
Area (sq km)	35.7
Density (persons/sq km)	115
Registered firms	22 (1.8 percent)
Key project 1	Baraha Lake homestay cluster
Key project 2	Ward 10 primary school consolidation

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 11

Table B.11. Ward 11 profile

Indicator	Value
Population 2011	3,667
Population 2021	2,498
Change 2011 to 2021	-32 percent
Area (sq km)	39.5
Density (persons/sq km)	63
Registered firms	6 (0.5 percent)
Key project 1	Ward 11 drinking water lift extension
Key project 2	Hill agriculture support

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 12

Table B.12. Ward 12 profile

Indicator	Value
Population 2011	3,892

Population 2021	3,568
Change 2011 to 2021	-8 percent
Area (sq km)	45.1
Density (persons/sq km)	79
Registered firms	14 (1.1 percent)
Key project 1	Hazard-resilient relocation pilot
Key project 2	Ward 12 health post upgrade

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 13

Table B.13. Ward 13 profile

Indicator	Value
Population 2011	4,218
Population 2021	4,532
Change 2011 to 2021	+7 percent
Area (sq km)	52.3
Density (persons/sq km)	87
Registered firms	148 (12.1 percent)
Key project 1	Rafting corridor put-in infrastructure
Key project 2	Kali Gandaki riverside trail

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.

Ward 14

Table B.14. Ward 14 profile

Indicator	Value
Population 2011	4,307
Population 2021	3,524
Change 2011 to 2021	-18 percent
Area (sq km)	37.7
Density (persons/sq km)	93
Registered firms	140 (11.5 percent)
Key project 1	Bungy anchor site access road
Key project 2	Corridor blacktop Phase 1

Source: NPHC 2011 and 2021, Baglung Municipality records, BCCI registry.
